

TAB 7



Board of Education Report

File #: Rep-006-25/26, **Version:** 1
In Control: Facilities Contract Actions

Agenda Date: 9/16/2025

Approval of Facilities Contracts Actions

Procurement Services Division - Facilities Contracts

Brief Description:

(Approval of Facilities Contracts Actions) Recommends the ratification of Procurement Services Division contract actions taken by Facilities Contracts under delegated authority as listed in Attachment “A” including: award of advertised construction contracts; award of job order contracts; award of job order contract amendments; approval of change orders; completion of contracts; award of informal contracts; assignment and assumption of rights and delegation of duties; award of architectural and engineering contracts; extra services / amendments for architectural and engineering contracts and approved proposed contracts in Attachment B including fire life safety training and video creation services and materials testing and special inspection services contracts.

Action Proposed:

Ratify the Procurement Services Division (PSD) contract actions taken by Facilities Contracts under delegated authority as listed in Attachment “A” including: award of advertised construction contracts; award of job order contracts; award of job order contract amendments; approval of change orders; completion of contracts; award of informal contracts; assignment and assumption of rights and delegation of duties; award of architectural and engineering contracts; extra services / amendments for architectural and engineering contracts and approved proposed contracts in Attachment B including fire life safety training and video creation services and materials testing and special inspection services contracts.

Background:

Facilities Contracts staff prepares monthly reports for contract actions necessary for the execution of projects approved by the Board and contained in the FSD Strategic Execution Plan (SEP), and for the maintenance and operation of District facilities in accordance with District policies and Board-delegated authority. As described in the November 12, 2013 Board Report #048-13/14 Informative, detailed information is provided on the Facilities Services website.

Expected Outcomes:

Approval of these items will allow services provided by these contracts to proceed in support of FSD projects, District policies and goals, and the Board-approved FSD-SEP.

Board Options and Consequences:

The Board can approve all actions presented or postpone selected actions pending receipt of additional information. Non-ratification of actions awarded under delegated authority in Attachment “A” will result in the immediate discontinuance of services. While non-ratification may be legally defensible, it will likely result in costly litigation over discontinued payments or if the District attempts to reclaim payments made to a vendor. District costs will likely increase as fewer contractors compete for future procurements.

File #: Rep-006-25/26, **Version:** 1
In Control: Facilities Contract Actions

Agenda Date: 9/16/2025

Policy Implications:

This action does not change District policy and conforms to California Education Code section 17604 that permits the Board of Education to delegate authority for Facilities Contracts (Board Report #444-17/18), which the Board exercised on May 08, 2018.

Budget Impact:

The contract actions presented are within the budget authority previously approved by the Board. Unless indicated otherwise, all contract actions are Bond funded.

Student Impact:

The contract actions will help ensure that the students are provided with safe and healthy environments, and up to-date facilities that promote learning.

Equity Impact:

Not Applicable

Issues and Analysis:

There are no policy implications on these agreements.

Attachments:

Attachment A - Ratification of Facilities Contract Actions Awarded Under Delegated Authority

Submitted:

08/21/25

File #: Rep-006-25/26, Version: 1
In Control: Facilities Contract Actions

Agenda Date: 9/16/2025

RESPECTFULLY SUBMITTED,

APPROVED BY:


ALBERTO M. CARVALHO
Superintendent


PEDRO SALCIDO
Deputy Superintendent
Business Services & Operations

REVIEWED BY:

APPROVED BY:


DEVORA NAVERA REED
General Counsel


SUNG YON LEE
Deputy Chief Business Officer
Business Services and Operations

☒ Approved as to form.

REVIEWED BY:

APPROVED & PRESENTED BY:


KURT E. JOHN
Deputy Chief Financial Officer


MATTHEW A. FRIEDMAN
Chief Procurement Officer
Procurement Services Division

☒ Approved as to budget impact statement.

REVIEWED BY:


KRISZTINA TOKES
Chief Facilities Executive

☒ Approved as to facilities impact

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

AWARD OF ADVERTISED CONSTRUCTION CONTRACTS

Item A

\$38,334,937

Contractor/ ID No.	Site	Project Type	Project Authorization and Scope	Contract Term	Contract Amount	BD/ Region
Best Contracting Services, Inc./C9534	Alta Loma ES	Roofing Project	Board Report No. 036-21/22 09/14/21	06/06/25 – Completion	\$1,807,605	BD-1 West
Best Contracting Services, Inc./C9524	San Miguel ES	Roofing Project	Board Report No. 323-18/19 04/23/19	05/23/25 – Completion	\$748,855	BD-5 East
Best Contracting Services, Inc./C9536	Nevin Avenue ES	Roofing Project	Board Report No. 035-23/24 09/12/23	06/06/25 – Completion	\$1,613,015	BD-5 East
Best Contracting Services, Inc./C9538	Pio Pico MS	Roofing Project	Board Report No. 208-22/23 18/23	06/06/25 – Completion	\$2,209,910	BD-1 West
Best Contracting Services, Inc./C9599	Clover Avenue ES	Roofing Project	Board Report No. 009-22/23 08/30/22	06/16/25 – Completion	\$1,081,815	BD-1 West
Eberhard, A Tecta America Company LLC/ C9507	Westchester Enriched Science Magnets	Roofing Project	Board Report No. 086-17/18 11/14/17	06/23/25 – Completion	\$10,099,323	BD-4 West
Danny Letner Inc., dba Letner Roofing Company /C9669	Carson Senior HS	Roofing Project	Board Report No. 427-17/18 05/08/18	07/28/25 – Completion	\$5,546,800	BD-7 South
Best Contracting Services, Inc./C9673	Gompers MS	Roofing Project	Board Report No. 346-21/22 06/14/22	07/28/25 – Completion	\$2,232,614	BD-7 South

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

AWARD OF ADVERTISED CONSTRUCTION CONTRACTS

Item A (cont'd)

Contractor/ ID No.	Site	Project Type	Project Authorization and Scope	Contract Term	Contract Amount	BD/ Region
California Certified Construction and Electrical, Inc./C9554	El Camino Real Charter HS	New Pipelines Sitewide	Board Report No. 298-19/20 05/19/20	06/02/25 – Completion	\$7,989,000	BD-3 North
D. John Roser, Inc./C9556	Los Angeles ES	Green Schoolyard Improvement	Board Report No. 024-23/24 12/12/23	06/16/25 – Completion	\$1,150,000	BD-5 West
HZS Engineering Inc., dba HZS Construction /C9466	Ford Boulevard ES	Green Schoolyard Improvement	Board Report No. 024-23/24 12/12/23	05/28/25 – Completion	\$1,287,000	BD-2 East
D. John Roser, Inc./C9623	Gratts EEC	Outdoor Classroom & Campus Upgrade	Board Report No. 094-22/23 12/13/22	07/01/25 – Completion	\$679,000	BD-2 East
AP Construction Group, Inc., dba Air Plus /C9639	Highland Park Continuation HS	HVAC Project	Board Report No. 234-21/22 03/08/22	06/30/25 – Completion	\$1,890,000	BD-2 East

Ratification of formally competed construction contracts to provide roofing, pipeline, green schoolyard improvements, outdoor campus upgrade and HVAC services at various sites.

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

AWARD OF ADVERTISED CONSTRUCTION CONTRACTS – Best Value

Item B**\$38,234,000**

Contractor/ ID No.	Site	Project Type	Project Authorization and Scope	Contract Term	Contract Amount	BD/ Region
NSA Construction Group, Inc./C9630	Bright ES	Outdoor Learning Environment	Board Report No. 075-22/23 12/13/22	07/14/25 – Completion	\$3,196,000	BD-1 West
Masters Contracting Corp/C9368	McBride Special Education Center	Campus Improvement	Board Report No. 281-22/23 06/13/23	04/28/25 – Completion	\$12,165,500	BD-4 West
Ian Thomas Group/ C9508	Clover Avenue ES	Classroom Replacement- Emergency Soil Mitigation	Board Report No. 211-23/24 03/12/24	05/15/25 – Completion	\$5,598,000	BD-1 West
Masters Contracting Corp/C9458	Canoga Park MS	ADA Improvements	Board Report No. 007-22/23 08/30/22	06/02/25 – Completion	\$5,749,500	BD-3 North
Pars Arvin Construction, Inc./C9560	Marvin ES	ADA Barrier Removal & Site Utility Upgrades	Board Report No. 271-19/20 03/10/20	06/13/25 – Completion	\$11,525,000	BD-1 West

Ratification of formally competed best value construction contracts to provide outdoor learning environment, campus improvement, emergency soil mitigation, and Americans with Disabilities Act (ADA) improvement services at various sites.

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

**AWARD OF ADVERTISED CONSTRUCTION CONTRACTS –
East Region Bundle Pkg E3 Campus Safety Systems**

Item C

First Fire Systems, Inc., dba First Fire Alarm System			\$2,389,629
Site/ID No.	Contract Term	Contract Amount	Board District/ Region
Montara ES/C9698	07/03/25 - Completion	\$150,129	BD 5 – East
Woodlawn ES/C9699	07/03/25 – Completion	\$171,938	BD 5 – East
San Antonio ES/C9700	07/03/25 – Completion	\$153,966	BD 5 – East
Garza PC/C9701	07/03/25 – Completion	\$163,328	BD 2 – East
Lorena ES/C9702	07/03/25 – Completion	\$145,166	BD 2 – East
Sunrise ES/C9703	07/03/25 – Completion	\$169,824	BD 2 – East
Breed ES/C9704	07/03/25 – Completion	\$148,865	BD 2 – East
Brooklyn ES/C9705	07/03/25 – Completion	\$177,434	BD 2 – East
Monterey HS/C9707	07/03/25 – Completion	\$75,419	BD 2 – East
Highland Pk HS/C9708	07/03/25 – Completion	\$74,799	BD 2 – East
Trinity ES/C9709	07/03/25 – Completion	\$156,070	BD 5 – East
Esperanza ES/C9710	07/03/25 – Completion	\$145,668	BD 2 – East
Newmark HS/C9711	07/03/25 – Completion	\$102,473	BD 2 – East
Ride ES/C9712	07/03/25 – Completion	\$162,855	BD 5 – East
Hillside ES/C9713	07/03/25 – Completion	\$158,761	BD 2 – East
Mendez HS/C9714	07/03/25 – Completion	\$232,934	BD 2 – East

Ratification of formally competed Best Value contracts to provide video surveillance system (VMS), monitoring system and IP enabled intrusion alarm system as authorized on December 12, 2023 ([Board Report No. 024-23/24](#)), and subsequently authorized for defeasement on March 11, 2025 ([Board Report No. 247-24/25](#)).

Requester:

Soheil Katal, Chief Information Officer
Information Technology Services

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

**AWARD OF ADVERTISED CONSTRUCTION CONTRACTS –
South Region Bundle Pkg S3 Campus Safety Systems**
Item D

Telenet VoIP, Inc.			\$3,009,120
Site/ID No.	Contract Term	Contract Amount	Board District/ Region
118 th Street ES/C9573	07/15/25 – Completion	\$189,771	BD 7 – South
122 nd Street ES/C9575	07/15/25 – Completion	\$188,737	BD 7 – South
32 nd Street/USC Magnet/C9576	07/15/25 – Completion	\$189,765	BD 1 – South
66 th Street ES/C9577	07/15/25 – Completion	\$179,959	BD 7 – South
Alexander Science Center ES/C9579	07/15/25 – Completion	\$202,590	BD 1 – South
Graham ES/C9580	07/15/25 – Completion	\$163,469	BD 7 – South
Knox ES/C9581	07/15/25 – Completion	\$231,637	BD 7 – South
Raymond ES/C9582	07/15/25 – Completion	\$194,016	BD 1 – South
South Park ES/C9583	07/15/25 – Completion	\$179,596	BD 7 – South
153 rd Street ES/C9584	07/15/25 – Completion	\$169,019	BD 7 – South
186 th Street ES/C9585	07/15/25 – Completion	\$171,851	BD 7 – South
Angels Gate HS/C9586	07/15/25 – Completion	\$68,992	BD 7 – South
Caroldale LC/C9587	07/15/25 – Completion	\$209,668	BD 7 – South
Avalon HS/C9588	07/15/25 – Completion	\$63,389	BD 7 – South
Fries ES/C9589	07/15/25 – Completion	\$194,548	BD 7 – South
Normont ES/C9590	07/15/25 – Completion	\$193,827	BD 7 – South
Willenberg Special Education Center/C9591	07/15/25 – Completion	\$218,280	BD 7 – South

ATTACHMENT A**RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY**

Ratification of formally competed Best Value contracts to provide CCTV installation, Intrusion installation, cabling, and some pathway as authorized on December 12, 2023 ([Board Report No. 024-23/24](#)), and subsequently authorized for defeasement on March 11, 2025 ([Board Report No. 247-24/25](#)).

Requester:

Soheil Katal, Chief Information Officer
Information Technology Services

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

JOB ORDER CONTRACTS AWARDS –

Item E**\$29,000,000**

ABATEMENT AND DEMOLITION CONTRACTING BENCH		\$9,000,000
Contractor/ ID No.	Initial Contract Amount	Contact Term
Asbestos Instant Response, Inc. dba AIR Demolition & Environmental Solutions (SBE)/C9428	\$550,000	05/07/25 – 05/06/26 (with two (2) option years)
Karcher Environmental, Inc. (SBE)/C9441	\$550,000	05/07/25 – 05/06/26 (with two (2) option years)
Delta 4 Environmental, Inc., dba Asbestos Abatement (Micro SBE)/C9442	\$350,000	05/08/25 – 05/07/26 (with two (2) option years)

Ratification of three (3) formally competed Job Order Contract awards procured via RFQ R-25037 to provide abatement and demolition contracting services District-wide. Authorization to amend Job Order Contracts not-to-exceed the aggregate amount of \$9,000,000 without further board action.

GENERAL CONTRACTING BENCH		\$20,000,000
Contractor/ ID No.	Initial Contract Amount	Contract Term
Thomasville Construction, Inc. (SBE)/C9611	\$1,000,000	06/12/25 – 06/11/26
Exbon Development, Inc./C9610	\$900,000	06/11/25 – 06/10/26
R Brothers, Inc. (SBE)/C9571	\$1,000,000	06/09/25 – 06/08/26
Fredrick Towers, Inc. (SBE)/C9602	\$1,000,000	06/11/25 – 06/10/26

Ratification of four (4) formally competed Job Order Contract awards procured via RFQ R-25042 to provide general contracting services District-wide. Authorization to amend Job Order Contracts not-to-exceed the aggregate amount of \$20,000,000 without further board action.

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

JOB ORDER CONTRACTS AMENDMENTS

\$9,310,000

Item F

Contractor/ ID No.	Project Authorization and Scope	Contract Term Including This Amendment	Amendment Amount
Electrical and Low Voltage Contracting Services – Category A: CCTV & Intrusion Alarm System Installations Services – Information Technology Services			
Advanced Cable Solutions, Inc. / C446	Board Report No. 158-23/24 04/09/24	01/23/24 – 01/21/25	\$100,000
General Contracting Services – Facilities Services Division			
Reyes Electrical Contractor, Inc., dba Reyes Engineering Corp (SBE) / C1117	Board Report No. 013-24/25 09/10/24	06/21/24 – 06/20/25	\$2,300,000
Thomasville Construction, Inc. (SBE)/ C1120	Board Report No. 013-24/25 09/10/24	06/17/24 – 06/16/25	\$1,500,000
R Brothers, Inc. (SBE) / C1121	Board Report No. 013-24/25 09/10/24	06/14/24 – 06/13/25	\$3,000,000
Beta Investments & Contracts, Inc. (SBE) / C1123	Board Report No. 013-24/25 09/10/24	06/25/24 – 06/24/25	\$950,000
Fredrick Towers, Inc (SBE) / C1127	Board Report No. 013-24/25 09/10/24	06/13/24 – 06/12/25	\$1,460,000

Ratification of six (6) formally competed Job Order Contract Amendments to increase contract capacity of 6 formally competed contracts to provide electrical & low voltage and general contracting services District-wide.

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

Item G

B. APPROVAL OF CHANGE ORDERS

July 2025 = \$3,516,875

		<u>QUANTITY</u>	<u>AMOUNT</u>
	i. New Construction contract change orders that do not individually exceed 10 percent for July 2025 (Average Transaction: \$24,045; Median Transaction: \$11,298)	39	\$937,749
	ii. New Construction contract credit change orders for July 2025:	1	<\$1,179,976>
	iii. Existing Facilities contract change orders that do not individually exceed 15 percent for July 2025 (Average Transaction: \$16,329; Median Transaction: \$6,564):	262	\$4,278,359
	iv. Existing Facilities contract credit change orders for July 2025:	14	<\$519,257>
	v. Existing Facilities contract change orders that individually exceed 15 percent (but do not exceed 25 percent) for July 2025, requiring 75 percent approval by the Board:	0	\$0

C.	COMPLETION OF CONTRACTS – July 2025	31	\$316,452,789
-----------	--	----	---------------

D.	AWARD OF INFORMAL CONTRACTS (Not Exceeding \$114,800)		
	A & B Letters for July 2025 (Average Transaction: \$45,754; Median Transaction: \$27,794)	29	\$1,326,857

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

ASSIGNMENT AND ASSUMPTION OF RIGHTS AND DELEGATION OF DUTIES

Item H

Contractor/ ID No.	Services	Contract Term	Amount
FS3, Inc dba fs3 Hodges to Overwatch Construction Management / C3825	Construction Scheduling Review and/or Time Impact Analysis (Task Order)	05/01/24-04/30/29, includes two (2) one- year renewal options	\$0
WSP USA Environment & Infrastructure Inc. to WSP USA Inc. / C2314	California Environmental Quality Act Services (Professional Services)		\$0

Ratification of Assignment and Assumption Agreements for one task order agreement and one professional services agreement.

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

AWARD OF ARCHITECTURAL AND ENGINEERING CONTRACTS

Item I**\$4,626,487**

Contractor/ ID No.	Site	Project Type	Project Authorization and Scope	Contract Term	Contract Amount	BD/ Region
The Hill Partnership, Inc. dba HPI Architecture /C9546	Dodson MS	Classroom Upgrade	Board Report No. 064-24/25 10/22/24	05/23/25 – Closeout	\$373,835	BD-7 South
The Hill Partnership, Inc. dba HPI Architecture /C9567	Drew MS	Classroom Upgrade	Board Report No. 064-24/25 10/22/24	06/09/25 – Closeout	\$356,336	BD-7 South
Leo A. Daly California, Inc. dba Leo A. Daly /C9613	El Sereno MS	Classroom Upgrade	Board Report No. 064-24/25 10/22/24	06/13/25 – Closeout	\$346,832	BD-2 East
Leo A. Daly California, Inc. dba Leo A. Daly /C9614	Stevenson College & Career Prep	Classroom Upgrade	Board Report No. 064-24/25 10/22/24	07/01/25 – Closeout	\$436,753	BD-2 East
PBWS Architecture /C9547	Vanalden Avenue ES	Green Schoolyard Upgrade	Board Report No. 024-23/24 12/12/23	06/20/25 – Closeout	\$796,226	BD-4 North
DSH Architecture /C7507	San Pedro Street ES	Green Schoolyard Upgrade	Board Report No. 024-23/24 12/12/23	06/27/25 – Closeout	\$426,246	BD-5 East
QDG Incorporated, dba QDG Architecture /C9265	Manchester Avenue ES	Green Schoolyard Upgrade	Board Report No. 024-23/24 12/12/23	05/08/25– Closeout	\$506,680	BD-1 South
Mun Leu Architect, Inc. dba MLArchitecture /C9480	Encino Charter ES	Green Schoolyard Upgrade	Board Report No. 024-23/24 12/12/23	05/09/25– Closeout	\$401,325	BD-4 North

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

AWARD OF ARCHITECTURAL AND ENGINEERING CONTRACTS

Item I (cont'd)

Contractor/ ID No.	Site	Project Type	Project Authorization and Scope	Contract Term	Contract Amount	BD/ Region
Martinez + Marin Architecture /C9640	Willenberg Special Education Center	Accessibility Enhancement Project	Board Report No. 064-24/25 10/22/24	07/01/25 – Closeout	\$329,964	BD-7 South
Bureau Veritas /C7678	Pomelo Charter ES	Playground & Campus Exterior Upgrade	Board Report No. 018-23/24 08/22/23	06/17/25 – Closeout	\$652,290	BD-3 North

Ratification of design contracts to provide architectural and engineering services procured via RFQ's R-19012 and R-24025 to provide site analysis/preliminary schematic design, final schematic design, design development, and construction documents for various projects.

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

EXTRA SERVICES / AMENDMENTS FOR ARCHITECTURAL AND ENGINEERING CONTRACTS \$227,551

Item J**Extra Services Totals**

CONTRACT NOS.	1620141/C3074; 1920023/C1140; 1920023/C1140; 2220012/C3092; 2220013/C3093; 2420029/C3008; 2420037/C1200; 2420037/C1200; 2420037/C1200
---------------	---

Extra services are for design work that is not covered under the original Agreement. June and July Extra Services are listed at the following link: [BOE 006 Extra Services](#)

ATTACHMENT B
APPROVAL OF CONTRACTS NOT UNDER DELEGATED AUTHORITY

A. APPROVAL OF PROFESSIONAL SERVICES CONTRACTS

ITEM K

<u>Contractor/ ID No.</u>	<u>Contract Term</u>	<u>Not-To-Exceed Aggregate Amount</u>
Building Safety Solutions, Inc. (BSS) / C9166	10/01/25–09/30/30, includes two (2) one-year renewal options	\$356,914 General Funds (100%)

Authorization to award a formally competed contract selected from two (2) bids received to provide Fire Life Safety Training and Video Creation Services for Beaudry Building procured via RFP R-25024.

BSS will provide all training, content, videos, and services to remain current and in compliance with all applicable city codes and regulations. All site-specific content and videos will be hosted on a secure, District-managed platform (e.g., MyPLN) and remain valid for the duration of the contract.

The current training videos and certification programs, developed by BSS in the early 2000s, are becoming obsolete as BSS retires its legacy web-based platform. Additionally, concerns about potential cybersecurity risks have been raised by the Information Technology Services (ITS) Division.

Neither the District nor staff are approved by the City of Los Angeles to conduct on-line computer-based Fire/Life Safety Training. Additionally, the District does not have the resources in place to immediately develop a comprehensive life/safety training and certification program along with the necessary training videos that will meet and/or exceed the requirements outlined in Los Angeles Municipal Code (LAMC) 57.408. The selected vendor must maintain a valid Los Angeles Fire Department Certificate of Fitness to perform high-rise life safety services in the City of Los Angeles and must also be approved by the City to conduct on-line computer-based Fire/Life Safety Training.

Without approval the District risks regulatory non-compliance with LAMC 57.408 which could lead to penalties from the City of Los Angeles and potential building closure due to restriction on occupancy.

[Click here to view project scope, schedule, and budget](#)

Linked Materials
to
BR-006-25/26
Facilities Contracts
(Background Information)



LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report

209

Report Number:	048-13/14
Date:	November 12, 2013
Subject:	Facilities Services Division Contract Actions
Responsible Staff:	
Name:	Mark Hovatter, Chief Facilities Executive
Office/Division:	Facilities Services Division
Telephone No.:	(213) 241-4811

BOARD REPORT

- Action Proposed:** Staff proposes that the Board of Education (Board) ratify the Facilities Services Division (FSD) contract actions taken by Facilities Contracts under delegated authority as listed in Attachment “A” including: award of advertised construction contracts; job order contracts; approval of change orders; completion of contracts; award of informal contracts; rejection of bids; and extra services/amendments.
- Background:** Facilities Contracts staff prepares monthly reports for contract actions necessary for the execution of projects approved by the Board and contained in the FSD Strategic Execution Plan (SEP), and for the maintenance and operation of District facilities in accordance with District policies and Board-delegated authority. As described in the attached Informative, detailed information is provided on the Facilities Services website.
- Expected Outcomes:** Approval of these items will allow services provided by these contracts to proceed in support of FSD projects, District policies and goals, and the Board-approved FSD-SEP.
- Board Options and Consequences:** The Board can approve all actions presented or postpone selected actions pending receipt of additional information. Non-ratification of actions awarded under delegated authority in Attachment “A” will result in the immediate discontinuance of services. While non-ratification may be legally defensible, it will likely result in costly litigation over discontinued payments or if the District attempts to reclaim payments made to a vendor. District costs will likely increase as fewer contractors compete for future procurements.
- Policy Implications:** This action does not change District policy and conforms to *California Education Code section 17604* that permits the Board of Education to delegate authority for Facilities Contracts (Board Report #200-12/12), which the Board exercised on April 16, 2013.



210

LOS ANGELES UNIFIED SCHOOL DISTRICT Board of Education Report

Budget Impact:	The contract actions presented are within the budget authority previously approved by the Board.
Issues & Analysis:	There are no policy implications on these agreements.
Attachments:	Attachment "A" - Ratification of Facilities Contract Actions Awarded Under Delegated Authority.
X Informative	Attached
Desegregation Impact Statement	N/A



LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report

211

Respectfully submitted,

APPROVED BY:

Dr. JOHN E. DEASY
Superintendent

MICHELLE KING
Senior Deputy Superintendent
School Operations

APPROVED BY:

REVIEWED BY:

MARK HOVATTER
Chief Facilities Executive
Facilities Services Division

DAVID HOLMQUIST
General Counsel

Approved as to form.

PRESENTED BY:

TONY ATIENZA
Director of Budget Services and Financial
Planning

Approved as to budget impact statement.

YVETTE MERRIMAN-GARRETT
Director of Facilities Contracts
Facilities Services Division

ATTACHMENT A
RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

212
\$3,515,650

A. AWARD OF ADVERTISED CONSTRUCTION CONTRACTS

<u>CONTRACTOR</u>	<u>BID NO./ CONTRACT NO.</u>	<u>SCHOOL / PROJECT</u>	<u>AMOUNT</u>
Axis Construction, Inc. (SBE)	1310133 / 4400002172	<u>Reseda HS</u> Convert shop classroom into a flexible science classroom Board Member: Mónica Ratliff	\$549,000
LA Electricom, Inc. (SBE)	1310135 / 4400002044	<u>Los Angeles Academy MS</u> Replace and upgrade energy management system including chillers and boilers Board Member: Richard Vladovic	\$1,334,000
Edessa Construction, Inc. (SBE)	1410010 / 4400002088	<u>Strathern ES</u> Paint and refinish the exterior and masonry/stucco of the school buildings and appurtenant structures Board Member: Mónica Ratliff	\$71,000

The District has engaged in two-tier procurement for its Year 2012 Local Area Network (LAN) Modernization Projects (ITD/E-Rate) partially funded by Federal E-Rate grants. The fourteen (14) contracts below represent the 2nd tier procurement made pursuant to Public Contract Code Section 20118.2.

<u>CONTRACTOR</u>	<u>BID NO./ CONTRACT NO.</u>	<u>SCHOOL / PROJECT</u>	<u>AMOUNT</u>
Edessa Construction, Inc. (SBE)	1410000 / 1200206	<u>Eagle Rock ES</u> Board Member: Bennett Kayser	\$139,075
LA Electricom, Inc. (SBE)	1410004 / 1300027	<u>Castlebay Lane ES</u> Board Member: Tamar Galatzan	\$232,870
Edessa Construction, Inc. (SBE)	1410006 / 1200204	<u>Lillian ES</u> Board Member: Bennett Kayser	\$70,880
Jam Fire Protection, Inc. dba Jam Corporation (SBE)	1410007 / 1200204	<u>Vanalden ES</u> Board Member: Tamar Galatzan	\$61,000
RB Developing Group, Inc. (SBE)	1410009 / 1300026	<u>Warner ES</u> Board Member: Steve Zimmer	\$106,125
WNG Construction J V, Inc. (SBE)	1410011 / 1200206	<u>McBride Special Education Center</u> Board Member: Steve Zimmer	\$139,000
WNG Construction J V, Inc. (SBE)	1410012 / 1200204	<u>Salvin Special Education Center</u> Board Member: Mónica García	\$85,100
LA Electricom, Inc. (SBE)	1410013 / 1200204	<u>Breed ES</u> Board Member: Mónica García	\$83,600
RB Developing Group, Inc. (SBE)	1410015 / 1300025	<u>Woodland Hills Elementary Charter for Enriched Studies</u> Board Member: Steve Zimmer	\$97,125
RB Developing Group, Inc. (SBE)	1410016 / 1300025	<u>Wilbur ES</u> Board Member: Steve Zimmer	\$116,125
WNG Construction J V, Inc. (SBE)	1410017 / 1300027	<u>Chatsworth Park ES</u> Board Member: Tamar Galatzan	\$123,800
RB Developing Group, Inc. (SBE)	1410020/ 1300025	<u>Encino Charter ES</u> Board Member: Steve Zimmer	\$104,125

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

213

A. AWARD OF ADVERTISED CONSTRUCTION CONTRACTS (CONT.'D)

<u>CONTRACTOR</u>	<u>BID NO./ CONTRACT NO.</u>	<u>SCHOOL / PROJECT</u>	<u>AMOUNT</u>
RB Developing Group, Inc. (SBE)	1410021/ 1300025	<u>Paseo del Rey Elementary Natural Science Magnet</u> Board Member: <u>Steve Zimmer</u>	\$107,125
Jam Fire Protection, Inc. dba Jam Corporation (SBE)	1410022 / 1300025	<u>Roscomare ES</u> Board Member: <u>Steve Zimmer</u>	\$95,700

17406 CONTRACTS

<u>CONTRACTOR</u>	<u>CONTRACT NO.</u>	<u>SCHOOL/PROJECT</u>	<u>AMOUNT</u>
None			

17406 CONTRACT AMENDMENTS

<u>CONTRACTOR</u>	<u>CONTRACT NO.</u>	<u>SCHOOL / PROJECT</u>	<u>AMOUNT</u>
None			

JOB ORDER CONTRACT AWARDS

\$34,400,000

<u>CONTRACTOR</u>	<u>BID NO. / CONTRACT NO.</u>	<u>SCHOOL / PROJECT</u>	<u>AMOUNT</u>
Reyes Electrical Contractor, Inc. (SBE)	1330032/4400002312	<u>Electrical and Wireless Local Area Network (WLAN) / LAN Contracting Services</u> Board Member: <u>District Wide</u>	\$350,000
WNG Construction JV, Inc. (SBE)	1330037/4400002195	<u>Electrical and Wireless Local Area Network (WLAN) / LAN Contracting Services</u> Board Member: <u>District Wide</u>	\$3,000,000
Telenet VoIP, Inc. (SBE)	1330039/4400002173	<u>Electrical and Wireless Local Area Network (WLAN) / LAN Contracting Services</u> Board Member: <u>District Wide</u>	\$3,000,000
First Fire Systems, Inc. (SBE)	1330041/4400002311	<u>Electrical and Wireless Local Area Network (WLAN) / LAN Contracting Services</u> Board Member: <u>District Wide</u>	\$5,000,000
First Fire Systems, Inc. (SBE)	1330042/4400002218	<u>Electrical and Wireless Local Area Network (WLAN) / LAN Contracting Services</u> Board Member: <u>District Wide</u>	\$5,000,000
Enterprise Construction, Inc. (SBE)	1330049/4400002214	<u>General Contracting Services</u> Board Member: <u>District Wide</u>	\$ 350,000
Enterprise Construction, Inc. (SBE)	1330050/4400002215	<u>General Contracting Services</u> Board Member: <u>District Wide</u>	\$350,000
Fredrick Towers, Inc. (SBE)	1330051/4400002216	<u>General Contracting Services</u> Board Member: <u>District Wide</u>	\$350,000
Telenet VoIP, Inc. (SBE)	1430000/4400002175	<u>Electrical and Wireless Local Area Network (WLAN) / LAN Contracting Services</u> Board Member: <u>District Wide</u>	\$ 1,000,000

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

A. WARD OF ADVERTISED CONSTRUCTION CONTRACTS

214

JOB ORDER CONTRACT AWARDS (CONT.'D)

<u>CONTRACTOR</u>	<u>RFP NO. / CONTRACT NO.</u>	<u>SCHOOL / PROJECT</u>	<u>AMOUNT</u>
Technion Contractors TCI, Inc. (SBE)	1430001/4400002217	<u>Electrical and Wireless Local Area Network (WLAN) / LAN Contracting Services</u> Board Member: <u>District Wide</u>	\$ 1,000,000
Jam Fire Protection Inc. dba JAM Corporation (SBE)	1430002/4400002177	<u>Electrical and Wireless Local Area Network (WLAN) / LAN Contracting Services</u> Board Member: <u>District Wide</u>	\$ 1,000,000
WNG Construction JV, Inc. (SBE)	1430003/4400002223	<u>Electrical and Wireless Local Area Network (WLAN) / LAN Contracting Services</u> Board Member: <u>District Wide</u>	\$ 3,000,000
JAM Fire Protection Inc. dba JAM Corporation (SBE)	1430004/4400002178	<u>Electrical and Wireless Local Area Network (WLAN) / LAN Contracting Services</u> Board Member: <u>District Wide</u>	\$ 3,000,000
Telenet VoIP, Inc. (SBE)	1430005/4400002174	<u>Electrical and Wireless Local Area Network (WLAN) / LAN Contracting Services</u> Board Member: <u>District Wide</u>	\$ 3,000,000
WNG Construction JV, Inc. (SBE)	1430007/4400002224	<u>Electrical and Wireless Local Area Network (WLAN) / LAN Contracting Services</u> Board Member: <u>District Wide</u>	\$ 5,000,000

JOB ORDER CONTRACT AMENDMENTS

<u>CONTRACTOR</u>	<u>RFP NO. / CONTRACT NO. (Amendment No.)</u>	<u>SCHOOL / PROJECT</u>	<u>CAPACITY INCREASE</u>
None			

B. APPROVAL OF CHANGE ORDERS

\$3,095,642

	<u>QUANTITY</u>	<u>AMOUNT</u>
Construction contracts that have change orders which do not individually exceed 10 percent for September 2013 (Average Transaction: \$15,297)	117	\$1,789,774
Repair and modernization contracts that have change orders which do not individually exceed 15 percent for September 2013 (Average Transaction: \$17,412)	75	\$1,305,868
Repair and modernization contracts that have change orders which individually exceed 15 percent (but do not exceed 25 percent) for September 2013 that require 75 percent approval by the Board.	0	

QUANTITY

C. COMPLETION OF CONTRACTS – September 2013

18

D. AWARD OF INFORMAL CONTRACTS (Not Exceeding \$83,400)

\$1,728,830

	<u>QUANTITY</u>	<u>AMOUNT</u>
A & B Letters for July, August and September 2013 (Avg. Trans. \$12,090)	143	\$1,728,830

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

215

E. REJECTION OF BIDS

<u>BID NO./CONTRACT NO.</u>	<u>SCHOOL/PROJECT</u>	<u>REASON</u>
1410031/1310026	<u>Calabash Charter Academy ES</u> Year 2012 Local Area Network Modernization Board Member: <u>Steve Zimmer</u>	All bids were rejected due to excessive cost. The project will be re-advertised with an anticipated construction start date of early December 2013.
1410032/1310026	<u>Overland ES</u> Year 2012 Local Area Network Modernization Board Member: <u>Marguerite Poindexter-Lamotte</u>	All bids were rejected due to excessive cost. The project will be redesigned and re-advertised with an anticipated construction start date of early December 2013.
1410043/1310026	<u>Hamilton SH Complex & Marina Del Rey MS</u> Wireless Local Area Network Modernization (WLANS) Board Member: <u>Marguerite Poindexter LaMotte & Steve Zimmer</u>	All bids were rejected due to excessive cost. The project will be redesigned and re-advertised with an anticipated construction start date of early December 2013
1410044/1300026	<u>University SH & Wright MS STEAM Magnet</u> Wireless Local Area Network Modernization (WLANS) and Partial Local Area Network (LAN) Replacement Board Member: <u>Steve Zimmer</u>	All bids were rejected due to excessive cost. The project will be re-advertised with an anticipated construction start date of early December, 2013.

F. TERMINATION OF CONTRACTS FOR CONVENIENCE

<u>CONTRACTOR</u>	<u>CONTRACT NO.</u>	<u>SCHOOL/PROJECT</u>	<u>REASON</u>
-------------------	---------------------	-----------------------	---------------

None

G. AWARD OF NEGOTIATED SOLE SOURCE CONTRACT

<u>CONTRACTOR</u>	<u>BID NO./ CONTRACT NO.</u>	<u>SCHOOL/PROJECT</u>	<u>AMOUNT</u>
-------------------	----------------------------------	-----------------------	---------------

None

H. AWARD OF ARCHITECTURAL AND ENGINEERING CONTRACTS

TASK ORDERS ISSUED AGAINST CONTRACTS AWARDED THROUGH AN RFQ PROCESS

<u>CONTRACTOR</u>	<u>BID NO./ CONTRACT NO.</u>	<u>SCHOOL/PROJECT</u>	<u>NOT-TO-EXCEED AMOUNT</u>
-------------------	----------------------------------	-----------------------	---------------------------------

None

ARCHITECTURAL AND ENGINEERING CONTRACT AMENDMENTS

<u>CONTRACTOR</u>	<u>BID NO./ CONTRACT NO. (Amendment No.)</u>	<u>SCHOOL/PROJECT</u>	<u>AMOUNT</u>
-------------------	--	-----------------------	---------------

None

EXTRA SERVICES /AMENDMENTS**\$189,279**

Contract No.: 0120090, 0120253, 520001, 0520176, 0720016, 0820002, and 0820040

INTEROFFICE CORRESPONDENCE
 Los Angeles Unified School District
 Facilities Services Division

INFORMATIVE

TO: Members, Board of Education
 Dr. John E. Deasy, Superintendent

DATE: October 25, 2013

FROM: Yvette Merriman-Garrett
 Director of Facilities Contracts

**SUBJECT: FACILITIES SERVICES DIVISION CONTRACT ACTIONS TO BE
 INCLUDED IN FACILITIES SERVICES DIVISION WEBSITE**

Due to the July 1, 2013 reorganization, the Facilities Services website will now provide additional detail for contract actions taken by FSD within delegated authority as listed in the regular Board of Education Report Attachment "A". The transactions include Change Orders for new and existing facilities; Completion of contracts including job order contract completions; Award of informal contracts; and Extra Services agreements.

The FSD website is located at <http://www.laschools.org/new-site/contracts/boe-contract-actions> and is accessible to Board Members and District staff through their regular District sign-on.

If you have any questions or require additional information, please contact me at (213) 241-2650.

c: Michelle King
 David Holmquist
 Mark Hovatter
 Enrique Boull't
 George Silva
 Jefferson Crain
 Hugh Tucker



Los Angeles Unified School District

333 South Beaudry Ave,
Los Angeles, CA 90017

Board of Education Report

File #: Rep-444-17/18, Version: 1

**ADOPTED BY BOARD
MAY 8, 2018**

Delegations of Authority for Procurement and Facilities Contracts

May 08, 2018

Procurement Services Division

Action Proposed:

Staff proposes the Board of Education approve the renewal of the updated delegations of authority for Procurement contracts, including Facilities contracts, as set forth in Attachment "A" (District Delegation Forms), with an effective date of July 1, 2018.

Background:

On May 9, 2017 (Board Report No. 463-16/17), the Board of Education approved Delegations of Authority for Procurement (including Facilities Contracts) through June 30, 2018. The delegations of authority set forth in Attachment "A" renew updated delegations of authority, including the following significant changes:

- Changed Requesting Division to OFFICE OF THE BUSINESS MANAGER to reflect the change in organizational reporting structure.
- Added to section (iii) Construction under APPROVAL OF PROCUREMENT CONTRACTS the delegation limit of repair and general maintenance up to \$1 million.
- Allows sunset date to expire.

Expected Outcomes:

Renewal of the attached delegations of authority will enable the LAUSD to continue to award, manage and enforce contracts in support of the District's Operational and Facilities programs, while reducing administrative effort, time and costs.

Board Options and Consequences:

Approving the renewal of the attached delegations will enable the District to expedite contract actions and obtain the highest quality services and materials at the lowest possible cost, without loss of accountability. This action will allow the District to continue to award, manage and enforce contracts in support of the LAUSD's building and modernization, and operational programs, while reducing administrative effort, time and costs. Delaying these actions while waiting for future Board approval for projects already approved by the Board needlessly decreases efficiency and increases administrative, project and legal costs. All delegated actions will continue to be submitted to the Board for ratification in accordance with the California Education Code, Government Code, Public Contract Code and all other applicable statutory provisions.

Policy Implications:

This action supports the Board's initiatives to streamline processes, enhance efficiency, and reduce expenditures.

Budget Impact:

There is no budget impact.

File #: Rep-444-17/18, **Version:** 1

ADOPTED BY BOARD
MAY 8, 2018

Student Impact:

This will allow Procurement and Facilities Contracts to efficiently execute contracts to ensure that students are provided with safe and healthy environments and up-to-date facilities that promote learning.

Attachments:


Attachment "A" - District Delegation Form

File #: Rep-444-17/18, Version: 1

**ADOPTED BY BOARD
MAY 8, 2018**

RESPECTFULLY SUBMITTED,

APPROVED & PRESENTED BY:


VIVIAN EKCHIAN
Interim Superintendent


JANICE SAWYER
Interim Business Manager
Office of the Business Manager

REVIEWED BY:

APPROVED & PRESENTED BY:


DAVID HOLMQUIST
General Counsel


SUNG YON LEE
Interim Chief Procurement Officer
Procurement Services Division

 Approved as to form.

REVIEWED BY:


CHERYL SIMPSON
Director, Budget Services and Financial Planning

 Approved as to budget impact statement.

REVIEWED BY:


MARK HOVATTER
Chief Facilities Executive
 Approved as to facilities impact.

☐ Fiscal Delegation (to enter contracts)
☐ Operational Delegation (to perform a non-fiscal operation)

Del. No. []

**ADOPTED BY BOARD
MAY 8, 2018**

ATTACHMENT A

DISTRICT DELEGATION FORM

Requesting Division: OFFICE OF THE BUSINESS MANAGER

Select One: ☐ NEW DELEGATION ☒ AMENDED DELEGATION

Date: May 08, 2018 Board Report No.: 444-17/18

Delegation No.: _____ Amendment No.: 7

DESIRED TEXT OF DELEGATION (*Underline amended language if applicable*)

APPROVAL OF PROCUREMENT CONTRACT POLICY, AWARD, MANAGEMENT, AND ENFORCEMENT (Procurement Contracts) ~~April 16, 2013 June 10, 2014 May 12, 2015 May 10, 2016 May 09, 2017~~ May 08, 2018

Delegation of authority to the Superintendent, or his or her designee who shall have authority to further delegate to another employee of the LAUSD, to create and implement procedures, advertise, issue requests for qualification and proposal, negotiate, evaluate, award, execute, commence and continue performance of, enforce, authorize payments under, amend, exercise options, and terminate (whether by default or convenience) Procurement contracts (including Facilities contracts), as described below, subject to and in accordance with California Public Contract Code (PCC), California Education Code, California Government Code, and any other statutory provisions as applicable including, but not limited to, the following:

- (i) to establish contractor and vendor prequalification requirements and procedures; to make contractor prequalification determinations; to reject bids or proposals; to declare bidders non-responsive or non-responsible; to release low bidders and award to the next lowest responsible, responsive bidder; and to release or assess payment against bid bonds;
- (ii) to act as hearing officer to conduct and render decisions regarding the procurement and enforcement of Procurement contracts, including, without limitation, bid protests, bid appeals, contractor responsibility hearings, subcontractor substitution hearings; provided, the Board of Education shall be given written notification of any decision rendered by the hearing officer within 5 business days following the issuance of such decision;
- (iii) to review, analyze and respond to claims and petitions for leave to present late claims presented to LAUSD pursuant to Government Code section 900 et seq.;
- (iv) to withhold contract payments and penalties from contractors who fail to comply with contract terms and conditions;
- (v) to establish and assess appropriate penalties or other permitted sanctions for contractor violations of the Subletting and Subcontracting Fair Practices Act of the California Public

To Be Completed By the Board Secretariat Only:
 Board Approval: ☐ Yes ☐ No

Board Approval Date: _____

☐ Fiscal Delegation (to enter contracts)
☐ Operational Delegation (to perform a non-fiscal operation)

Del. No. ☐ ☐

Contract Code and to make recommendations for penalties and other permitted sanctions to the Department of Industrial Relations for contractor violations of the California Labor Code;

- (vi) to approve change orders within the limits set forth in California Public Contract Code section 20118.4;
- (vii) to issue notices to proceed or other documents necessary to commence contract performance and to file notices of completion or cessation;
- (viii) to retain a percent of payment for completed work as required by current statute and to release retention upon a determination that the contract has been completed satisfactorily and a notice of completion is ~~filed with the county~~ issued;
- (ix) to arbitrate contract matters and pay arbitration awards not to exceed \$25,000 per disputed amount;
- (x) to authorize payments of liquidated damages assessed against the District or to assess liquidated damages against a contractor pursuant to contract terms, and to authorize payments of interest and penalties pursuant to contract terms or the California Public Contract Code;
- (xi) to award or assess payment against performance bonds;
- (xii) to approve assignment of contract money to a surety which has invoked its right of assignment under its indemnity agreement with the contractor;
- (xiii) to sell, lease, or dispose of all personal property that is surplus, obsolete or not suitable for school use in accordance with applicable law;
- (xiv) to sell Los Angeles Unified School District published materials, not to exceed \$10,000 per sale, to any person, political subdivision, public officer or agency or educational institution;
- (xv) to issue P-cards and Buyer cards;
- (xvi) to purchase, as needed, the following items essential to the operation of the District where a competitive selection for an equivalent source or product is not available:
 - a. Bus Pass/MTA tokens
 - b. Institutional membership renewals (e.g., National Association of School Boards)
 - c. School/LAUSD accreditation (e.g., Western Association of Schools and Colleges)
 - d. Renewal subscription fees (e.g., software license renewal, maintenance of leased equipment)
 - e. Student testing

**ADOPTED BY BOARD
MAY 8, 2018**

To Be Completed By the Board Secretariat Only:
 Board Approval: ☐ Yes ☐ No

Board Approval Date: _____

☐ Fiscal Delegation (to enter contracts)
☐ Operational Delegation (to perform a non-fiscal operation)

Del. No. []

- f. Postage, metering, and sorting fees
- g. Waste fees as associated with the Office of Environmental Health and Safety
- h. Advance payments to utilities
- i. Shipping and handling charges
- j. Utility fees

(xvii) to make purchases through "piggyback" contracts within the authority limits defined herein in accordance with procurement law.

(xviii) adopt and publish procedures and required guidelines for evaluating the qualifications of the bidders that ensure the best value selections by the District are conducted in a fair and impartial manner pursuant to section 20119 et seq. of the Public Contract Code.

DISTRICT DELEGATION FORM

Requesting Division: OFFICE OF THE BUSINESS MANAGER

Select One: ☐ NEW DELEGATION ☒ AMENDED DELEGATION

Date: May 08, 2018 Board Report No.: 444-17/18

Delegation No.: _____ Amendment No.: 7

DESIRED TEXT OF DELEGATION (*Underline amended language if applicable*)

APPROVAL OF PROCUREMENT CONTRACTS

(Procurement Contracts) ~~April 16, 2013 June 10, 2014 May 12, 2015 May 10, 2016 May 09, 2017~~
May 08, 2018.

Delegation of authority to the Superintendent, or his or her designee who shall have authority to further delegate to another employee of the LAUSD to create and implement procedures, advertise, issue requests for qualification, proposal and other solicitations, negotiate, evaluate, award, execute, commence and continue performance of, enforce, authorize payments under, amend, exercise options, and terminate (whether by default or convenience) with respect to the following Procurement contracts (including Facilities contracts), as described below:

(i) **Architectural and Engineering Services**

Contracts for architectural and engineering services for approved Facilities projects so long as such contracts do not impose costs upon the District in excess of the applicable Board-approved project budget.

ADOPTED BY BOARD MAY 8, 2018

To Be Completed By the Board Secretariat Only:
Board Approval: ☐ Yes ☐ No

Board Approval Date: _____

- ☐ Fiscal Delegation (to enter contracts)
☐ Operational Delegation (to perform a non-fiscal operation)

Del. No. []

(ii) Professional Services (Excluding Architectural and Engineering)

Contracts, exercising existing options or amendments, for all other professional services (other than architectural and engineering services) up to \$250,000 for a single contract action for approved projects with cumulative contract actions for a single Division with a single contractor not to exceed \$500,000 in a 12-month period.

(iii) Construction

Contracts for construction as permitted by and in accordance with the California Public Contract Code and California Education Code (including, without limitation, publicly bid contracts, job order contracts, informal A and B letter agreements, ~~and~~ takeover and completion contracts, contracts pursuant to Public Contract Code section 20119 et seq. ("best value,"), and contracts pursuant to California Education Code section 17406 ("lease-leaseback") up to \$85 million per contract for approved Facilities projects.

Contracts for routine repair and general maintenance up to \$1 million.

Notwithstanding the foregoing, the authority to execute contracts pursuant to California Education Code section 17515 ("joint occupancy") is expressly excluded from this delegation of authority.

(iv) Supply Contracts and General Services

Contracts for supplies, materials, equipment, general services, and other personal property up to \$250,000 or for contracts that do not impose costs upon the District in excess of the applicable Board-approved program or project budget authority.

(v) Special One-Time Delegated Authority

Contracts for the procurement of regular Distribution Center materiel of food, and food related supplies (including miscellaneous food items), furniture, office essentials, custodial/maintenance & operations, paper, visual arts, educational supplies/tools, science/home economics/first aide, audio visual, athletic equipment, forms & publications, and music which do not exceed a total of 75% of the average annual expenditures per fiscal year.

(vi) Special Services and Other Services

Contracts for special services and other services specified by Government Code section 53060 or similar authority up to \$250,000 per action.

(vii) Miscellaneous

Contracts under which the District will receive no more than \$500,000 in exchange for or in recognition of services or products provided by the District.

**ADOPTED BY BOARD
MAY 8, 2018**

To Be Completed By the Board Secretariat Only:
 Board Approval: ☐ Yes ☐ No

Board Approval Date: _____

☐ Fiscal Delegation (to enter contracts)
☐ Operational Delegation (to perform a non-fiscal operation)

Del. No. ☐

Single/Sole source contracts in amounts not to exceed the value of the relevant grant for each vendor that is identified as the District's exclusive partner in the grant.

Authority to enter into other single/sole source contracts with a single entity up to \$1 million subject to applicable law. This authority shall not be delegated below the ~~Chief Executive Officer, Office of Educational Services~~ Business Manager, Office of the Business Manager level.

Contracts and other instruments, invoices, and obligations not otherwise covered by items (i) through (vii) above up to \$25,000 per action. This delegation shall include the authority to take or authorize actions necessary for or incidental to the foregoing contract authority, provided such actions are routine ministerial actions, relatively minor transactions, or non-substantive matters.

DISTRICT DELEGATION FORM

Requesting Division: OFFICE OF THE BUSINESS MANAGER

Select One: ☐ NEW DELEGATION ☒ AMENDED DELEGATION

Date: May 08, 2018 Board Report No.: 444-17/18

Delegation No.: _____ Amendment No.: 7

DESIRED TEXT OF DELEGATION (*Underline amended language if applicable*)

SOLICIT PROPOSALS AND CONDUCT A PRICE DISCOVERY AUCTION FOR UTILITIES, GOODS, AND SERVICES

(Procurement Contracts) ~~April 16, 2013 June 10, 2014 May 12, 2015 May 10, 2016 May 09, 2017~~
May 08, 2018.

Delegation of authority to the Superintendent, or his or her designee, who shall have authority to further delegate to another employee of the LAUSD, to conduct a competitive price discovery auction or a similar process utilizing transparent and objective selection criteria to receive a real-time market quote on electricity, natural gas and/or any other type of energy or for goods and services, and to enter into a contract with the lowest responsive/responsible bidder if such contract is expected to result in cost savings to the District as compared to current goods/services from the local utility or through other procurement options.

PRIOR AMENDMENTS:	<u>Date</u>	<u>Amendment No.</u>	<u>Board Report No.</u>
	<u>April 10, 2012</u>	<u>1</u>	<u>211 – 11/12</u>
	<u>April 16, 2013</u>	<u>2</u>	<u>200 – 12/13</u>
	<u>June 10, 2014</u>	<u>3</u>	<u>474 – 13/14</u>
	<u>May 12, 2015</u>	<u>4</u>	<u>461 – 14/15</u>
	<u>May 10, 2016</u>	<u>5</u>	<u>311 – 15/16</u>
	<u>May 09, 2017</u>	<u>6</u>	<u>463 – 16/17</u>

**ADOPTED BY BOARD
MAY 8, 2018**

To Be Completed By the Board Secretariat Only:
 Board Approval: ☐ Yes ☐ No

Board Approval Date: _____

- ☐ Fiscal Delegation (to enter contracts)
☐ Operational Delegation (to perform a non-fiscal operation)

Del. No. []

 Signature
Sung Yon Lee, Interim Chief Procurement Officer
 Division Head/Sr. Administrator (Print Name)

May 08, 2018
 Date Submitted

 Signature

 Office of the Board Secretariat (Print Name)

 Date Received

ADOPTED BY BOARD MAY 8, 2018

 To Be Completed By the Board Secretariat Only:
 Board Approval: ☐ Yes ☐ No

Board Approval Date: _____



Board of Education Report

File #: Rep-036-21/22, **Version:** 1

Amendment to the Facilities Services Division Strategic Execution Plan to Define and Approve Seven Projects that Address Critical Replacement and Upgrade Needs at Schools

September 14, 2021

Facilities Services Division

Action Proposed:

Approve an amendment to the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to define and approve seven projects that address critical replacement and upgrade needs at schools, as listed on Attachment A. And further authorize the Chief/Deputy Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the proposed projects, including budget modifications and the purchase of equipment and materials. The total combined budget for the seven projects is \$12,716,601.

Background:

Priorities for the expenditure of capital funding are evaluated to ensure the District's most pressing priorities are being addressed. More than 70 percent of Los Angeles Unified School District (Los Angeles Unified or District) school buildings were built more than 50 years ago, and more than \$50 billion of unfunded school facilities needs have been identified Districtwide, and these needs grow every year. As the District's capital needs far exceed available funding, the most pressing unfunded critical needs will continue to be addressed based on an evaluation of known facilities conditions and needs at schools. Projects developed under this category of need, *Critical Replacements and Upgrades of School Building/Site Systems and Components*, will replace failing building systems that create safety concerns and are disruptive to school operations. Systems in the worst condition, especially those that pose a safety hazard and/or will negatively impact school operations and other building systems if not addressed, will be addressed first.

The project proposals contained in this Board Report align with these priorities. Attachment A provides additional details pertaining to the seven proposed projects.

Expected Outcomes:

Staff anticipates that the Board of Education will approve the proposed action to define and approve seven projects to address critical replacement and upgrade needs that will improve student health, safety and educational quality.

Board Options and Consequences:

A "yes" vote will authorize staff to proceed with the expenditure of bond funds to undertake the project proposals in accordance with the provisions set forth in Los Angeles Unified local bond measures K, R, Y, Q, and RR. If the proposed action is not approved, bond funds will not be expended, and critical replacement and upgrade needs will remain unaddressed.

Policy Implications:

The proposal is consistent with the Los Angeles Unified's long-term goal to address unmet school facilities needs and significantly improve the conditions of aging and deteriorating school facilities as described in Los Angeles Unified local bond measures.

Budget Impact:

The total combined budget for the seven projects is \$12,716,601. The projects will be funded with Bond Program funds earmarked specifically for critical replacements and upgrades of school building/site systems and components.

Each project budget was prepared based on the current information known and assumptions about the project scope, site conditions, and market conditions. Individual project budgets will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise, and will be adjusted accordingly to enable the successful completion of each project.

Student Impact:

Approval of the proposed projects enables the District to continue our ongoing efforts to undertake facilities improvements that help ensure students are provided with safe school environments that promote teaching and learning.

Issues and Analysis:

It may be necessary to undertake feasibility studies, site analysis, scoping, and/or due diligence activities on the proposed projects prior to initiating design. As necessary, the Office of Environmental Health and Safety (OEHS) will evaluate the proposed projects in accordance with the California Environmental Quality Act (CEQA) to ensure compliance. If through the planning and design process it is determined that the proposed project scope(s) will not sufficiently address the critical needs identified, the project scope, schedule and budget will be revised accordingly.

Bond Oversight Committee Recommendations:

This item was considered by the School Construction Bond Citizen's Oversight Committee (BOC) at its meeting on September 2, 2021. Staff has concluded that this proposed Facilities SEP amendment is in alignment with BOC recommendations and will facilitate Los Angeles Unified's ability to successfully implement the Facilities SEP.

Attachments:

Attachment A - Project Definitions for Seven Projects that Address Critical Replacement and Upgrade Needs
Attachment B - BOC Resolution

Informatives:

None.

Submitted:

8/27/21

RESPECTFULLY SUBMITTED,

MEGAN K. REILLY
Interim Superintendent

APPROVED BY:

PEDRO SALCIDO
Interim Deputy Superintendent

REVIEWED BY:

DEVORA NAVERA REED
General Counsel

☒ Approved as to form.

APPROVED BY:

MARK HOVATTER
Chief Facilities Executive
Facilities Services Division

REVIEWED BY:

TONY ATIENZA
Director, Budget Services and Financial Planning

☒ Approved as to budget impact statement.

PRESENTED BY:

ROBERT LAUGHTON
Director of Maintenance and Operations
Facilities Services Division



LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report
Attachment A

1. Alta Loma Elementary School – Project to Provide New Roofing

- *Local District West, Board District 1 – McKenna*
- *Project Background and Scope* – This project is to provide approximately 45,398 square feet of new roofing sitewide, including the installation of new gutters and downspouts and painting of affected areas.
- *Project Budget* -- \$1,027,482
- *Project Schedule* – Construction is anticipated to begin in Q3 2022 and conclude in Q4 2022.

2. Bell Senior High School – Project to Provide New Roofing

- *Local District East, Board District 5 – Goldberg*
- *Project Background and Scope* – This project is to provide approximately 212,217 square feet of new roofing sitewide, including the installation of new gutters and downspouts and painting of affected areas.
- *Project Budget* -- \$3,597,686
- *Project Schedule* – Construction is anticipated to begin in Q2 2022 and conclude in Q4 2022.

3. Foshay Learning Center – Project to Provide New Roofing

- *Local District Central, Board District 1 – McKenna*
- *Project Background and Scope* – This project is to provide approximately 92,142 square feet of new roofing sitewide, including the installation of new gutters and downspouts, gravity vents, and painting of affected areas.
- *Project Budget* -- \$2,252,088
- *Project Schedule* – Construction is anticipated to begin in Q2 2022 and conclude in Q4 2022.

4. Palms Middle School – Project to Provide New Roofing

- *Local District West, Board District 1 – McKenna*
- *Project Background and Scope* – This project is to provide approximately 156,947 square feet of new roofing sitewide, including the installation of new gutters and downspouts and painting of affected areas.
- *Project Budget* -- \$2,105,197
- *Project Schedule* – Construction is anticipated to begin in Q2 2022 and conclude in Q4 2022.

5. Richland Elementary School – Project to Provide New Roofing

- *Local District West, Board District 4 – Melvoin*
- *Project Background and Scope* – This project is to provide approximately 52,238 square feet of new roofing sitewide, including the installation of new gutters and downspouts and painting of affected areas.
- *Project Budget* -- \$1,093,435
- *Project Schedule* – Construction is anticipated to begin in Q3 2022 and conclude in Q4 2022.

6. Roscomare Elementary School – Project to Provide New Roofing

- *Local District West, Board District 4 – Melvoin*
- *Project Background and Scope* – This project is to provide approximately 43,664 square feet of new roofing sitewide, including the installation of new gutters and downspouts and painting of affected areas.
- *Project Budget* -- \$913,087
- *Project Schedule* – Construction is anticipated to begin in Q2 2022 and conclude in Q3 2022.



LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report
Attachment A

7. Walnut Park Elementary School – Project to Provide New Roofing

- *Local District East, Board District 5 – Goldberg*
- *Project Background and Scope* – This project is to provide approximately 81,168 square feet of new roofing sitewide, including the installation of new gutters and downspouts and painting of affected areas.
- *Project Budget* -- \$1,727,626
- *Project Schedule* – Construction is anticipated to begin in Q3 2022 and conclude in Q1 2023.

LOS ANGELES UNIFIED SCHOOL DISTRICT

SCHOOL CONSTRUCTION BOND CITIZENS' OVERSIGHT COMMITTEE

Rachel Greene, Chair

Tenth District PTSA

Chris Hannan, Vice-Chair

L.A. Co. Federation of Labor AFL-CIO

Margaret Fuentes, Secretary

LAUSD Student Parent

Araceli Sandoval-Gonzalez, Executive Committee

Early Education Coalition

Alvin Trotter, Jr., Executive Committee

L.A. Area Chamber of Commerce

Tracy Bartley31st District PTSA**Laura Baz**

LAUSD Student Parent

Neelura Bell

CA Charter School Association

Jeffrey Fischbach

CA Tax Reform Assn.

Greg Good

L.A. City Mayor's Office

D. Michael Hamner

American Institute of Architects

Hyepin Im

L.A. City Controller's Office

Susan Linschoten

L.A. Co. Auditor-Controller's Office

Dolores Sobalvarro

AARP

Roger Uy

Assoc. General Contractors of CA

Celia Ayala (Alternate)

Early Education Coalition

Dr. Clarence Monteclaro (Alternate)

Tenth District PTSA

Samantha Rowles (Alternate)

LAUSD Student Parent

Connie Yee (Alternate)

L.A. Co. Auditor-Controller's Office

Joseph P. Buchman – Legal Counsel

Burke, Williams & Sorensen, LLP

Lori Raineri and Keith Weaver – Oversight Consultants

Government Financial Strategies

Timothy Popejoy

Bond Oversight Administrator

Perla Zitle

Bond Oversight Coordinator

RESOLUTION 2021-24

BOARD REPORT NO. 036-21/22

**AMENDMENT TO THE FACILITIES SERVICES DIVISION STRATEGIC
EXECUTION PLAN TO DEFINE AND APPROVE SEVEN PROJECTS
THAT ADDRESS CRITICAL REPLACEMENT AND UPGRADE NEEDS
AT SCHOOLS**

WHEREAS, District Staff proposes that the Board of Education approve an amendment to the Facilities Services Division (FSD) Strategic Execution Plan (SEP) to define and approve seven projects that address critical replacement and upgrade needs at schools with a budget of \$12,716,601 (the "Projects") as described in Board Report 036-21/22 attached hereto; and authorize the Chief Procurement Officer and/or the Chief Facilities Executive, and/or his designee(s), to execute all instruments necessary to implement the Projects; and

WHEREAS, Projects developed under the School Upgrade Program category of need, *Critical Replacements and Upgrades of School Building/Site Systems and Components*, will replace failing building systems projects that create safety concerns and are disruptive to school operations; and

WHEREAS, The Projects are consistent with the Los Angeles Unified's long-term goal to address unmet school facilities needs and significantly improve the conditions of aging and deteriorating school facilities as described in Los Angeles Unified local bond measures; and

WHEREAS, District Staff has determined that the Projects are necessary to improve student health, safety and educational quality; and

Bond Oversight Committee333 S. Beaudry Avenue, 23rd Floor, Los Angeles, CA 90017 ♦ Phone: 213. 241.5183 ♦ Fax: 213.241.8354 ♦ www.laschools.org/bond

RESOLUTION 2021-24**AMENDMENT TO THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO DEFINE AND APPROVE SEVEN PROJECTS THAT ADDRESS CRITICAL REPLACEMENT AND UPGRADE NEEDS AT SCHOOLS**

WHEREAS, the Board of Education's approval of the Projects will authorize District Staff to proceed with the expenditure of bond funds to undertake the Projects in accordance with the provisions set forth in Los Angeles Unified local bond Measures K, R, Y, Q, and RR; and

WHEREAS, District Staff has concluded that the proposed SEP amendment will facilitate implementation of the FSD SEP, and therefore, it will not adversely affect the District's ability to successfully complete the FSD SEP.

NOW, THEREFORE, BE IT RESOLVED THAT:

1. The School Construction Citizens' Bond Oversight Committee recommends that the Board of Education adopt an amendment to the Facilities Services Division (FSD) Strategic Execution Plan (SEP) to define and approve seven projects that address critical replacement and upgrade needs at schools, with a budget of \$12,716,601, as defined in Board Report 036-21/22, a copy of which is attached hereto in the form it was presented to the BOC and is incorporated herein by reference.
2. This resolution shall be transmitted to the Los Angeles Unified School District Board of Education and posted on the Oversight Committee's website.
3. The District is directed to track the above recommendation and to report on the adoption, rejection, or pending status of the recommendations as provided in section 6.2 of the Charter and Memorandum of Understanding between the Oversight Committee and the District.

ADOPTED on September 2, 2021, by the following vote:

AYES: 12

ABSTENTIONS: 0

NAYS: 0

ABSENCES: 3

/Rachel Greene/

Rachel Greene
Chair

/Margaret Fuentes/

Margaret Fuentes
Secretary



Board of Education Report

File #: Rep-323-18/19, **Version:** 1

Amendment to the Facilities Services Division Strategic Execution Plan to Define and Approve Six Projects that Address Critical School Repair Needs

April 23, 2019

Facilities Services Division

Action Proposed:

Staff proposes that the Board of Education approve an amendment to the Facilities Services Division (FSD) Strategic Execution Plan (SEP) to define and approve six projects that address critical school repair needs, as listed on Attachment A. Staff further proposes that the Board authorize the (Interim) Chief/Deputy Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the proposed projects, including budget modifications and the purchase of equipment and materials. The total combined budget for the six projects is \$8,709,620.

Background:

As the District's capital needs far exceed available funding, priorities for the expenditure of capital funding are evaluated to ensure the District's most pressing priorities are being addressed. Based on an evaluation of known facilities conditions and needs at schools, the following types of projects have been identified as the most pressing unfunded critical school repair and safety needs that should continue to be addressed within the limited funding available:

- Failing, deteriorated, and outdated building systems and components
- School buildings, rooms and/or facilities deemed unsafe for occupancy
- Other critical health and safety concerns, urgent/emergency conditions, and/or health and safety code compliance issues that may arise

The project proposals contained in this Board Report align with these identified types of pressing critical school repair and safety conditions. The list consists of flooring, roofing, and synthetic turf replacement projects. Attachment A provides additional details pertaining to the proposed projects.

Expected Outcomes:

Staff anticipates that the Board of Education will approve the proposed action to define and approve six projects to address critical school repair needs that will improve student health, safety and educational quality.

Board Options and Consequences:

A "yes" vote will authorize staff to proceed with the expenditure of bond funds to undertake the project proposals in accordance with the provisions set forth in Measures K, R, Y and Q. If the proposed action is not approved, bond funds will not be expended and critical school repair needs will remain unaddressed.

File #: Rep-323-18/19, **Version:** 1

Policy Implications:

The action is consistent with the District's commitment to address unmet school facilities needs and provide students with a safe and healthy learning environment. Moreover, the proposal is aligned with the Board-adopted Facilities Bond Program strategy to address unfunded and pressing school facilities needs related to safety, compliance, and instructional requirements (Board Report No. 048-17/18).

Budget Impact:

The total combined budget for the six projects is \$8,709,620. The projects will be funded with Bond Program funds earmarked specifically for critical school repair and safety improvements to school building components.

Each project budget was prepared based on the current information known, and assumptions about, the project scope, site conditions, and market conditions. Individual project budgets will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise, and will be adjusted accordingly to enable the successful completion of each project.

Student Impact:

Continuing our efforts to undertake critical school repair and safety improvement projects is a vital component to the District's ability to provide safe school environments that promote teaching and learning.

Issues and Analysis:

It may be necessary to undertake feasibility studies, site analysis, scoping, and/or due diligence activities on the proposed projects prior to initiating design. As necessary, the Office of Environmental Health and Safety (OEHS) will evaluate the proposed projects in accordance with the California Environmental Quality Act (CEQA) to ensure compliance. If through the planning and design process it is determined that the proposed project scope(s) will not sufficiently address the critical need identified, the project scope, schedule and budget will be revised accordingly.

Bond Oversight Committee Recommendations:

This item was considered by the BOC at its meeting on April 11, 2019. Staff has concluded that this proposed FSD SEP amendment will facilitate implementation of the FSD SEP, and therefore, it will not adversely affect the District's ability to successfully complete the FSD SEP.

Attachments:

Attachment A - Project Definitions for Six Projects that Address Critical School Repair Needs
BOC Resolution

Informatives:

None.

Submitted:

4/5/19

File #: Rep-323-18/19, Version: 1

RESPECTFULLY SUBMITTED,


 AUSTIN BEUTNER
 Superintendent


APPROVED BY:


 MARK HOVATTER
 Chief Facilities Executive
 Facilities Services Division

REVIEWED BY:


 DAVID HOLMQUIST
 General Counsel

PRESENTED BY:


 ROBERT LAUGHTON
 Director of Maintenance & Operations
 Facilities Services Division

 Approved as to form.

REVIEWED BY:


 CHERYL SIMPSON
 Director, Budget Services and Financial Planning

 Approved as to budget impact statement.



**LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report**

Attachment A

1. Fairfax High School – Project to Provide New Flooring

- *Local District West, Board District 4 – Melvoin*
- *Project Background and Scope* – This project is to replace approximately 254,000 square feet of deteriorated flooring.
- *Project Budget* -- \$1,973,282
- *Project Schedule* – Construction is anticipated to begin in Q2 2020 and conclude in Q3 2022.

2. Franklin High School – Project to Provide New Flooring

- *Local District Central, Board District 5 – Vacant*
- *Project Background and Scope* – This project is to replace approximately 178,000 square feet of deteriorated flooring.
- *Project Budget* -- \$1,265,358
- *Project Schedule* – Construction is anticipated to begin in Q1 2020 and conclude in Q1 2022.

3. Pacoima Charter Elementary School – Project to Provide New Roofing

- *Local District Northeast, Board District 6– Gonez*
- *Project Background and Scope* – This project is to provide approximately 34,000 square feet of new roofing at eight buildings, including new gutters and downspouts, and painting of affected areas.
- *Project Budget* -- \$831,475
- *Project Schedule* – Construction is anticipated to begin in Q1 2020 and conclude in Q3 2020.

4. San Miguel Elementary School – Project to Provide New Roofing

- *Local District East, Board District 5– Vacant*
- *Project Background and Scope* – This project is to provide approximately 22,000 square feet of new roofing at 13 buildings, including new gutters and downspouts, and painting of affected areas.
- *Project Budget* -- \$568,423
- *Project Schedule* – Construction is anticipated to begin in Q4 2019 and conclude in Q2 2020.

5. South Gate Middle School – Project to Provide New Roofing

- *Local District East, Board District 5– Vacant*
- *Project Background and Scope* – This project is to provide approximately 93,000 square feet of new roofing at 19 buildings, including new gutters and downspouts, installation of skylights and painting of affected areas.
- *Project Budget* -- \$2,405,492
- *Project Schedule* – Construction is anticipated to begin in Q3 2019 and conclude in Q3 2020.

6. Belmont High School – Project to Provide New Synthetic Turf Field

- *Local District Central, Board District 2– Garcia*
- *Project Background and Scope* – This project is to replace approximately 67,000 square feet of deteriorated synthetic turf at the football field.
- *Project Budget* -- \$1,665,590
- *Project Schedule* – Construction is anticipated to begin in Q4 2019 and conclude in Q2 2020.

SCHOOL CONSTRUCTION BOND CITIZENS' OVERSIGHT COMMITTEE

Rachel Greene, Chair

Tenth District PTSA

Bevin Ashenmiller, Vice-Chair

LAUSD Student Parent

Susan Linschoten, Secretary

L.A. Co. Auditor-Controller's Office

Araceli Sandoval-Gonzalez, Executive**Committee**

Early Education Coalition

Karen Krygier, Executive Committee

L.A. City Controller's Office

Jeffrey Fischbach

CA Tax Reform Assn.

Greg Good

L.A. City Mayor's Office

Michael Keeley

CA Charter School Association

Kate Mergen

Assoc. General Contractors of CA

Ron Miller

L.A. Co. Federation of Labor AFL-CIO

Scott Pansky

L.A. Area Chamber of Commerce

Dolores Sobalvarro

AARP

Douglas Teiger

American Institute of Architects

Celia Ayala (Alternate)

Early Education Coalition

Arlene Barrera (Alternate)

L.A. Co. Auditor-Controller's Office

Jose Zambrano (Alternate)

Tenth District PTSA

(Vacant)

LAUSD Student Parent

(Vacant)31st District PTSA**Joseph P. Buchman – Legal Counsel**

Burke, Williams & Sorensen, LLP

Lori Raineri and Keith Weaver – Oversight**Consultants**

Government Financial Strategies

Timothy Popejoy

Bond Oversight Administrator

Perla Zitle

Asst. Administrative Analyst

RESOLUTION 2019-9

BOARD REPORT NO. 323-18/19

**AMENDMENT TO THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION
PLAN TO DEFINE AND APPROVE SIX PROJECTS THAT ADDRESS CRITICAL SCHOOL
SAFETY AND REPAIR NEEDS**

WHEREAS, District Staff proposes that the Board of Education approve an amendment to the Facilities Services Division (FSD) Strategic Execution Plan (SEP) to define and approve six projects that address critical school repair needs with a budget of \$8,709,620 (the "Projects") as described in Board Report 323-18/19 attached hereto; and authorize the Chief/Deputy Procurement Officer and/or the Chief Facilities Executive, and/or his designee(s), to execute all instruments necessary to implement the proposed projects; and

WHEREAS, District Staff has determined that the Projects are necessary to improve student health, safety and educational quality; and

WHEREAS, District Staff has determined that the Projects will help facilitate the implementation of the Facilities Bond Program strategy to address unfunded and pressing school facilities related to safety, compliance, and instructional requirements; and

WHEREAS, the Projects are consistent with the District's commitment to address unmet school facilities needs and provide students with a safe and healthy learning environment; and

WHEREAS, the Board of Education's approval of the Projects will authorize District Staff to proceed with the expenditure of bond funds to undertake the Projects in accordance with the provisions set forth in Measures K, R, Y and Q; and

Bond Oversight Committee333 S. Beaudry Avenue, 23rd Floor, Los Angeles, CA 90017 ♦ Phone: 213. 241.5183 ♦ Fax: 213.241.8354 ♦ www.laschools.org/bond

Page 1

RESOLUTION 2019-9**AMENDMENT TO THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO DEFINE AND APPROVE SIX PROJECTS THAT ADDRESS CRITICAL SCHOOL SAFETY AND REPAIR NEEDS**

WHEREAS, District Staff has concluded that the proposed SEP amendment will facilitate implementation of the FSD SEP, and therefore, it will not adversely affect the District's ability to successfully complete the FSD SEP.

NOW, THEREFORE, BE IT RESOLVED THAT:

1. The School Construction Citizens' Bond Oversight Committee recommends that the Board of Education adopt an amendment to the Facilities Services Division (FSD) Strategic Execution Plan (SEP) to define and approve four projects that address critical school safety and repair needs, with a budget of \$8,709,620, as defined in Board Report 323-18/19, a copy of which is attached hereto in the form it was presented to the BOC and is incorporated herein by reference.
2. This resolution shall be transmitted to the Los Angeles Unified School District Board of Education and posted on the Oversight Committee's website.
3. The District is directed to track the above recommendation and to report on the adoption, rejection, or pending status of the recommendations as provided in section 6.2 of the Charter and Memorandum of Understanding between the Oversight Committee and the District.

ADOPTED on April 11, 2019, by the following vote:

AYES: 8

ABSTENTIONS: 0

NAYS: 0

ABSENCES: 4



Rachel Greene
Chair



Bevin Ashenmiller
Vice-Chair



Board of Education Report

File #: Rep-035-23/24, **Version:** 1

Define and Approve Three Projects to Provide Critical Replacements and Upgrades of School Building/Site Systems and Components and Amend the Facilities Services Division Strategic Execution Plan to Incorporate Therein

September 12, 2023

Facilities Services Division

Action Proposed:

Define and approve three projects to provide critical replacements and upgrades of school building/site systems and components (Projects), as described on Exhibit A, and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein. The total combined budget for the three Projects is \$5,421,661.

Authorize the Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the proposed Projects, including budget modifications and the purchase of equipment and materials.

Background:

Priorities for the expenditure of capital funding are evaluated to ensure the District's most pressing priorities are being addressed. More than 70 percent of Los Angeles Unified School District (Los Angeles Unified or District) school buildings were built more than 50 years ago, and more than \$50 billion of unfunded school facilities needs have been identified Districtwide, and these needs grow every year. As the District's capital needs far exceed available funding, the most pressing unfunded critical needs will continue to be addressed based on an evaluation of known facilities conditions and needs at schools.

Projects developed under this category of need, Critical Replacements and Upgrades of School Building/Site Systems and Components, will replace failing building systems that create safety concerns and are disruptive to school operations. Systems in the worst condition, especially those that pose a safety hazard and/or will negatively impact school operations and other building systems if not addressed, will be addressed first. The Project proposals contained in this Board Report align with these priorities.

Bond Oversight Committee Recommendations:

This item was considered by the School Construction Bond Citizens' Oversight Committee (BOC) at its meeting on August 31, 2023. Staff has concluded that this proposed Facilities SEP amendment is in alignment with BOC recommendations and will facilitate Los Angeles Unified's ability to successfully implement the Facilities SEP.

Expected Outcomes:

Staff anticipates that the Board of Education will adopt the proposed amendment to the Facilities SEP to define and approve three Projects that address critical replacement and upgrade needs. Approval will authorize staff to proceed with the implementation of the proposed Projects to improve student health, safety, and educational quality.

Board Options and Consequences:

Adoption of the proposed action will authorize staff to proceed with the expenditure of Bond Program funds to undertake the proposed Projects in accordance with the provisions set forth in Los Angeles Unified local bond measures K, R, Y, Q, and RR. If the proposed action is not approved, Bond Program funds will not be expended, and critical replacement and upgrade needs will remain unaddressed.

Policy Implications:

The proposal is consistent with Los Angeles Unified's long-term goal to address unmet school facilities needs and significantly improve the conditions of aging and deteriorating school facilities as described in Los Angeles Unified local bond measures. The proposed action advances Los Angeles Unified's 2022-2026 Strategic Plan, Pillar 4 Operational Effectiveness, Modernizing Infrastructure by providing critical replacements and upgrades at schools.

Budget Impact:

The total combined budget for the three Projects is \$5,421,661. The Projects will be funded with Bond Program funds earmarked specifically for critical replacements and upgrades of school building/site systems and components.

Each Project budget was prepared based on the current information known and assumptions about the Project scope, site conditions, and market conditions. Individual Project budgets will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise and will be adjusted accordingly to enable the successful completion of each Project.

Student Impact:

Approval of the proposed Projects enables the District to continue ongoing efforts to undertake facilities improvements that help ensure the approximately 1,500 students attending these three schools are provided with a safe school environment that promotes teaching and learning.

Equity Impact:

Building components/systems in the worst condition, especially those that pose a safety hazard and/or will negatively impact school operations and other building systems if not addressed, will be addressed first.

Issues and Analysis:

It may be necessary to undertake feasibility studies, site analysis, scoping, and/or due diligence activities on the proposed Projects prior to initiating design. As necessary, the Office of Environmental Health and Safety (OEHS) will evaluate the proposed Projects in accordance with the California Environmental Quality Act (CEQA) to ensure compliance. If, through the planning and design process, it is determined the proposed Project scopes will not sufficiently address the critical needs identified, the Project scopes, schedule, and budget will be revised accordingly.

Attachments:

- Exhibit A - Projects to Replace Failing Building Systems that Create Safety Concerns and are Disruptive to School Operations
- Exhibit B - BOC Resolution

File #: Rep-035-23/24, Version: 1

Informatives:
None

Submitted:
08/11/23

RESPECTFULLY SUBMITTED,


ALBERTO M. CARVALHO
Superintendent

APPROVED BY:


PEDRO SALCIDO
Deputy Superintendent,
Business Services and Operations

REVIEWED BY:


DEVORA NAVERA REED
General Counsel☒ Approved as to form.


APPROVED BY:


KRISZTINA TOKES
Chief Facilities Executive
Facilities Services Division

REVIEWED BY:


NOLBERTO DELGADILLO
Deputy Chief Business Officer, Finance☒ Approved as to budget impact statement.

PRESENTED BY:


INDIA R. GRIFFIN
Director of Facilities Maintenance and Operations

**LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report**

Exhibit A

**Projects to Replace Failing Building Systems that Create Safety Concerns and are
Disruptive to School Operations**

1. Erwin Elementary School – Project to Provide New Roofing

- *Board District 6 – Kelly Gonez, North Region*
- *Project Background and Scope* – This project is to provide approximately 90,000 square feet of new roofing at 27 buildings, including the installation of new gutters and downspouts, and painting of affected areas.
- *Project Budget* -- \$2,555,744
- *Project Schedule* – Construction is anticipated to begin in Q1-2024 and conclude in Q3-2024.

2. Nevin Elementary School – Project to Provide New Roofing

- *Board District 5 – Jackie Goldberg, East Region*
- *Project Background and Scope* – This project is to provide approximately 42,000 square feet of new roofing at eight buildings, including the installation of new gutters and downspouts, and painting of affected areas.
- *Project Budget* -- \$1,183,007
- *Project Schedule* – Construction is anticipated to begin in Q1-2024 and conclude in Q3-2024.

3. Strathern Elementary School – Project to Provide New Roofing

- *Board District 6 – Kelly Gonez, North Region*
- *Project Background and Scope* – This project is to provide approximately 63,400 square feet of new roofing at 23 buildings, including the installation of new gutters and downspouts, and painting of affected areas.
- *Project Budget* -- \$1,682,910
- *Project Schedule* – Construction is anticipated to begin in Q1-2024 and conclude in Q3-2024.

SCHOOL CONSTRUCTION BOND CITIZENS' OVERSIGHT COMMITTEE

Margaret Fuentes, Chair

LAUSD Student Parent

D. Michael Hamner, FAIA, Vice-Chair

American Institute of Architects

Samantha Rowles, Secretary

LAUSD Student Parent

Robert Campbell, Executive Committee

L.A. Co. Auditor-Controller's Office

Scott Pansky, Executive Committee

L.A. Area Chamber of Commerce

Neelura Bell

CA Charter School Association

Jeffrey Fischbach

CA Tax Reform Assn.

Chris Hannan

L.A. Co. Federation of Labor AFL-CIO

Patrick MacFarlane

Early Education Coalition

Jennifer McDowell

L.A. City Mayor's Office

Brian Mello

Assoc. General Contractors of CA

Dr. Clarence Monteclaro

Tenth District PTSA

William O. Ross IV

31st District PTSA

Dolores Sobalvarro

AARP

Chad Boggio (Alternate)

L.A. Co. Federation of Labor AFL-CIO

Connie Yee (Alternate)

L.A. Co. Auditor-Controller's Office

Vacant

L.A. City Controller's Office

Joseph P. Buchman – Legal Counsel

Burke, Williams & Sorensen, LLP

Lori Raineri and Keith Weaver – Oversight Consultants

Government Financial Services Joint
Powers Authority

Timothy Popejoy

Bond Oversight Administrator

Perla Zitle

Bond Oversight Coordinator

RESOLUTION 2023-25

BOARD REPORT 035-23/24

**RECOMMENDING BOARD APPROVAL TO DEFINE AND APPROVE THREE PROJECTS
TO PROVIDE CRITICAL REPLACEMENTS AND UPGRADES OF SCHOOL BUILDING/SITE
SYSTEMS AND COMPONENTS AND AMEND THE FACILITIES SERVICES DIVISION
STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN**

WHEREAS, District Staff proposes that the Board of Education (Board) define and approve three projects that address critical replacement and upgrade needs at schools with a combined budget of \$5,421,661 (the “Projects”) as described in Board Report 035-23/24 attached hereto, and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein, and authorize the Chief Procurement Officer and/or the Chief Facilities Executive, and/or their designee(s), to execute all instruments necessary to implement the Projects; and

WHEREAS, Projects developed under the School Upgrade Program category of need, Critical Replacements and Upgrades of School Building/Site Systems and Components, will replace failing building systems that create safety concerns and are disruptive to school operations; and

WHEREAS, The Projects are consistent with the Los Angeles Unified School District (Los Angeles Unified or District)’s long-term goal to address unmet school facilities needs and significantly improve the conditions of aging and deteriorating school facilities as described in Los Angeles Unified local bond measures; and

WHEREAS, District Staff has determined that the Projects are necessary to improve student health, safety and educational quality; and

WHEREAS, The Board of Education’s approval of the Projects will authorize District Staff to proceed with the expenditure of Bond Program funds to undertake the Projects in accordance with the provisions set forth in Los Angeles Unified local bond measures K, R, Y, Q, and RR; and

RESOLUTION 2023-25**194****RECOMMENDING BOARD APPROVAL TO DEFINE AND APPROVE THREE PROJECTS TO PROVIDE CRITICAL REPLACEMENTS AND UPGRADES OF SCHOOL BUILDING/SITE SYSTEMS AND COMPONENTS AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN**

WHEREAS, District staff has concluded that this proposed Facilities SEP amendment will facilitate Los Angeles Unified's ability to successfully complete the Facilities SEP.

NOW, THEREFORE, BE IT RESOLVED THAT:

1. The School Construction Citizens' Bond Oversight Committee (BOC) recommends that the Board of Education define and approve three Projects that address critical replacement and upgrade needs at schools, with a combined budget of \$5,421,661, and amend the Facilities SEP to incorporate therein, as described in Board Report 035-23/24, a copy of which is attached hereto in the form it was presented to the BOC and is incorporated herein by reference.
2. This resolution shall be transmitted to the Los Angeles Unified School District Board of Education and posted on the Oversight Committee's website.
3. The District is directed to track the above recommendation and to report on the adoption, rejection, or pending status of the recommendations as provided in section 6.2 of the Charter and Memorandum of Understanding between the Oversight Committee and the District.

ADOPTED on August 31, 2023, by the following vote:

AYES: 11

ABSTENTIONS: 0

NAYS: 0

ABSENCES: 3

/Margaret Fuentes/

Margaret Fuentes
Chair

/Michael Hamner/

D. Michael Hamner
Vice-Chair



Board of Education Report

[Back to Order of Business](#)

File #: Rep-208-22/23, Version: 1

Define and Approve the Pio Pico Middle School Roofing Project and Amend the Facilities Services Division Strategic Execution Plan to Incorporate Therein

April 18, 2023

Facilities Services Division

Action Proposed:

Define and approve the Pio Pico Middle School Roofing Project (Project) and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein. The total budget for the Project is \$1,697,449.

Authorize the Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement this proposed project, including budget modifications and the purchase of equipment and materials.

Background:

Priorities for the expenditure of capital funding are evaluated to ensure the District's most pressing priorities are being addressed. More than 70 percent of Los Angeles Unified School District (Los Angeles Unified or District) school buildings were built more than 50 years ago, and more than \$50 billion of unfunded school facilities needs have been identified District-wide, and these needs grow every year. As the District's capital needs far exceed available funding, the most pressing unfunded critical needs will continue to be addressed based on an evaluation of known facilities conditions and needs at schools. Projects developed under this category of need, Critical Replacements and Upgrades of School Building/Site Systems and Components, will replace failing building systems that create safety concerns and are disruptive to school operations. Systems in the worst condition, especially those that pose a safety hazard and/or will negatively impact school operations and other building systems if not addressed, will be addressed first.

The proposed Project aligns with these priorities. This project is to provide approximately 68,495 square feet of new roofing campus wide including the installation of new gutters, downspouts, and painting of affected areas. Construction is anticipated to begin in the third quarter of 2023 and be completed in the first quarter of 2024.

Bond Oversight Committee Recommendations:

This item was considered by the School Construction Bond Citizens' Oversight Committee (BOC) at its meeting on March 16, 2023. Staff has concluded that this proposed Facilities SEP amendment is in alignment with BOC recommendations and will facilitate Los Angeles Unified's ability to successfully implement the Facilities SEP.

Expected Outcomes:

Staff anticipates the Board of Education will adopt this proposed amendment to the Facilities SEP to define and approve the Project to address critical replacement and upgrade needs. Approval will authorize staff to proceed with the implementation of the proposed Project to improve student health, safety, and educational quality.

File #: Rep-208-22/23, Version: 1

Board Options and Consequences:

Adoption of the proposed action will authorize staff to proceed with the expenditure of Bond Program funds to undertake the proposed Project in accordance with the provisions set forth in Los Angeles Unified local bond measures K, R, Y, Q, and RR. If the proposed action is not approved, Bond Program funds will not be expended, and critical replacement and upgrade needs will remain unaddressed.

Policy Implications:

The proposal is consistent with the Los Angeles Unified's long-term goal to address unmet school facilities needs and significantly improve the conditions of aging and deteriorating school facilities as described in Los Angeles Unified local bond measures.

Budget Impact:

The Project budget is \$1,697,449 and will be funded with Bond Program funds earmarked specifically for critical replacements and upgrades of school building/site systems and components.

The Project budget was prepared based on the current information known and assumptions about the Project scope, site conditions, and market conditions. The Project budget will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise and will be adjusted accordingly to enable the successful completion of the Project.

Student Impact:

Approval of the Project enables the District to continue our ongoing efforts to undertake facilities improvements that help ensure the approximately 210 students attending the school are provided with a safe school environment that promotes teaching and learning.

Equity Impact:

Building components/systems in the worst condition, especially those that pose a safety hazard and/or will negatively impact school operations and other building systems if not addressed, will be addressed first.

Issues and Analysis:

It may be necessary to undertake feasibility studies, site analysis, scoping, and/or due diligence activities on the proposed Project prior to initiating design. As necessary, the Office of Environmental Health and Safety (OEHS) will evaluate the proposed Project in accordance with the California Environmental Quality Act (CEQA) to ensure compliance. If, through the planning and design process, it is determined the proposed Project scope will not sufficiently address the critical needs identified, the Project scope, schedule, and budget will be revised accordingly.

Attachments:

Attachment A - BOC Resolution

Informatives:

None

Submitted:

03/08/2023

File #: Rep-208-22/23, Version: 1


RESPECTFULLY SUBMITTED,


ALBERTO M. CARVALHO
Superintendent

APPROVED BY:


PEDRO SALCIDO
Deputy Superintendent,
Business Services and Operations

REVIEWED BY:


DEVORA NAVERA REED
General Counsel

☒ Approved as to form.

APPROVED BY:



MARK HOVATTER
Chief Facilities Executive
Facilities Services Division

REVIEWED BY:


TONY ATIENZA
Director, Budget Services and Financial Planning

☒ Approved as to budget impact statement.

PRESENTED BY:


INDIA R. GRIFFIN
Director of Facilities Maintenance and Operations

Type text here

LOS ANGELES UNIFIED SCHOOL DISTRICT**SCHOOL CONSTRUCTION BOND CITIZENS' OVERSIGHT COMMITTEE****Margaret Fuentes, Chair**

LAUSD Student Parent

D. Michael Hamner, Vice-Chair

American Institute of Architects

Jennifer McDowell, Secretary

L.A. City Mayor's Office

Susan Linschoten, Executive Committee

L.A. Co. Auditor-Controller's Office

Scott Pansky, Executive Committee

L.A. Area Chamber of Commerce

Neelura Bell

CA Charter School Association

Jeffrey Fischbach

CA Tax Reform Assn.

Chris Hannan

L.A. Co. Federation of Labor AFL-CIO

Hyepin Im

L.A. City Controller's Office

Brian Mello

Assoc. General Contractors of CA

Dr. Clarence Montecarlo

Tenth District PTSA

William O. Ross, IV31st District PTSA**Samantha Rowles**

LAUSD Student Parent

Araceli Sandoval-Gonzalez

Early Education Coalition

Dolores Sobalvarro

AARP

Celia Ayala (Alternate)

Early Education Coalition

Chad Boggio (Alternate)

L.A. Co. Federation of Labor AFL-CIO

Peggy Robertson (Alternate)

Assoc. General Contractors of CA

Connie Yee (Alternate)

L.A. Co. Auditor-Controller's Office

Joseph P. Buchman – Legal Counsel

Burke, Williams & Sorensen, LLP

Lori Raineri and Keith Weaver – Oversight**Consultants**

Government Financial Strategies Joint

Powers Authority

Timothy Popejoy

Bond Oversight Administrator

Perla Zitle

Bond Oversight Coordinator

RESOLUTION 2023-06**BOARD REPORT NO. 208-22/23****RECOMMENDING BOARD APPROVAL TO DEFINE AND APPROVE THE PIO PICO MIDDLE SCHOOL ROOFING PROJECT AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN**

WHEREAS, District Staff proposes the Board of Education define and approve the Pio Pico Middle School Roofing Project with a budget of \$1,697,449 (Project), as described in Board Report 208-22/23 attached hereto, and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein, and authorize the Chief Procurement Officer and/or the Chief Facilities Executive, and/or their designee(s), to execute all instruments necessary to implement the Project; and

WHEREAS, Projects developed under the School Upgrade Program category of need, Critical Replacements and Upgrades of School Building/Site Systems and Components, will replace failing building systems that create safety concerns and are disruptive to school operations; and

WHEREAS, This project is to provide approximately 68,495 square feet of new roofing campus wide including the installation of new gutters, downspouts, and painting of affected areas; and

WHEREAS, Construction is anticipated to begin in the third quarter of 2023 and be completed in the first quarter of 2024; and

WHEREAS, The Project is consistent with the Los Angeles Unified School District's (Los Angeles Unified or District) long-term goal to address unmet school facilities needs and significantly improve the conditions of aging and deteriorating school facilities as described in Los Angeles Unified local bond measures; and



Board of Education Report

File #: Rep-009-22/23, **Version:** 1

Define and Approve 127 Projects to Provide Critical Replacements and Upgrades of School Building/Site Systems and Components and Amend the Facilities Services Division Strategic Execution Plan to Incorporate Therein

August 30, 2022

Facilities Services Division

Action Proposed:

Define and approve 127 projects to provide critical replacements and upgrades of school building/site systems and components, as listed on Attachments A and B, and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein. The total combined budget for the 127 projects is \$73,069,993.

Authorize the Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the proposed projects, including budget modifications and the purchase of equipment and materials.

Background:

Priorities for the expenditure of capital funding are evaluated to ensure the District's most pressing priorities are being addressed. More than 70 percent of Los Angeles Unified School District (Los Angeles Unified or District) school buildings were built more than 50 years ago, and more than \$50 billion of unfunded school facilities needs have been identified Districtwide, and these needs grow every year. As the District's capital needs far exceed available funding, the most pressing unfunded critical needs will continue to be addressed based on an evaluation of known facilities conditions and needs at schools. Projects developed under this category of need, Critical Replacements and Upgrades of School Building/Site Systems and Components, will replace failing building systems that create safety concerns and are disruptive to school operations. Systems in the worst condition, especially those that pose a safety hazard and/or will negatively impact school operations and other building systems if not addressed, will be addressed first.

The project proposals contained in this Board Report align with these priorities. Attachment A includes seven projects to replace failing building systems that create safety concerns and are disruptive to school operations. Attachment B includes 120 projects to provide new secure entry systems.

Expected Outcomes:

Staff anticipates that the Board of Education will define and approve 127 projects that address critical replacement and upgrade needs and amend the Facilities SEP to incorporate therein. Approval will authorize staff to proceed with the implementation of the proposed projects to improve student health, safety and educational quality.

Board Options and Consequences:

Adoption of the proposed action will authorize staff to proceed with the expenditure of Bond Program funds to undertake the project proposals in accordance with the provisions set forth in Los Angeles Unified local bond

measures K, R, Y, Q, and RR. If the proposed action is not approved, Bond Program funds will not be expended, and critical replacement and upgrade needs will remain unaddressed.

Policy Implications:

The proposal is consistent with the Los Angeles Unified's long-term goal to address unmet school facilities needs and significantly improve the conditions of aging and deteriorating school facilities as described in Los Angeles Unified local bond measures. Moreover, the proposed secure entrance projects support the *Protecting Our Students and School Sites* Board Resolution (Res-032-17/18).

Budget Impact:

The total combined budget for the 127 projects is \$73,069,993. The projects will be funded with Bond Program funds earmarked specifically for critical replacements and upgrades of school building/site systems and components.

Each project budget was prepared based on the current information known and assumptions about the project scope, site conditions, and market conditions. Individual project budgets will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise and will be adjusted accordingly to enable the successful completion of each project.

Student Impact:

Approval of the proposed projects enables the District to continue our ongoing efforts to undertake facilities improvements that help ensure students are provided with safe school environments that promote teaching and learning.

Equity Impact:

See Attached.

Issues and Analysis:

It may be necessary to undertake feasibility studies, site analysis, scoping, and/or due diligence activities on the proposed projects prior to initiating design. As necessary, the Office of Environmental Health and Safety (OEHS) will evaluate the proposed projects in accordance with the California Environmental Quality Act (CEQA) to ensure compliance. If through the planning and design process it is determined that the proposed project scope(s) will not sufficiently address the critical needs identified, the project scope, schedule and budget will be revised accordingly.

Bond Oversight Committee Recommendations:

This item was considered by the School Construction Bond Citizen's Oversight Committee (BOC) at its meeting on August 11, 2022. Staff has concluded that this proposed Facilities SEP amendment is in alignment with BOC recommendations and will facilitate Los Angeles Unified's ability to successfully implement the Facilities SEP.

Attachments:

Attachment A - Projects to Replace Failing Building Systems that Create Safety Concerns and are Disruptive to School Operations

Attachment B - Projects to Provide New Secure Entry Systems

Attachment C - BOC Resolution


File #: Rep-009-22/23, **Version:** 1

Informatives:
Not Applicable

Submitted:
8/8/2022 rev

File #: Rep-009-22/23, Version: 1

RESPECTFULLY SUBMITTED,


ALBERTO M. CARVALHO
Superintendent

APPROVED BY:


MEGAN K. REILLY
Deputy Superintendent

REVIEWED BY:


DEVORA NAVERA REED
General Counsel

☒ Approved as to form.

APPROVED BY:


MARK HOVATTER
Chief Facilities Executive
Facilities Services Division

REVIEWED BY:


TONY ATIENZA
Director, Budget Services and Financial Planning

☒ Approved as to budget impact statement.

PRESENTED BY:


INDIA R. GRIFFIN
Director of Maintenance and Operations
Facilities Services Division



LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report
Attachment A

Projects to Replace Failing Building Systems that Create Safety Concerns and are Disruptive to School Operations

- 1. Chatsworth Charter High School – Project to Provide New Heating, Ventilation, and Air Conditioning Systems**
 - *Local District Northwest, Board District 3 – Schmerelson*
 - *Project Background and Scope* – This project is to provide new heating, ventilation, and air conditioning (HVAC) systems campus-wide.
Project Budget -- \$52,527,074
 - *Project Schedule* – Construction is anticipated to begin in Q1 2025 and conclude in Q2 2028.
- 2. Cowan Avenue Elementary School – Project to Provide Slope Remediation and Asphalt Paving**
 - *Local District West, Board District 4 – Melvoin*
 - *Project Background and Scope* – This project is to provide new drainage, foundation, and perimeter fencing, rails and poles to prevent further slope erosion along the northwest of the main playground. In addition, the project will replace approximately 18,900 square feet of asphalt pavement on the playground, regrade for proper drainage, repair cracks, spalling, and local settlement at the pavement.
 - *Project Budget* -- \$2,957,057
 - *Project Schedule* – Construction is anticipated to begin in Q3 2024 and conclude in Q3 2025.
- 3. Robert F. Kennedy Community Schools – Project to Replace Synthetic Turf Fields**
 - *Local District Central, Board District 5 – Goldberg*
 - *Project Background and Scope* – This project is to replace approximately 72,000 square feet of synthetic turf on the soccer field, approximately 50,000 square feet of synthetic turf on the multi-purpose playfield, and replace the track around the multi-purpose playfield.
 - *Project Budget* -- \$7,632,721
 - *Project Schedule* – Construction is anticipated to begin in Q2 2024 and conclude in Q4 2025.
- 4. Clover Avenue Elementary School – Project to Provide New Roofing**
 - *Local District West, Board District 1 – McKenna*
 - *Project Background and Scope* – This project is to provide approximately 52,250 square feet of new roofing at 20 buildings, including the installation of new gutters and downspouts, and painting of affected areas.
 - *Project Budget* -- \$1,127,881
 - *Project Schedule* – Construction is anticipated to begin in Q3 2023 and conclude in Q2 2024.
- 5. Odyssey Continuation High School – Project to Provide New Roofing**
 - *Local District East, Board District 5 – Goldberg*
 - *Project Background and Scope* – This project is to provide approximately 13,200 square feet of new roofing at one building, including the installation of new gutters and downspouts, and painting of affected areas.
 - *Project Budget* -- \$328,824
 - *Project Schedule* – Construction is anticipated to begin in Q3 2023 and conclude in Q1 2024.



LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report
Attachment A

6. Walter Reed Middle School – Project to Provide New Roofing

- *Local District Northeast, Board District 3 – Schmerelson*
- *Project Background and Scope* – This project is to provide approximately 59,200 square feet of new roofing at 16 buildings, including the installation of new gutters and downspouts, skylights, and painting of affected areas.
- *Project Budget* -- \$1,340,124
- *Project Schedule* – Construction is anticipated to begin in Q3 2023 and conclude in Q2 2024.

7. William Howard Taft Charter High School – Project to Provide New Roofing

- *Local District Northwest, Board District 4 – Melvoin*
- *Project Background and Scope* – This project is to provide approximately 100,730 square feet of new roofing at seven buildings, including the installation of new gutters and downspouts, and painting of affected areas.
- *Project Budget* -- \$1,900,518
- *Project Schedule* – Construction is anticipated to begin in Q3 2023 and conclude in Q2 2024.



LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report

Attachment B
Projects to Provide New Secure Entry Systems

#	BD	LD	Cost Center	School	Project Budget*	Anticipated Construction Start	Anticipated Construction Completion
1	1	South	1402001	Bakewell PC	\$31,930	Q3 2022	Q4 2022
2	1	West	1312301	Clover ES	\$45,000	Q3 2022	Q4 2022
3	1	West	1598601	Palms ES	\$45,000	Q3 2022	Q4 2022
4	1	West	1465801	YES Academy at Hyde Park ES	\$45,000	Q3 2022	Q4 2022
5	2	Central	1708201	10th St. ES	\$45,000	Q3 2022	Q4 2022
6	2	Central	1550501	9th St. ES	\$45,000	Q3 2022	Q4 2022
7	2	Central	1238601	Del Olmo ES	\$45,000	Q3 2022	Q4 2022
8	2	Central	1864301	Franklin HS	\$45,000	Q3 2022	Q4 2022
9	2	Central	1238501	Gratts Learning Academy for Young Scholars	\$45,000	Q3 2022	Q4 2023
10	2	Central	1324701	Plasencia ES	\$45,000	Q3 2022	Q4 2023
11	2	East	1453401	Hillside ES	\$45,000	Q3 2022	Q4 2023
12	2	East	1737001	Utah Span School	\$45,000	Q3 2022	Q4 2023
13	3	Northeast	1740101	Cardenas ES	\$45,000	Q3 2022	Q4 2023
14	3	Northeast	1282201	Carpenter Community Charter ES	\$45,000	Q3 2022	Q4 2023
15	3	Northeast	1295901	Chandler Learning Academy	\$45,000	Q3 2022	Q4 2023
16	3	Northeast	1316401	Colfax Charter ES	\$45,000	Q3 2022	Q4 2023
17	3	Northeast	1472601	Kester ES	\$45,000	Q3 2022	Q4 2023
18	3	Northeast	1669901	Sherman Oaks Charter ES	\$45,000	Q3 2022	Q4 2023
19	3	Northwest	1211701	Andasol ES	\$45,000	Q3 2022	Q4 2023
20	3	Northwest	1226901	Balboa Gifted/High Ability Magnet ES	\$45,000	Q3 2022	Q4 2023
21	3	Northwest	1232301	Bassett ES	\$45,000	Q3 2022	Q4 2023
22	3	Northwest	1275301	Canoga Park ES	\$45,000	Q3 2022	Q4 2023
23	3	Northwest	1276701	Cantara ES	\$45,000	Q3 2022	Q4 2023
24	3	Northwest	1313701	Cohasset ES	\$45,000	Q3 2022	Q4 2023
25	3	Northwest	1334001	Darby ES	\$45,000	Q3 2022	Q4 2023

*Projects budgets of \$45,000 are based on the average cost for similar completed projects. Site-specific detailed scopes have not been fully developed yet. Obtaining project approvals now will allow for immediate purchase of long lead-time items and will accelerate the completion of all secure entrance projects.



LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report

Attachment B
Projects to Provide New Secure Entry Systems

#	BD	LD	Cost Center	School	Project Budget*	Anticipated Construction Start	Anticipated Construction Completion
26	3	Northwest	1354501	El Oro Way Charter for Enriched Studies	\$41,692	Q3 2022	Q4 2023
27	3	Northwest	1361001	Enadia Way Technology Charter	\$45,000	Q3 2022	Q4 2023
28	3	Northwest	1411001	Gault ES	\$45,000	Q3 2022	Q4 2023
29	3	Northwest	1423301	Granada ES	\$45,000	Q3 2022	Q4 2023
30	3	Northwest	1445201	Haskell STEAM Magnet ES	\$45,000	Q3 2022	Q4 2023
31	3	Northwest	1447301	Haynes Charter for Enriched Studies	\$45,000	Q3 2022	Q4 2023
32	3	Northwest	1476201	Knollwood Preparatory Academy ES	\$45,000	Q3 2022	Q4 2023
33	3	Northwest	1953001	Lemay EEC	\$45,000	Q3 2022	Q4 2023
34	3	Northwest	1191001	Miller Career & Transition Center	\$45,000	Q3 2022	Q4 2023
35	3	Northwest	1545901	Nevada ES	\$45,000	Q3 2022	Q4 2023
36	3	Northwest	1230301	Porter Ranch Community School	\$45,000	Q3 2022	Q4 2023
37	3	Northwest	1689001	Stagg ES	\$45,000	Q3 2022	Q4 2023
38	3	Northwest	1698601	Sunny Brae ES	\$45,000	Q3 2022	Q4 2023
39	3	Northwest	1700701	Superior Charter ES	\$45,000	Q3 2022	Q4 2023
40	3	Northwest	1742201	Van Gogh Charter ES	\$45,000	Q3 2022	Q4 2023
41	3	Northwest	1783601	Winnetka ES	\$45,000	Q3 2022	Q4 2023
42	4	Northwest	1243801	Bertrand ES	\$45,000	Q3 2022	Q4 2023
43	4	Northwest	1361601	Encino Charter ES	\$45,000	Q3 2022	Q4 2023
44	4	Northwest	1402701	Fullbright ES	\$39,056	Q3 2022	Q4 2023
45	4	Northwest	1405501	Garden Grove ES	\$45,000	Q3 2022	Q4 2023
46	4	Northwest	1452101	Hesby Oaks Leadership Charter	\$45,000	Q3 2022	Q4 2023
47	4	Northwest	1190801	Leichman Career Preparatory & Transition Center	\$45,000	Q3 2022	Q4 2023
48	4	Northwest	1194701	Lokrantz Special Education Center	\$45,000	Q3 2022	Q4 2023

*Projects budgets of \$45,000 are based on the average cost for similar completed projects. Site-specific detailed scopes have not been fully developed yet. Obtaining project approvals now will allow for immediate purchase of long lead-time items and will accelerate the completion of all secure entrance projects.



LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report

Attachment B
Projects to Provide New Secure Entry Systems

#	BD	LD	Cost Center	School	Project Budget*	Anticipated Construction Start	Anticipated Construction Completion
49	4	Northwest	1740201	Mosk ES	\$45,000	Q3 2022	Q4 2023
50	4	Northwest	1547901	Newcastle ES	\$38,915	Q3 2022	Q4 2023
51	4	Northwest	1884201	Sherman Oaks Center for Enriched Studies	\$45,000	Q3 2022	Q4 2023
52	4	Northwest	1704101	Tarzana ES	\$45,000	Q3 2022	Q4 2023
53	4	Northwest	1789001	Woodland Hills Charter ES	\$32,181	Q3 2022	Q4 2023
54	4	West	1274101	Community Magnet Charter ES	\$45,000	Q3 2022	Q4 2023
55	4	West	1326001	Cowan ES	\$45,000	Q3 2022	Q4 2023
56	4	West	1469901	Kenter Canyon Charter ES	\$45,000	Q3 2022	Q4 2023
57	4	West	1588901	Open Magnet Charter ES	\$45,000	Q3 2022	Q4 2023
58	5	Central	1727401	20th St. ES	\$40,148	Q3 2022	Q4 2023
59	5	Central	1236901	RFK Community Schools - Ambassador School - Global Education	\$45,000	Q3 2022	Q4 2023
60	5	Central	1778301	RFK Community Schools - New Open World Academy	\$45,000	Q3 2022	Q4 2023
61	5	Central	1778001	RFK Community Schools - UCLA Community School	\$45,000	Q3 2022	Q4 2023
62	5	Central	1195501	Salvin Special Education	\$45,000	Q3 2022	Q4 2023
63	5	Central	1857701	Sotomayor Learning Academies	\$45,000	Q3 2022	Q4 2023
64	5	East	1321001	Madison ES	\$45,000	Q3 2022	Q4 2023
65	5	East	1464001	Walnut Park ES	\$32,212	Q3 2022	Q4 2023
66	5	East	1230901	Willow ES	\$32,709	Q3 2022	Q4 2023
67	6	Northeast	1216401	Apperson ES	\$45,000	Q3 2022	Q4 2023
68	6	Northeast	1220501	Arminta ES	\$45,000	Q3 2022	Q4 2023
69	6	Northeast	1232901	Beachy ES	\$45,000	Q3 2022	Q4 2023
70	6	Northeast	1248601	Brainard ES	\$45,000	Q3 2022	Q4 2023
71	6	Northeast	1382901	Broadous ES	\$45,000	Q3 2022	Q4 2023
72	6	Northeast	1265801	Burton ES	\$45,000	Q3 2022	Q4 2023

*Projects budgets of \$45,000 are based on the average cost for similar completed projects. Site-specific detailed scopes have not been fully developed yet. Obtaining project approvals now will allow for immediate purchase of long lead-time items and will accelerate the completion of all secure entrance projects.



LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report

Attachment B
Projects to Provide New Secure Entry Systems

#	BD	LD	Cost Center	School	Project Budget*	Anticipated Construction Start	Anticipated Construction Completion
73	6	Northeast	1278101	Canterbury ES	\$45,000	Q3 2022	Q4 2023
74	6	Northeast	1501601	Coughlin ES	\$45,000	Q3 2022	Q4 2023
75	6	Northeast	1349301	Dyer ES	\$45,000	Q3 2022	Q4 2023
76	6	Northeast	1354101	El Dorado ES	\$45,000	Q3 2022	Q4 2023
77	6	Northeast	1814201	Fulton College Preparatory School	\$45,000	Q3 2022	Q4 2023
78	6	Northeast	1419201	Glenwood ES	\$45,000	Q3 2022	Q4 2023
79	6	Northeast	1443101	Harding ES	\$45,000	Q3 2022	Q4 2023
80	6	Northeast	1451501	Herrick ES	\$45,000	Q3 2022	Q4 2023
81	6	Northeast	1739901	Korenstein ES	\$45,000	Q3 2022	Q4 2023
82	6	Northeast	1534201	Monlux ES	\$45,000	Q3 2022	Q4 2023
83	6	Northeast	1539701	Morningside ES	\$45,000	Q3 2022	Q4 2023
84	6	Northeast	1540401	Mountain View ES	\$45,000	Q3 2022	Q4 2023
85	6	Northeast	1589401	Osceola ES	\$45,000	Q3 2022	Q4 2023
86	6	Northeast	1619201	Ranchito ES	\$45,000	Q3 2022	Q4 2023
87	6	Northeast	1645201	San Fernando ES	\$45,000	Q3 2022	Q4 2023
88	6	Northeast	1357401	Sendak ES	\$45,000	Q3 2022	Q4 2023
89	6	Northeast	1666501	Sharp ES	\$45,000	Q3 2022	Q4 2023
90	6	Northeast	1697301	Sunland ES	\$45,000	Q3 2022	Q4 2023
91	6	Northeast	1701401	Sylmar ES	\$45,000	Q3 2022	Q4 2023
92	6	Northeast	1740801	Sylmar Leadership Academy	\$45,000	Q3 2022	Q4 2023
93	6	Northeast	1738401	Valerio ES	\$45,000	Q3 2022	Q4 2023
94	6	Northeast	1789501	Valley Oaks Center for Enriched Studies	\$45,000	Q3 2022	Q4 2023
95	6	Northeast	1746601	Vena ES	\$45,000	Q3 2022	Q4 2023
96	6	Northeast	1754801	Vinedale ES	\$45,000	Q3 2022	Q4 2023
97	6	Northeast	1740001	Vista del Valle Dual Language Academy	\$45,000	Q3 2022	Q4 2023
98	6	Northwest	1739801	Alta California ES	\$45,000	Q3 2022	Q4 2023
99	6	Northwest	1413001	Gledhill ES	\$45,000	Q3 2022	Q4 2023
100	6	Northwest	1479001	Lassen ES	\$45,000	Q3 2022	Q4 2023
101	6	Northwest	1487001	Liggett ES	\$45,000	Q3 2022	Q4 2023

*Projects budgets of \$45,000 are based on the average cost for similar completed projects. Site-specific detailed scopes have not been fully developed yet. Obtaining project approvals now will allow for immediate purchase of long lead-time items and will accelerate the completion of all secure entrance projects.



**LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report**

**Attachment B
*Projects to Provide New Secure Entry Systems***

#	BD	LD	Cost Center	School	Project Budget*	Anticipated Construction Start	Anticipated Construction Completion
102	6	Northwest	1560401	Panorama City ES	\$45,000	Q3 2022	Q4 2023
103	6	Northwest	1357601	Parks Learning Center	\$45,000	Q3 2022	Q4 2023
104	6	Northwest	1612301	Plummer ES	\$45,000	Q3 2022	Q4 2023
105	6	Northwest	1647901	San Jose ES	\$45,000	Q3 2022	Q4 2023
106	7	South	1587701	135th St. ES	\$32,824	Q3 2022	Q4 2023
107	7	South	1582201	153rd St. ES	\$45,000	Q3 2022	Q4 2023
108	7	South	1575301	186th St. ES	\$45,000	Q3 2022	Q4 2023
109	7	South	1732901	232nd Pl. ES	\$45,000	Q3 2022	Q4 2023
110	7	South	1194101	Banneker Career & Transition Center	\$33,770	Q3 2022	Q4 2023
111	7	South	1281501	Caroldale Learning Community	\$45,000	Q3 2022	Q4 2023
112	7	South	1345201	Dolores ES	\$45,000	Q3 2022	Q4 2023
113	7	South	1346601	Dominguez ES	\$45,000	Q3 2022	Q4 2023
114	7	South	1404101	Gardena ES	\$32,321	Q3 2022	Q4 2023
115	7	South	1434201	Halldale ES	\$36,075	Q3 2022	Q4 2023
116	7	South	1442501	Harbor City ES	\$45,000	Q3 2022	Q4 2023
117	7	South	1482901	Leapwood ES	\$45,000	Q3 2022	Q4 2023
118	7	South	1734201	Meyler ES	\$31,489	Q3 2022	Q4 2023
119	7	South	1703501	Taper ES	\$30,472	Q3 2022	Q4 2023
120	7	South	1741901	Van Deene ES	\$45,000	Q3 2022	Q4 2023
Total					\$5,255,794		

*Projects budgets of \$45,000 are based on the average cost for similar completed projects. Site-specific detailed scopes have not been fully developed yet. Obtaining project approvals now will allow for immediate purchase of long lead-time items and will accelerate the completion of all secure entrance projects.

LOS ANGELES UNIFIED SCHOOL DISTRICT**SCHOOL CONSTRUCTION BOND CITIZENS' OVERSIGHT COMMITTEE****Margaret Fuentes, Chair**

LAUSD Student Parent

D. Michael Hamner, Vice-Chair

American Institute of Architects

Jennifer McDowell, Secretary

L.A. City Mayor's Office

Susan Linschoten, Executive Committee

L.A. Co. Auditor-Controller's Office

Scott Pansky, Executive Committee

L.A. Area Chamber of Commerce

Jeffrey Fischbach

CA Tax Reform Assn.

Chris Hannan

L.A. Co. Federation of Labor AFL-CIO

Hyepin Im

L.A. City Controller's Office

Samantha Rowles

LAUSD Student Parent

Araceli Sandoval-Gonzalez

Early Education Coalition

Dolores Sobalvarro

AARP

Celia Ayala (Alternate)

Early Education Coalition

Chad Boggio (Alternate)

L.A. Co. Federation of Labor AFL-CIO

Connie Yee (Alternate)

L.A. Co. Auditor-Controller's Office

Vacant31st District PTSA**Vacant**

Assoc. General Contractors of CA

Vacant

CA Charter School Association

Vacant

Tenth District PTSA

Joseph P. Buchman – Legal Counsel

Burke, Williams & Sorensen, LLP

Lori Raineri and Keith Weaver – Oversight Consultants

Government Financial Strategies

Timothy Popejoy

Bond Oversight Administrator

Perla Zitle

Bond Oversight Coordinator

RESOLUTION 2022-33**BOARD REPORT NO. 009-22/23****RECOMMENDING BOARD APPROVAL TO DEFINE AND APPROVE 127 PROJECTS TO PROVIDE CRITICAL REPLACEMENTS AND UPGRADES OF SCHOOL BUILDING/SITE SYSTEMS AND COMPONENTS AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN**

WHEREAS, District Staff proposes that the Board of Education define and approve 127 projects that address critical replacement and upgrade needs at schools with a budget of \$73,069,993 (the "Projects") as described in Board Report 009-22/23 attached hereto, and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein, and authorize the Chief Procurement Officer and/or the Chief Facilities Executive, and/or their designee(s), to execute all instruments necessary to implement the Projects; and

WHEREAS, Projects developed under the School Upgrade Program category of need, Critical Replacements and Upgrades of School Building/Site Systems and Components, will replace failing building systems that create safety concerns and are disruptive to school operations; and

WHEREAS, The Projects are consistent with the Los Angeles Unified School District (Los Angeles Unified or District)'s long-term goal to address unmet school facilities needs and significantly improve the conditions of aging and deteriorating school facilities as described in Los Angeles Unified local bond measures; and

WHEREAS, District Staff has determined that the Projects are necessary to improve student health, safety and educational quality; and

Bond Oversight Committee333 S. Beaudry Avenue, 23rd Floor, Los Angeles, CA 90017 ♦ Phone: 213. 241.5183 ♦ www.laschools.org/bond

RESOLUTION 2022-33**RECOMMENDING BOARD APPROVAL TO DEFINE AND APPROVE 127 PROJECTS TO PROVIDE CRITICAL REPLACEMENTS AND UPGRADES OF SCHOOL BUILDING/SITE SYSTEMS AND COMPONENTS AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN**

WHEREAS, the Board of Education's approval of the Projects will authorize District Staff to proceed with the expenditure of bond funds to undertake the Projects in accordance with the provisions set forth in Los Angeles Unified local bond measures K, R, Y, Q, and RR; and

WHEREAS, District Staff has concluded that this proposed Facilities SEP amendment will facilitate Los Angeles Unified's ability to successfully complete the Facilities SEP.

NOW, THEREFORE, BE IT RESOLVED THAT:

1. The School Construction Citizens' Bond Oversight Committee recommends that the Board of Education define and approve 127 projects that address critical replacement and upgrade needs at schools, with a combined budget of \$73,069,993, and amend the Facilities SEP to incorporate therein, as described in Board Report 009-22/23, a copy of which is attached hereto in the form it was presented to the BOC and is incorporated herein by reference.
2. This resolution shall be transmitted to the Los Angeles Unified School District Board of Education and posted on the Oversight Committee's website.
3. The District is directed to track the above recommendation and to report on the adoption, rejection, or pending status of the recommendations as provided in section 6.2 of the Charter and Memorandum of Understanding between the Oversight Committee and the District.

ADOPTED on August 11, 2022, by the following vote:

AYES: 8

ABSTENTIONS: 0

NAYS: 0

ABSENCES: 3

/Margaret Fuentes/

Margaret Fuentes
Chair

/Michael Hamner/

D. Michael Hamner
Vice-Chair



Board of Education Report

File #: Rep-086-17/18, **Version:** 1

Amendment to the Facilities Services Division Strategic Execution Plan to Approve Six Project Definition Proposals that Address Critical School Safety and Repair Needs

November 14, 2017

Facilities Services Division

Action Proposed:

Staff proposes that the Board of Education (Board) amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to approve six Project Definition proposals that address critical school safety and repair needs, as described in Attachment A, for a combined total of \$13,866,044:

- Four Project Definition proposals included in this action request authorization and funding to execute all project related activities (pre-construction and construction activities). The total combined budget for these four projects is \$12,205,765; and
- Two Project Definition proposals request authorization to execute only pre-construction activities. The total combined budget for these two projects (pre-construction only) is \$1,660,279.

Background:

The District encompasses approximately 1,300 different schools and centers, and Facilities is responsible for maintaining, repairing, and upgrading more than 13,500 school buildings, the majority of which are over 50 years old. Despite the significant investments the District has made in its school facilities over the last two decades, schools continue to age and deteriorate and older buildings may not align with instructional requirements. As the District's capital needs far exceed available funding, priorities for the expenditure of capital funding must be evaluated to ensure the District's most pressing priorities are being addressed.

On October 10, 2017, the Board approved the Facilities Bond Program strategy to address unfunded and pressing school facilities needs related to safety, compliance, and instructional requirements through 2018 (Board Report No. 048-17/18). Staff has determined that the project proposals included in this Board Report will help facilitate the implementation of the strategy. This strategy included bringing project proposals for pre-construction activities only in situations where the project requires a significant period of design. Typically pre-construction activities represent ten to fifteen percent of the total project cost. The amount of funding that remains targeted for critical school repair and safety projects is limited, a significant amount of unfunded needs exist, and design activities typically occur over a two year period. Given these realities, the approach for proposing projects for only pre-construction activities will allow more projects to be ready for construction when future funding becomes available.

Once the Division of the State Architect (DSA) approval is obtained, the District has one year to begin construction activities and may request renewal of the approval for up to three additional years. Staff has a high degree of confidence that over the course of the next six years (the time period for design and duration of DSA approval), additional sources of funds will be identified to support construction activities. Future sources of funds may include funds associated with the continued close-out of legacy projects and State matching funds.

Expected Outcomes:

Staff anticipates that the Board of Education will approve the Project Definition proposals, as described in Attachment A, to address critical school safety and repair needs that will improve student health, safety and educational quality.

Board Options and Consequences:

A “yes” vote will authorize staff to proceed with the expenditure of bond funds to undertake the project proposals in accordance with the provisions set forth in Measures K, R, Y and Q. If the proposed action is not approved, bond funds will not be expended and critical school repair and safety needs will remain unaddressed.

Policy Implications:

These actions are consistent with the District’s commitment to address unmet school facilities needs and provide students with a safe and healthy learning environment.

Budget Impact:

The total combined budget for the six Project Definition proposals is \$13,866,044 of which \$12,205,765 will support pre-construction and construction activities for four projects, and \$1,660,279 will support pre-construction only for two projects, as described in Attachment A. The six projects will be funded with Bond program funds earmarked specifically for critical school repair and safety improvements.

Student Impact:

These project proposals address critical school repair and safety improvement needs that must be undertaken to provide students with a safe and healthy learning environment, and up-to-date facilities that promote teaching and learning.

Issues and Analysis:

Traditionally, projects are initially presented to the Bond Citizens’ Oversight Committee (BOC) and the Board to authorize funding for both pre-construction and construction activities. However, before a project can proceed into construction, the design, plans, and specifications must be completed and approved by DSA, and California Environmental Quality Act (CEQA) review must be complete, and as applicable, certified by the Board. At least two years are needed to complete these activities and obtain DSA approval. (Once DSA approval is obtained, the District has one year to begin construction activities and may request renewal of the approval for up to three additional years.)

An alternative project approval approach is to request initial funding for pre-construction activities only. Pre-construction activities include: due diligence, planning, and design activities, and may include environmental analysis in accordance with CEQA regulations. This approach allows more pressing needs to be addressed through design and DSA approval and allocates significantly less funding today. Given that a significant amount of unfunded needs exist and the amount of funding that remains available to address critical school repair and safety needs is limited, and moreover that design typically occurs over a period of two years, staff has determined that using this alternative approach for some project proposals would allow more of these needs to be addressed sooner because more projects would be ready to start construction when funding becomes available in the future. Future sources of funds may include funds associated with the continued close-out of legacy projects and State matching funds.

File #: Rep-086-17/18, **Version:** 1

This action includes two project proposals - Franklin High School and Palisades Charter High School - that require a significant period of design and as such are being proposed for funding for pre-construction activities only. Staff will return to the BOC and the Board at a later date for authorization and funding for construction related activities.

The Office of Environmental Health and Safety (OEHS) will evaluate the project proposals in accordance with the California Environmental Quality Act (CEQA) to ensure compliance. If through the planning and design process it is determined that the proposed project scope(s) will not sufficiently address the critical need identified, the project scope, schedule and budget will be revised accordingly.

Bond Oversight Committee Recommendations:

This item was considered by the BOC at its meeting on November 2, 2017. Staff has concluded that this proposed FSD SEP amendment will facilitate implementation of the FSD SEP, and therefore, it will not adversely affect the District's ability to successfully complete the FSD SEP.

Attachments:

Attachment A - Six Project Definition Proposals that Address Critical School Safety and Repair Needs
BOC Resolution

Informatives:


None.

Submitted:

10/27/17

File #: Rep-086-17/18, Version: 1

RESPECTFULLY SUBMITTED,


MICHELLE KING, Ed.D.
Superintendent

APPROVED BY:


MARK HOVATTER
Chief Facilities Executive
Facilities Services Division

REVIEWED BY:


DAVID HOLMQUIST
General Counsel

PRESENTED BY:

 by direction
10/27/2017
ROGER FINSTAD
Director of Maintenance of Operations
Facilities Services Division

 Approved as to form.

REVIEWED BY:


CHERYL SIMPSON
Director, Budget Services and Financial Planning

 Approved as to budget impact statement.



**LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report**

Attachment A

PRE-CONSTRUCTION & CONSTRUCTION

1. Belmont High School – Project to Provide New Roofing Campus-Wide

- *Local District Central, Board District 2 – García*
- *Project Background and Scope* – This project is to provide approximately 145,058 square feet of new roofing campus-wide, including new Heating, Ventilation and Air Conditioning units and equipment, gutters and downspouts. (Includes 11 buildings, eight of which to be upgraded with new HVAC.)
- *Project Budget* -- \$7,435,281
- *Project Schedule* – Construction is anticipated to begin in Q2 2018 and conclude in Q1 2019.

2. Euclid Elementary School – Project to Provide Fire Damage Repairs

- *Local District East, Board District 2 – García*
- *Project Background and Scope* – This project is to provide fire damage repairs at the Euclid Elementary School kitchen. Major repairs consist of the removal and replacement of walls, framing, doors, ceiling, exhaust fan, plumbing fixtures, water heater, flooring, Heating, Ventilation and Air Conditioning ductwork, electrical systems, low voltage systems, fire alarm, interior casework, and kitchen appliances.
- *Project Budget* -- \$792,507
- *Project Schedule* – Construction began in Q3 2017 and is expected to conclude in Q1 2018.

Repairs began in July 2017 using Routine Repair and General Maintenance Funds, which will be reimbursed using Bond funds. Any insurance claim proceeds received by the District will be applied to this project in lieu of bond funds.

3. Santee Education Complex – Project to Replace Failed Chiller

- *Local District Central, Board District 2 – García*
- *Project Background and Scope* – This project is to replace a failed 300-ton chiller. Currently, a rental unit is being used as a temporary replacement for the failed chiller.
- *Project Budget* -- \$266,163
- *Project Schedule* – Construction is anticipated to begin in Q1 2018 and conclude in Q2 2018.

4. Westchester High School – Project to Provide New Roofing Campus-Wide

- *Local District West, Board District 4– Melvoin*
- *Project Background and Scope* – This project is to provide approximately 326,417 square feet of new roofing campus-wide, including new gutters and downspouts. (Includes 18 buildings.)
- *Project Budget* -- \$3,711,814
- *Project Schedule* – Construction is anticipated to begin in Q2 2018 and conclude in Q1 2019.



**LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report**

Attachment A

PRE-CONSTRUCTION ONLY

5. Franklin High School – Pre-Construction Activities for Project to Provide Seismic Retrofits at Auditorium Building

- *Local District Central, Board District 5 – Rodriguez*
- *Project Background and Scope* – This proposal is for pre-construction activities associated with seismic retrofits at the Auditorium Building which encompasses a total area of approximately 40,200 square feet. The project includes providing ADA upgrades as required.
- *Project Budget* -- \$761,244
- *Project Schedule* – Pre-construction activities are anticipated to begin in Q1 2018 and conclude in Q1 2019.

Staff anticipates the total budget for this project (including pre-construction and construction activities) to be \$5.7M. We expect this would be updated prior to future Board approval of construction activities based on a completed design.

6. Palisades Charter High School – Pre-Construction Activities for Project to Provide New Underground Hot Water Pipes

- *Local District West, Board District 4 – Melvoin*
- *Project Background and Scope* – This proposal is for pre-construction activities associated with the replacement of the deteriorated underground hot water pipes serving the entire campus. The pipes were originally installed in the 1960s and recently failed resulting in flooding throughout the campus. Temporary repairs were provided until a long-term solution is planned to address the deteriorated water pipes. The project includes providing new hot water boilers at eight classroom buildings.
- *Project Budget* -- \$899,035
- *Project Schedule* – Pre-construction activities are anticipated to begin in Q2 2018 and conclude in Q2 2019.

Staff anticipates the total budget for this project (including pre-construction and construction activities) to be \$6.5M. We expect this would be updated prior to future Board approval of construction activities based on a completed design.

SCHOOL CONSTRUCTION BOND CITIZENS' OVERSIGHT COMMITTEE

Quynh Nguyen, Chair
LAUSD Student Parent
Barry Waite, Vice Chair
CA Tax Reform Assn.
Susan Linschoten, Secretary
L.A. Co. Auditor-Controller's Office
Stuart Magruder, Executive Committee
American Institute of Architects
Rachel Greene, Executive Committee
Tenth District PTSA

Bevin Ashenmiller
LAUSD Student Parent
Araceli Sandoval-Gonzalez
Early Education Coalition
Greg Good
L.A. City Mayor's Office
Michael Keeley
CA Charter School Association
Karen Krygier
L.A. City Controller's Office
Kate Mergen
Assoc. General Contractors of CA

Ron Miller
L.A. Co. Federation of Labor AFL-CIO
Scott Pansky
L.A. Area Chamber of Commerce
Dolores Sobalvarro
AARP
Kathryn Steinberg
31st District PTSA
Celia Ayala (Alternate)
Early Education Coalition
Arlene Barrera (Alternate)
L.A. Co. Auditor-Controller's Office

Joseph P. Buchman – Legal Counsel
Burke, Williams & Sorensen, LLP
Thomas A. Rubin, CPA
Oversight Committee Consultant

Timothy Popejoy
Bond Oversight Administrator
Daniel Hwang
Asst. Administrative Analyst

RESOLUTION 2017-41**BOARD REPORT NO. 086-17/18**

**AMENDMENT TO THE FACILITIES SERVICES DIVISION STRATEGIC
EXECUTION PLAN TO APPROVE SIX PROJECT DEFINITION
PROPOSALS THAT ADDRESS CRITICAL SCHOOL SAFETY
AND REPAIR NEEDS**

WHEREAS, District Staff proposes that the Board of Education approve an amendment to the Facilities Services Division (FSD) Strategic Execution Plan (SEP) to approve six Project Definition proposals that address critical school safety and repair needs as described in Board Report 086-17/18 a copy of which is attached hereto in the form it was presented to the BOC and is incorporated herein by reference; and

WHEREAS, four Project Definition proposals are for pre-construction activities and construction activities for a combined budget of \$12,205,765; and two Project Definition proposals are for pre-construction activities only for a combined budget of \$1,660,279; and

WHEREAS, District Staff has determined that the project proposals will help facilitate the implementation of the Facilities Bond Program strategy to address unfunded and pressing school facilities related to safety, compliance, and instructional requirements through 2018 (Board Report No. 048-17/18); and

WHEREAS, the School Upgrade Program, the latest phase of the District's Bond Program, includes a spending target to address "Critical School Repair and Safety Improvements to School Building Components"; and

WHEREAS, District Staff has determined that the Project Definition proposals are necessary to improve student health, safety and educational quality; and

RESOLUTION 2017-41**AMENDMENT TO THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO APPROVE SIX PROJECT DEFINITION PROPOSALS THAT ADDRESS CRITICAL SCHOOL SAFETY AND REPAIR NEEDS****PAGE 2**

WHEREAS, the Board of Education's approval of the Project Definition proposals will authorize District Staff to proceed with the expenditure of bond funds to undertake the project proposals in accordance with the provisions set forth in Measures K, R, Y and Q; and

WHEREAS, the Project Definition proposals are consistent with the District's commitment to address unmet school facilities needs and provide students with a safe and healthy learning environment; and

WHEREAS, District Staff has concluded that the proposed SEP amendment will facilitate implementation of the FSD SEP, and therefore, it will not adversely affect the District's ability to successfully complete the FSD SEP.

NOW, THEREFORE, BE IT RESOLVED THAT:

1. The School Construction Citizens' Bond Oversight Committee recommends that the Board of Education adopt an amendment to the Facilities Services Division (FSD) Strategic Execution Plan (SEP) to approve Project Definition proposals that address critical school safety and repair needs, of which four proposals are for pre-construction and construction activities for a combined budget of \$12,205,765, and two proposals are for pre-construction activities only for a combined budget of \$1,660,279, as defined in Board Report 086-17/18, a copy of which is attached hereto in the form it was presented to the BOC and is incorporated herein by reference.
2. This resolution shall be transmitted to the Los Angeles Unified School District Board of Education and posted on the Oversight Committee's website.
3. The District is directed to track the above recommendation and to report on the adoption, rejection, or pending status of the recommendations as provided in section 6.2 of the Charter and Memorandum of Understanding between the Oversight Committee and the District.

ADOPTED on November 2, 2017, by the following vote:

AYES: 11

ABSTENTIONS: 0

NAYS:

ABSENCES: 4


Quynh Nguyen
Chair


Stuart Magruder
Executive Committee



Board of Education Report

File #: Rep-427-17/18, **Version:** 1

Amendment to the Facilities Services Division Strategic Execution Plan to Define and Approve Three Projects that Address Critical School Repair Needs

May 8, 2018

Facilities Services Division

Action Proposed:

Staff proposes that the Board of Education approve an amendment to the Facilities Services Division (FSD) Strategic Execution Plan (SEP) to define and approve three projects that address critical school repair needs, as listed on Attachment A. Staff further proposes that the Board authorize the (Interim) Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the proposed projects, including budget modifications and the purchase of equipment and materials. The total combined budget for the three projects is \$9,345,154.

Background:

The District encompasses approximately 1,300 different schools and centers, and Facilities is responsible for maintaining, repairing, and upgrading more than 13,500 school buildings, the majority of which are over 50 years old. Despite the significant investments the District has made in its school facilities over the last two decades, schools continue to age and deteriorate and older buildings may not align with instructional requirements. As the District's capital needs far exceed available funding, priorities for the expenditure of capital funding must be evaluated to ensure the District's most pressing priorities are being addressed.

Staff recently completed an evaluation of known school facilities conditions and needs to identify the most pressing unfunded critical school repair and safety needs that should continue to be addressed through the end of 2018 within the limited available funding. Failing air conditioning systems, deteriorated roofs, and school buildings/rooms damaged by fire incidents and/or deemed unsafe for occupancy were all identified as pressing critical school repair and safety needs. The project proposals contained in this Board Report align with the identified types of pressing critical school repair and safety conditions.

The proposed projects in this Board Report consist of providing new roofing campus-wide at Carson High School and University High School and new Heating, Ventilation and Air Conditioning systems at Sun Valley Magnet School. Attachment A provides additional details pertaining to the proposed projects.

Expected Outcomes:

Staff anticipates that the Board of Education will approve the proposed action to define and approve three projects to address critical school repair needs that will improve student health, safety and educational quality.

Board Options and Consequences:

A "yes" vote will authorize staff to proceed with the expenditure of bond funds to undertake the project proposals in accordance with the provisions set forth in Measures K, R, Y and Q. If the proposed action is not approved, bond funds will not be expended and critical school repair needs will remain unaddressed.

File #: Rep-427-17/18, **Version:** 1

Policy Implications:

The action is consistent with the District's commitment to address unmet school facilities needs and provide students with a safe and healthy learning environment. Moreover, the proposal is aligned with the Board-adopted Facilities Bond Program strategy to address unfunded and pressing school facilities needs related to safety, compliance, and instructional requirements through 2018 (Board Report No. 048-17/18).

Budget Impact:

The total combined budget for the three projects is \$9,345,154. The projects will be funded with Bond Program funds earmarked specifically for critical school repair and safety improvements to school building components.

Each project budget was prepared based on the current information known, and assumptions about, the project scope, site conditions, and market conditions. Individual project budgets will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise, and will be adjusted accordingly to enable the successful completion of each project.

Student Impact:

These proposed projects address critical school repair needs that must be undertaken to provide students with a safe and healthy learning environment and up-to-date facilities.

Issues and Analysis:

It may be necessary to undertake feasibility studies, site analysis, scoping, and/or due diligence activities on the proposed projects prior to initiating design. As necessary, the Office of Environmental Health and Safety (OEHS) will evaluate the proposed projects in accordance with the California Environmental Quality Act (CEQA) to ensure compliance. If through the planning and design process it is determined that the proposed project scope(s) will not sufficiently address the critical need identified, the project scope, schedule and budget will be revised accordingly.

Bond Oversight Committee Recommendations:

This item was considered by the BOC at its meeting on April 26, 2018. Staff has concluded that this proposed FSD SEP amendment will facilitate implementation of the FSD SEP, and therefore, it will not adversely affect the District's ability to successfully complete the FSD SEP.

Attachments:

Attachment A - Project Definitions for Three Projects that Address Critical School Repair Needs
BOC Resolution

Informatives:

None.

Submitted:

4/20/18

File #: Rep-427-17/18, Version: 1

RESPECTFULLY SUBMITTED,



VIVIAN EKCHIAN
Interim Superintendent

APPROVED BY:



MARK HOVATTER
Chief Facilities Executive
Facilities Services Division

REVIEWED BY:



DAVID HOLMQUIST
General Counsel


PRESENTED BY:



GREGORY GARCIA
Interim Director of Maintenance & Operations
Facilities Services Division

 Approved as to form.

REVIEWED BY:



CHERYL SIMPSON
Director, Budget Services and Financial Planning

 Approved as to budget impact statement.



**LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report**

223

Attachment A

1. Carson High School – Project to Provide New Roofing Campus-Wide and Selected Heating, Ventilation and Air Conditioning Units

- *Local District South, Board District 7– Vladovic*
- *Project Background and Scope* – This project is to provide approximately 155,000 square feet of new roofing at 32 buildings campus-wide, including new Heating, Ventilation and Air Conditioning units and equipment, skylight windows, gutters and downspouts.
- *Project Budget* -- \$3,388,146
- *Project Schedule* – Construction is anticipated to begin in Q3 2019 and conclude in Q3 2020.

2. University High School – Project to Provide New Roofing Campus-Wide and Selected Heating, Ventilation and Air Conditioning Units

- *Local District West, Board District 4– Melvoin*
- *Project Background and Scope* – This project is to provide approximately 71,000 square feet of new roofing at 20 buildings campus-wide, including new Heating, Ventilation and Air Conditioning units and equipment, gutters and downspouts.
- *Project Budget* -- \$2,186,171
- *Project Schedule* – Construction is anticipated to begin in Q1 2019 and conclude in Q3 2019.

3. Sun Valley Magnet School – Project to Provide New Heating, Ventilation and Air Conditioning Systems

- *Local District Northeast, Board District 6– Gonez*
- *Project Background and Scope* – This project is to provide a new Heating, Ventilation and Air Conditioning (HVAC) system in Building C. The existing HVAC system is undersized and does not provide adequate ventilation. Portable air conditioning units have been provided as an interim solution until the permanent system is installed.
- *Project Budget* -- \$3,770,837
- *Project Schedule* – Construction is anticipated to begin in Q1 2020 and conclude in Q4 2020.

SCHOOL CONSTRUCTION BOND CITIZENS' OVERSIGHT COMMITTEE

Quynh Nguyen, Chair
LAUSD Student Parent
Barry Waite, Vice Chair
CA Tax Reform Assn.
Susan Linschoten, Secretary
L.A. Co. Auditor-Controller's Office
Stuart Magruder, Executive Committee
American Institute of Architects
Rachel Greene, Executive Committee
Tenth District PTSA

Bevin Ashenmiller
LAUSD Student Parent
Araceli Sandoval-Gonzalez
Early Education Coalition
Greg Good
L.A. City Mayor's Office
Michael Keeley
CA Charter School Association
Karen Krygier
L.A. City Controller's Office
Kate Mergen
Assoc. General Contractors of CA

Ron Miller
L.A. Co. Federation of Labor AFL-CIO
Scott Pansky
L.A. Area Chamber of Commerce
Dolores Sobalvarro
AARP
Kathryn Steinberg
31st District PTSA
Celia Ayala (Alternate)
Early Education Coalition
Arlene Barrera (Alternate)
L.A. Co. Auditor-Controller's Office

Joseph P. Buchman – Legal Counsel
Burke, Williams & Sorensen, LLP
Thomas A. Rubin, CPA
Oversight Committee Consultant

Timothy Popejoy
Bond Oversight Administrator
Daniel Hwang
Asst. Administrative Analyst

RESOLUTION 2018-13**BOARD REPORT NO. 427-17/18**

**AMENDMENT TO THE FACILITIES SERVICES DIVISION STRATEGIC
EXECUTION PLAN TO DEFINE AND APPROVE THREE PROJECTS THAT
ADDRESS CRITICAL SCHOOL REPAIR NEEDS**

WHEREAS, District Staff proposes that the Board of Education approve an amendment to the Facilities Services Division (FSD) Strategic Execution Plan (SEP) to define and approve three projects that addresses critical school repair needs with a budget of \$9,345,154 (the "Project") as described in Board Report 427-17/18 attached hereto; and

WHEREAS, District Staff has determined that the Projects will help facilitate the implementation of the Facilities Bond Program strategy to address unfunded and pressing school facilities related to safety, compliance, and instructional requirements through 2018 (Board Report No. 048-17/18); and

WHEREAS, the School Upgrade Program, the latest phase of the District's Bond Program, includes a spending target to address "Critical School Repair and Safety Improvements to School Building Components"; and

WHEREAS, District Staff has determined that the Projects are necessary to improve student health, safety and educational quality; and

WHEREAS, the Board of Education's approval of the Projects will authorize District Staff to proceed with the expenditure of bond funds to undertake the Projects in accordance with the provisions set forth in Measures K, R, Y and Q; and

WHEREAS, these projects are consistent with the District's commitment to address unmet school facilities needs and provide students with a safe and healthy learning environment; and

Resolution 2018-13**AMENDMENT TO THE FACILITIES SERVICES DIVISION STRATEGIC
EXECUTION PLAN TO DEFINE AND APPROVE THREE PROJECTS THAT
ADDRESS CRITICAL SCHOOL REPAIR NEEDS****PAGE 2**

WHEREAS, District Staff has concluded that the proposed SEP amendment will facilitate implementation of the FSD SEP, and therefore, it will not adversely affect the District's ability to successfully complete the FSD SEP.

NOW, THEREFORE, BE IT RESOLVED THAT:

1. The School Construction Citizens' Bond Oversight Committee recommends that the Board of Education adopt an amendment to the Facilities Services Division (FSD) Strategic Execution Plan (SEP) to define and approve three projects that addresses critical school safety and repair needs, with a budget of \$9,345,154, as defined in Board Report 427-17/18, a copy of which is attached hereto in the form it was presented to the BOC and is incorporated herein by reference.
2. This resolution shall be transmitted to the Los Angeles Unified School District Board of Education and posted on the Oversight Committee's website.
3. The District is directed to track the above recommendation and to report on the adoption, rejection, or pending status of the recommendations as provided in section 6.2 of the Charter and Memorandum of Understanding between the Oversight Committee and the District.

ADOPTED on April 26, 2018, by the following vote:

AYES: 12

ABSTENTIONS: 0

NAYS: 0

ABSENCES: 3


Quynh Nguyen
Chair


Barry Waite
Vice Chair



Board of Education Report

File #: Rep-346-21/22, **Version:** 1

Define and Approve 33 Projects to Provide Critical Replacements and Upgrades of School Building/Site Systems and Components and Amend the Facilities Services Division Strategic Execution Plan to Incorporate Therein

June 14, 2022

Facilities Services Division

Action Proposed:

Define and approve 33 projects to provide critical replacements and upgrades of school building/site systems and components, as listed on Attachments A and B, and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein. The total combined budget for the 33 projects is \$7,717,557.

Authorize the Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the proposed projects, including budget modifications and the purchase of equipment and materials.

Background:

Priorities for the expenditure of capital funding are evaluated to ensure the District's most pressing priorities are being addressed. More than 70 percent of Los Angeles Unified School District (Los Angeles Unified or District) school buildings were built more than 50 years ago, and more than \$50 billion of unfunded school facilities needs have been identified Districtwide, and these needs grow every year. As the District's capital needs far exceed available funding, the most pressing unfunded critical needs will continue to be addressed based on an evaluation of known facilities conditions and needs at schools. Projects developed under this category of need, *Critical Replacements and Upgrades of School Building/Site Systems and Components*, will replace failing building systems that create safety concerns and are disruptive to school operations. Systems in the worst condition, especially those that pose a safety hazard and/or will negatively impact school operations and other building systems if not addressed, will be addressed first.

The project proposals contained in this Board Report align with these priorities. Attachment A includes three projects to replace failing building systems that create safety concerns and are disruptive to school operations. Attachment B includes 30 projects to provide new secure entry systems.

Expected Outcomes:

Staff anticipates that the Board of Education will define and approve 33 projects that address critical replacement and upgrade needs, and amend the Facilities SEP to incorporate therein. Approval will authorize staff to proceed with the implementation of the proposed projects to improve student health, safety and educational quality.

Board Options and Consequences:

Adoption of the proposed action will authorize staff to proceed with the expenditure of Bond Program funds to undertake the project proposals in accordance with the provisions set forth in Los Angeles Unified local bond

measures K, R, Y, Q, and RR. If the proposed action is not approved, Bond Program funds will not be expended, and critical replacement and upgrade needs will remain unaddressed.

Policy Implications:

The proposal is consistent with the Los Angeles Unified's long-term goal to address unmet school facilities needs and significantly improve the conditions of aging and deteriorating school facilities as described in Los Angeles Unified local bond measures. Moreover, the proposed secure entrance projects support the *Protecting Our Students and School Sites Board Resolution* (Res-032-17/18).

Budget Impact:

The total combined budget for the 33 projects is \$7,717,557. The projects will be funded with Bond Program funds earmarked specifically for critical replacements and upgrades of school building/site systems and components.

Each project budget was prepared based on the current information known and assumptions about the project scope, site conditions, and market conditions. Individual project budgets will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise and will be adjusted accordingly to enable the successful completion of each project.

Student Impact:

Approval of the proposed projects enables the District to continue our ongoing efforts to undertake facilities improvements that help ensure students are provided with safe school environments that promote teaching and learning.

Equity Impact:

Please see attached statement.

Issues and Analysis:

It may be necessary to undertake feasibility studies, site analysis, scoping, and/or due diligence activities on the proposed projects prior to initiating design. As necessary, the Office of Environmental Health and Safety (OEHS) will evaluate the proposed projects in accordance with the California Environmental Quality Act (CEQA) to ensure compliance. If through the planning and design process it is determined that the proposed project scope(s) will not sufficiently address the critical needs identified, the project scope, schedule and budget will be revised accordingly.

Bond Oversight Committee Recommendations:

This item was considered by the School Construction Bond Citizen's Oversight Committee (BOC) at its meeting on June 2, 2022. Staff has concluded that this proposed Facilities SEP amendment is in alignment with BOC recommendations and will facilitate Los Angeles Unified's ability to successfully implement the Facilities SEP.

Attachments:

Attachment A - Projects to Replace Failing Building Systems that Create Safety Concerns and are Disruptive to School Operations

Attachment B - Projects to Provide New Secure Entry Systems

Attachment C - BOC Resolution

File #: Rep-346-21/22, **Version:** 1

Informatives:

None.

Submitted:

5/20/22

File #: Rep-346-21/22, Version: 1

RESPECTFULLY SUBMITTED,

APPROVED BY:




ALBERTO M. CARVALHO
Superintendent



MEGAN K. REILLY
Deputy Superintendent

REVIEWED BY:

APPROVED BY:



DEVORA NAVERA REED
General Counsel



MARK HOVATTER
Chief Facilities Executive
Facilities Services Division

☒ Approved as to form.

REVIEWED BY:

PRESENTED BY:



TONY ATIENZA
Director, Budget Services and Financial Planning



ROBERT LAUGHTON
Director of Maintenance and Operations
Facilities Services Division

☒ Approved as to budget impact statement.

INTEROFFICE CORRESPONDENCE
Los Angeles Unified School District
FACILITIES SERVICES DIVISION
*Equity Impact Statement***

TO: Members, Board of Education
 Alberto M. Carvalho, Superintendent

DATE: May 25, 2022

FROM: Mark Hovatter, Chief Facilities Executive

SUBJECT: BR-346-21/22 DEFINE AND APPROVE 33 PROJECTS TO PROVIDE CRITICAL REPLACEMENTS AND UPGRADES OF SCHOOL BUILDING/SITE SYSTEMS AND COMPONENTS AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN

Board Meeting Date:	6/14/2022
----------------------------	------------------

Equity Impact				
Component	1	2	3	4
Recognition	Does not recognize historical inequities	Vaguely recognizes historical inequities	Affirmatively recognizes historical inequities	Actively recognizes and specifies historical inequities to correct
Resource Prioritization	Does not prioritize resources based on student need	Somewhat prioritizes resources based on student need	Prioritizes resources based on student need	Effectively prioritizes resources based on student need
Results	Unlikely to result in closed opportunity gaps and/or closing achievement gaps	May result in closed opportunity gaps and/or closing achievement gaps	Likely to result in closed opportunity gaps and/or closing achievement gaps	Extremely likely to result in closed opportunity gaps and/or closing achievement gaps

Component	Score	Score Rationale
Recognition	3	The proposed projects address the severe deterioration and/or inadequacy of these schools' building/site systems and components that result from historic underinvestment in District school facilities.
Resource Prioritization	4	Every student is entitled to a learning space that is safe, secure and functional, and where school building systems are sound, efficient and working. These projects address critical needs of core facilities where systems have failed and/or other pressing unmet school facilities needs. As the District's school facilities needs far exceed available funding, systems in the worst condition, especially those that pose a safety hazard and/or will negatively impact school operations and other building systems if not addressed, must be addressed first. A Districtwide Facilities Condition Assessment was conducted in which every building, space and room in the District was catalogued and assessed. Building components/systems in the

***Form to be completed for Districtwide or partial Districtwide Board Report items that expend resources.*

Component	Score	Score Rationale
		worst condition are prioritized first to ensure school facilities do not impair or impede students' ability to learn.
Results	3	All students deserve the opportunity to learn in safe and well maintained school facilities. Multiple aspects of the school environment support student learning and the proposed projects address the physical facilities aspect within this overall framework.
TOTAL	10	

Contact Person:	Telephone:	Email:
Andrea Reyes	213.241.6518	andrea.reyes@lausd.net



LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report
Attachment A

Projects to Replace Failing Building Systems that Create Safety Concerns and are Disruptive to School Operations

1. Gompers Middle School – Project to Provide New Roofing

- *Local District South, Board District 7 – Ortiz Franklin*
- *Project Background and Scope* – This project is to provide approximately 121,290 square feet of new roofing at 29 buildings, including the installation of new gutters and downspouts and painting of affected areas.
- *Project Budget* -- \$3,159,311
- *Project Schedule* – Construction is anticipated to begin in Q3 2023 and conclude in Q1 2024.

2. South Gate High School – Project to Provide New Roofing

- *Local District East, Board District 5 – Goldberg*
- *Project Background and Scope* – This project is to provide approximately 75,193 square feet of new roofing at 28 buildings, including the installation of new gutters and downspouts and painting of affected areas.
- *Project Budget* -- \$1,930,970
- *Project Schedule* – Construction is anticipated to begin in Q3 2023 and conclude in Q1 2024.

3. Sherman Oaks Elementary Charter School – Project to Provide New Playground Matting and Structure

- *Local District Northeast, Board District 3 – Schmerelson*
- *Project Background and Scope* – This project is to replace the playground matting and structure in the main yard and replace the playground matting in the kindergarten yard.
- *Project Budget* -- \$1,444,633
- *Project Schedule* – Construction is anticipated to begin in Q3 2023 and conclude in Q1 2024.



**LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report**

**Attachment B
Projects to Provide New Secure Entry Systems**

#	BD	LD	Cost Center	School	Project Budget	Anticipated Construction Start	Anticipated Construction Completion
1	1	West	1552101	95th St. ES	\$32,159	Q2 2022	Q3 2022
2	1	West	1227401	Baldwin Hills ES	\$38,022	Q2 2022	Q3 2022
3	1	Central	1511301	Mack ES	\$32,032	Q2 2022	Q3 2022
4	2	East	1443801	Harrison ES	\$57,626	Q2 2022	Q3 2022
5	2	East	1195301	Perez Special Education Center	\$39,218	Q2 2022	Q3 2022
6	2	Central	1254201	White ES	\$39,373	Q2 2022	Q3 2022
7	3	Northwest	1247001	Blythe ES	\$30,397	Q2 2022	Q3 2022
8	3	Northwest	1270401	Calabash Charter Academy	\$36,160	Q2 2022	Q3 2022
9	3	Northwest	1280201	Capistrano ES	\$36,908	Q2 2022	Q3 2022
10	3	Northwest	1337701	Dearborn Charter Academy ES	\$74,633	Q2 2022	Q3 2022
11	3	Northwest	1434901	Hamlin Charter Academy ES	\$36,876	Q2 2022	Q3 2022
12	3	Northwest	1444501	Hart ES	\$36,826	Q2 2022	Q3 2022
13	3	Northwest	1469201	Justice Academy Charter ES	\$38,642	Q2 2022	Q3 2022
14	3	Northwest	1488701	Lockhurst Charter ES	\$42,217	Q2 2022	Q3 2022
15	3	Northwest	1763701	Welby Way Charter ES	\$39,360	Q2 2022	Q3 2022
16	4	West	1611001	Playa Del Rey ES	\$37,717	Q2 2022	Q3 2022
17	4	Northwest	1660601	Serrania Charter for Enriched Studies	\$38,520	Q2 2022	Q3 2022
18	4	Northwest	1671201	Shirley ES	\$32,662	Q2 2022	Q3 2022
19	5	Central	1454801	Hobart ES	\$57,694	Q2 2022	Q3 2022
20	5	Central	1498201	Los Angeles ES	\$38,086	Q2 2022	Q3 2022
21	5	Central	1498301	Mariposa-Nabi PC	\$37,797	Q2 2022	Q3 2022
22	5	East	1690401	Stanford ES	\$32,777	Q2 2022	Q3 2022
23	5	East	1750701	Victoria ES	\$31,673	Q2 2022	Q3 2022



**LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report**

**Attachment B
Projects to Provide New Secure Entry Systems**

#	BD	LD	Cost Center	School	Project Budget	Anticipated Construction Start	Anticipated Construction Completion
24	6	Northeast	1429501	Gridley ES	\$56,059	Q2 2022	Q3 2022
25	6	Northeast	1460301	Hubbard ES	\$48,507	Q2 2022	Q3 2022
26	7	South	1663001	75th St. ES	\$32,049	Q2 2022	Q3 2022
27	7	South	1283601	Carson ES	\$31,064	Q2 2022	Q3 2022
28	7	South	1338401	Del Amo ES	\$32,425	Q2 2022	Q3 2022
29	7	South	1231301	Moore Math/Science/Technology Academy	\$31,871	Q2 2022	Q3 2022
30	7	South	1687201	Wisdom ES	\$33,293	Q2 2023	Q3 2023
Total					\$1,182,643		

LOS ANGELES UNIFIED SCHOOL DISTRICT**SCHOOL CONSTRUCTION BOND CITIZENS' OVERSIGHT COMMITTEE****Rachel Greene, Chair**

Tenth District PTSA

Chris Hannan, Vice-Chair

L.A. Co. Federation of Labor AFL-CIO

Margaret Fuentes, Secretary

LAUSD Student Parent

Araceli Sandoval-Gonzalez, Executive Committee

Early Education Coalition

Laura Baz

LAUSD Student Parent

Neelura Bell

CA Charter School Association

Jeffrey Fischbach

CA Tax Reform Assn.

D. Michael Hamner

American Institute of Architects

Hyepin Im

L.A. City Controller's Office

Susan Linschoten

L.A. Co. Auditor-Controller's Office

Jennifer McDowell

L.A. City Mayor's Office

Scott Pansky

L.A. Area Chamber of Commerce

Dolores Sobalvarro

AARP

Celia Ayala (Alternate)

Early Education Coalition

Chad Boggio (Alternate)

L.A. Co. Federation of Labor AFL-CIO

Dr. Clarence Montecarlo (Alternate)

Tenth District PTSA

Samantha Rowles (Alternate)

LAUSD Student Parent

Connie Yee (Alternate)

L.A. Co. Auditor-Controller's Office

Vacant31st District PTSA**Vacant**

Assoc. General Contractors of CA

Timothy Popejoy

Bond Oversight Administrator

Perla Zitle

Bond Oversight Coordinator

Joseph P. Buchman – Legal Counsel

Burke, Williams & Sorensen, LLP

Lori Raineri and Keith Weaver – Oversight Consultants

Government Financial Strategies

RESOLUTION 2022-27**BOARD REPORT NO. 346-21/22****RECOMMENDING BOARD APPROVAL TO DEFINE AND APPROVE 33 PROJECTS TO PROVIDE CRITICAL REPLACEMENTS AND UPGRADES OF SCHOOL BUILDING/SITE SYSTEMS AND COMPONENTS AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN**

WHEREAS, District Staff proposes that the Board of Education define and approve 33 projects that address critical replacement and upgrade needs at schools with a budget of \$7,717,557 (the "Projects") as described in Board Report 346-21/22 attached hereto, and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein, and authorize the Chief Procurement Officer and/or the Chief Facilities Executive, and/or their designee(s), to execute all instruments necessary to implement the Projects; and

WHEREAS, Projects developed under the School Upgrade Program category of need, Critical Replacements and Upgrades of School Building/Site Systems and Components, will replace failing building systems that create safety concerns and are disruptive to school operations; and

WHEREAS, The Projects are consistent with the Los Angeles Unified School District (Los Angeles Unified or District)'s long-term goal to address unmet school facilities needs and significantly improve the conditions of aging and deteriorating school facilities as described in Los Angeles Unified local bond measures; and

WHEREAS, District Staff has determined that the Projects are necessary to improve student health, safety and educational quality; and

RESOLUTION 2022-27**RECOMMENDING BOARD APPROVAL TO DEFINE AND APPROVE 33 PROJECTS TO PROVIDE CRITICAL REPLACEMENTS AND UPGRADES OF SCHOOL BUILDING/SITE SYSTEMS AND COMPONENTS AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN**

WHEREAS, the Board of Education's approval of the Projects will authorize District Staff to proceed with the expenditure of bond funds to undertake the Projects in accordance with the provisions set forth in Los Angeles Unified local bond measures K, R, Y, Q, and RR; and

WHEREAS, District Staff has concluded that this proposed Facilities SEP amendment will facilitate Los Angeles Unified's ability to successfully complete the Facilities SEP.

NOW, THEREFORE, BE IT RESOLVED THAT:

1. The School Construction Citizens' Bond Oversight Committee recommends that the Board of Education define and approve 33 projects that address critical replacement and upgrade needs at schools, with a combined budget of \$7,717,557, and amend the Facilities SEP to incorporate therein, as described in Board Report 346-21/22, a copy of which is attached hereto in the form it was presented to the BOC and is incorporated herein by reference.
2. This resolution shall be transmitted to the Los Angeles Unified School District Board of Education and posted on the Oversight Committee's website.
3. The District is directed to track the above recommendation and to report on the adoption, rejection, or pending status of the recommendations as provided in section 6.2 of the Charter and Memorandum of Understanding between the Oversight Committee and the District.

ADOPTED on June 2, 2022, by the following vote:

AYES: 9

ABSTENTIONS: 0

NAYS: 0

ABSENCES: 4

/Rachel Greene/

Rachel Greene
Chair

/Chris Hannan/

Chris Hannan
Vice-Chair



Board of Education Report

File #: Rep-298-19/20, **Version:** 1

Amendment to the Facilities Services Division Strategic Execution Plan to Define and Approve Two Projects that Address Critical School Repair Needs

May 19, 2020

Facilities Services Division

Action Proposed:

Staff proposes that the Board of Education approve an amendment to the Facilities Services Division (FSD) Strategic Execution Plan (SEP) to define and approve two projects that address critical school repair needs, as listed on Attachment A. Staff further proposes that the Board authorize the Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the proposed projects, including budget modifications and the purchase of equipment and materials. The total combined budget for the two projects is \$10,075,081.

Background:

As the District's capital needs far exceed available funding, priorities for the expenditure of capital funding are evaluated to ensure the District's most pressing priorities are being addressed. Based on an evaluation of known facilities conditions and needs at schools, the following types of projects have been identified as the most pressing unfunded critical school repair and safety needs that should continue to be addressed within the limited funding available:

- Failing, deteriorated, and outdated building systems and components
- School buildings, rooms and/or facilities deemed unsafe for occupancy
- Other critical health and safety concerns, urgent/emergency conditions, and/or health and safety code compliance issues that may arise

The project proposals contained in this Board Report align with these identified types of pressing critical school repair and safety conditions. The list consists of electrical and pipeline projects. Attachment A provides additional details pertaining to the proposed projects.

Expected Outcomes:

Staff anticipates that the Board of Education will approve the proposed action to define and approve two projects to address critical school repair needs that will improve student health, safety and educational quality.

Board Options and Consequences:

A "yes" vote will authorize staff to proceed with the expenditure of bond funds to undertake the project proposals in accordance with the provisions set forth in Measures K, R, Y and Q. If the proposed action is not approved, bond funds will not be expended and critical school repair needs will remain unaddressed.

File #: Rep-298-19/20, **Version:** 1

Policy Implications:

The action is consistent with the District's commitment to address unmet school facilities needs and provide students with a safe and healthy learning environment. Moreover, the proposal is aligned with the Board-adopted Facilities Bond Program strategy to address unfunded and pressing school facilities needs related to safety, compliance, and instructional requirements (Board Report No. 048-17/18).

Budget Impact:

The total combined budget for the two projects is \$10,075,081. The projects will be funded with Bond Program funds earmarked specifically for critical school repair and safety improvements to school building components. However, \$8,938,497 will first be transferred from Bond funds earmarked specifically for Districtwide charter school facilities for the underground heating lines replacement project at El Camino Real Charter High School, an independent charter school.

Each project budget was prepared based on the current information known and assumptions about the project scope, site conditions, and market conditions. Individual project budgets will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise, and will be adjusted accordingly to enable the successful completion of each project.

Student Impact:

Continuing our efforts to undertake critical school repair and safety improvement projects is a vital component to the District's ability to provide safe school environments that promote teaching and learning.

Issues and Analysis:

It may be necessary to undertake feasibility studies, site analysis, scoping, and/or due diligence activities on the proposed projects prior to initiating design. As necessary, the Office of Environmental Health and Safety (OEHS) will evaluate the proposed projects in accordance with the California Environmental Quality Act (CEQA) to ensure compliance. If through the planning and design process it is determined that the proposed project scope(s) will not sufficiently address the critical need identified, the project scope, schedule and budget will be revised accordingly.

Bond Oversight Committee Recommendations:

This item was considered by the BOC at its meeting on April 24, 2020. Staff has concluded that this proposed FSD SEP amendment will facilitate implementation of the FSD SEP, and therefore, it will not adversely affect the District's ability to successfully complete the FSD SEP.

Attachments:

Attachment A - Project Definitions for Two Projects that Address Critical School Repair Needs
Attachment B - BOC Resolution

Informatives:

None.

Submitted:

4/17/20

File #: Rep-298-19/20, Version: 1

RESPECTFULLY SUBMITTED,



AUSTIN BEUTNER
Superintendent

APPROVED BY:



MEGAN K. REILLY
Deputy Superintendent
Office of the Deputy Superintendent

REVIEWED BY:



DAVID HOLMQUIST
General Counsel

APPROVED BY:



MARK HOVATTER
Chief Facilities Executive
Facilities Services Division

 Approved as to form.

REVIEWED BY:



TONY ATIENZA
Director, Budget Services and Financial Planning

PRESENTED BY:



ROBERT LAUGHTON
Director of Maintenance and Operations
Facilities Services Division

 Approved as to budget impact statement.



LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report
Attachment A

1. Hale Charter Academy Middle School – Project to Replace the Main Electrical Switchgear

- *Local District Northwest, Board District 3 – Schmerelson*
- *Project Background and Scope* – The main electrical switchgear serves various buildings campus-wide with antiquated oil-filled circuit breakers. The breakers were designed decades ago and are leaking oil. This project is to replace the existing main electrical switchgear by installing new load interrupting switches.
- *Project Budget* -- \$1,136,584
- *Project Schedule* – Construction is anticipated to begin in Q2 2021 and conclude in Q3 2021.

2. El Camino Real Charter High School – Project to Provide New Pipelines Sitewide

- *Local District Northwest, Board District 3 – Schmerelson*
- *Project Background and Scope* – The existing pipelines are deteriorated and have repeatedly failed. This project is to provide new hot and chilled water pipelines serving the entire campus.
- *Project Budget* -- \$8,938,497
- *Project Schedule* – Construction is anticipated to begin in Q3 2021 and conclude in Q2 2022.

LOS ANGELES UNIFIED SCHOOL DISTRICT**SCHOOL CONSTRUCTION BOND CITIZENS' OVERSIGHT COMMITTEE****Rachel Greene, Chair**

Tenth District PTSA

Bevin Ashenmiller, Vice-Chair

LAUSD Student Parent

Karen Krygier, Secretary

L.A. City Controller's Office

Araceli Sandoval-Gonzalez, Executive Committee

Early Education Coalition

Tracy Bartley31st District PTSA**Jeffrey Fischbach**

CA Tax Reform Assn.

Melanie Freeland

American Institute of Architects

Margaret Fuentes

LAUSD Student Parent

Greg Good

L.A. City Mayor's Office

Chris Hannan

L.A. Co. Federation of Labor AFL-CIO

Michael Keeley

CA Charter School Association

Dolores Sobalvarro

AARP

Alvin Trotter, Jr.

L.A. Area Chamber of Commerce

Guy Zelenski

L.A. Co. Auditor-Controller's Office

Celia Ayala (Alternate)

Early Education Coalition

Connie Yee (Alternate)

L.A. Co. Auditor-Controller's Office

Jose Zambrano (Alternate)

Tenth District PTSA

(Vacant)

Assoc. General Contractors of CA

Joseph P. Buchman – Legal Counsel

Burke, Williams & Sorensen, LLP

Lori Raineri and Keith Weaver – Oversight Consultants

Government Financial Strategies

Timothy Popejoy

Bond Oversight Administrator

Perla Zitle

BOC Staff

RESOLUTION 2020-10**BOARD REPORT NO. 298-19/20****AMENDMENT TO THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO DEFINE AND APPROVE TWO PROJECTS THAT ADDRESS CRITICAL SCHOOL SAFETY AND REPAIR NEEDS**

WHEREAS, District Staff proposes that the Board of Education approve an amendment to the Facilities Services Division (FSD) Strategic Execution Plan (SEP) to define and approve two projects that address critical school repair needs with a budget of \$10,075,081 (the "Projects") as described in Board Report 298-19/20 attached hereto; and authorize the Chief Procurement Officer and/or the Chief Facilities Executive, and/or his designee(s), to execute all instruments necessary to implement the proposed projects; and

WHEREAS, District Staff has determined that the Projects are necessary to improve student health, safety and educational quality; and

WHEREAS, District Staff has determined that the Projects will help facilitate the implementation of the Facilities Bond Program strategy to address unfunded and pressing school facilities related to safety, compliance, and instructional requirements; and

WHEREAS, the Projects are consistent with the District's commitment to address unmet school facilities needs and provide students with a safe and healthy learning environment; and

WHEREAS, the Board of Education's approval of the Projects will authorize District Staff to proceed with the expenditure of bond funds to undertake the Projects in accordance with the provisions set forth in Measures K, R, Y and Q; and

Bond Oversight Committee

RESOLUTION 2020-10**AMENDMENT TO THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO DEFINE AND APPROVE TWO PROJECTS THAT ADDRESS CRITICAL SCHOOL REPAIR NEEDS**

WHEREAS, District Staff has concluded that the proposed SEP amendment will facilitate implementation of the FSD SEP, and therefore, it will not adversely affect the District's ability to successfully complete the FSD SEP.

NOW, THEREFORE, BE IT RESOLVED THAT:

1. The School Construction Citizens' Bond Oversight Committee recommends that the Board of Education adopt an amendment to the Facilities Services Division (FSD) Strategic Execution Plan (SEP) to define and approve two projects that address critical school safety and repair needs, with a budget of \$10,075,081, as defined in Board Report 298-19/20, a copy of which is attached hereto in the form it was presented to the BOC and is incorporated herein by reference.
2. This resolution shall be transmitted to the Los Angeles Unified School District Board of Education and posted on the Oversight Committee's website.
3. The District is directed to track the above recommendation and to report on the adoption, rejection, or pending status of the recommendations as provided in section 6.2 of the Charter and Memorandum of Understanding between the Oversight Committee and the District.

ADOPTED on April 24, 2020, by the following vote:

AYES: **14**

ABSTENTIONS: **0**

NAYS: **0**

ABSENCES: **0**

/Rachel Greene/

Rachel Greene
Chair

/Bevin Ashenmiller/

Bevin Ashenmiller
Vice-Chair



Board of Education Report

File #: Rep-024-23/24, Version: 2

Capital Plan Projects

December 12, 2023

Office of the Chief Business Officer

Action Proposed:

Approve the use of \$423.5 million of Certificates of Participation (COP) to fund all or a portion of nine Capital Plan projects and/or programs, to be undertaken at one or more sites, the scope schedule and budget of which is outlined in Attachment A, and authorize the Superintendent and/or his designee(s) to execute all instruments necessary, as legally permissible, to implement the initial Capital Plan projects and/or programs, including budget modifications.

Some of the listed projects may require additional funding to fully complete, however this proposal is to authorize COP expenditures in the amount equal to what was generated by the August 2023 issuance, which was authorized by the Board of Education (Board) in June 2023. The funding strategy for some projects may include the use of various General Fund sources.

Background:

On June 13, 2023, the Board authorized a resolution approving the execution and delivery of COPs in the not-to-exceed amount of \$500 million (Board Report No. 300-22/23). In August 2023, the Office of the Chief Business Officer (CBO) sold COPs generating \$423.5 million to fund critical unmet needs of our school support facilities, as well as high-priority school facility needs for which sufficient bond funding is not currently available.

Under the leadership of the Chief Business Officer, a five-year capital plan covering fiscal years 2023-24 through 2027-2028 is being developed. Projects and/or programs were proposed as priority projects from various divisions, and only individual projects over \$1 million for which sufficient bond funds are not currently available and/or eligible were considered. All projects were reviewed by a steering committee comprised of various District senior executives using criteria including health and safety, regulatory compliance, alignment to the Strategic Plan, and economic impact. This work resulted in the identification of 12 priority projects and/or programs with an approximate budget of \$1.3 billion, approximately \$1.1 billion of which was identified for COPs proceeds. Requests to authorize future sales of COPs are anticipated to be proposed to the Board in subsequent years. The projects and/or programs being proposed for funding are a result of this work. All 12 identified projects and/or programs are listed below:

1. Enrollment Modernization Project
2. Student Information Systems Upgrades Project
3. Student Support Applications Modernization*
4. Student Data Analytics, Reporting and Dashboards Project*
5. Sun Valley Electric Buses and Generator Purchases Project
6. Sun Valley Transportation Center Electrification Project*
7. Green Schools for All Program*

8. Campus Security Systems Improvements*
9. Cybersecurity Improvements*
10. Gardena Area Transportation Center and Electric Bus Charging**
11. Gardena Area Electric Bus and Generator Purchases**
12. Procurement Services Support Center Upgrades: Electrification and Industrial Fans**

**Based on current scope and budget estimates, anticipated to require additional funding to fully complete/implement.*

***No funding is being requested as part of this action; however, their current total estimated budget is part of the \$1.3 billion Capital Plan estimate.*

The project budgets were prepared based on current information, and assumptions about the project scope, site conditions, and market conditions. The project budgets will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise and will be adjusted accordingly to enable the successful completion of the proposed projects.

Expected Outcomes:

The Board will approve nine Capital Plan projects and/or programs, allowing the District to move forward with needed capital improvements.

Board Options and Consequences:

Upon Board approval, staff will be authorized to proceed with the expenditure of COP funds and all other activities necessary to implement the proposed projects. If the proposed action is not approved, the District will not move forward with the projects.

Policy Implications:

This does not impact existing policy.

Budget Impact:

The 2023-24 Budget included the annual debt service for the 2023 COPs and non-capital costs for the projects. In Fiscal Year 2024, the annual debt service cost is estimated at \$11.3 million, and from FY 2025-FY 2038 the estimated annual cost is \$33.4 million. The debt service will be paid out of the District's General Fund. Furthermore, some projects will require additional funding to fully complete and/or implement. Sources of funds may vary. These additional costs are estimated to be approximately \$800 million, with the majority of funds, approximately \$650 million, expected to be funded by future COP issuances, and approximately \$89.5 million from Restricted General Fund-Expanded Learning Opportunity Program (ELOP).

A portion of the scope of five projects was temporarily front funded with operational budget with the intent to reimburse with COP proceeds once approved for specific projects. With the Board's approval of the Capital Plan projects, any prior expenditures will be transferred to the proposed projects. The projects that received some front funding are:

- Sun Valley Electric Buses and Generator Purchases Project: due to the high demand for electric school buses and to account for additional time needed to fulfill an order of 180 buses.
- Sun Valley Transportation Center Electrification Project: to help meet the District's electrification goals.
- Campus Safety Systems Improvement Projects at 291 Sites (Phase 1): due to a need to address student

safety as quickly as possible at priority school sites.

- Cybersecurity Improvement Program: due to an urgent need to begin implementing cybersecurity enhancements throughout the District.

If future COPs issuances and/or other funding sources are authorized for Capital Plan projects, all funding sources will be integrated into the Capital Plan sources of funds to support funding flexibility and efficiency and the effective implementation of the Capital Plan.

Student Impact:

Projects will improve the educational opportunities for students. The cybersecurity project will reduce risks associated with students' personal information and coursework. Similarly, the campus security project will provide a safer physical environment for students. Electrification of the school bus fleet will reduce the long-term operating costs and improve air quality.

Equity Impact:

Component	Score	Score Rationale
Recognition	2	Some of the projects are influenced by equity.
Resource Prioritization	4	Implementation of many of the projects will be conducted such that underserved populations will be a priority.
Results	3	Many of the projects, including electrification of the fleet, are expected to benefit those most impacted by historic health inequities.
TOTAL	9	

Issues and Analysis:

Projects may be undertaken at multiple District sites and/or may include various phases. Exhibit A outlines the scope of work proposed to be undertaken within the initial COPs issuance of \$423.5 million. Three of the nine projects are anticipated to be completed in their entirety, and six projects include an additional phase(s) of scope requiring further funding or a future allocation of funds to complete the initial phase as scoped.

Staff expects to return to the Board at a later date for authorization to sell additional COPs to fund projects at other District sites, additional project phases, and/or new Capital Plan projects.

Attachments:




Attachment A - Capital Plan Projects - scope, schedule, and budget

Informatives:

None.

Submitted:

12/8/2023

RESPECTFULLY SUBMITTED,
ALBERTO M. CARVALHO
Superintendent**APPROVED BY:**
PEDRO SALCIDO
Deputy Superintendent, Business Services and Operations**REVIEWED BY:**
DEVORA NAVERA REED
General Counsel**APPROVED & PRESENTED BY:**
DAVID D. HART
Chief Business Officer

☒ Approved as to form.

REVIEWED BY:
NOLBERTO DELGADILLO
Deputy Chief Business Officer, Finance

☒ Approved as to budget impact statement.

**LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report**

Attachment A: Capital Plan Projects: Scope, Schedule, and Budget

1. Enrollment Modernization Project

Project Scope: Includes creation of an efficient process for families to apply, register and enroll their children in District schools by eliminating many of the forms parents currently must submit, transitioning from a manual, paper-based process to an automated one. This initiative will be accomplished via multiple projects in coordination with various business owners and stakeholders. One of the projects under this initiative is:

- o Configure online enrollment system to be mobile friendly.
- o Implement changes identified in Board Resolution (Res-044-18/19) "Everyone Counts", which requests that additional ethnicities be added to District applications to further disaggregate data for Asian, Pacific Islander, and other ethnic groups.
- o Enhancements to applications including, but not limited to, enrollment applications, MiSiS, SAP, Focus reports, data warehouse (IODS).
- o Develop new reports and dashboards for internal use as needed.
- o Develop new reports for external Federal and State reporting as needed.

Total Project Budget and COPs Allocation: \$2,000,000

Project Schedule: Implementation is anticipated to begin in Q1-2024 and be completed in Q4-2024.

2. Student Information Systems Upgrades Project

Project Scope: Includes updates to the District's student information system, including integration with the Bell Schedule, Household Hub (a system of record for parent information), and Early Education Student Information System. The scope may include, but is not limited to:

- o *Household Hub Integration:* Integrate the household hub with all District applications that use parent information. This includes the Parent Portal, Early Ed Student Information System (EESIS), Unified Enrollment, Cafeteria Management Services (CMS), etc.

This project will also support non-application needs such as reducing mailings (e.g., a single magnet flier can be sent to a household with multiple District students), providing wrap-around services for families (e.g., chronic absenteeism, mental health, etc.), and data analysis.

Furthermore, the project will address creation of a common path for updating parent information and sharing the household hub information. Options for cleaning existing parent information and sharing the cleansed data across the applications will also be explored.

- o *My Integrated Student Information System (MiSiS) with Bell Schedule:* Optimize the management of student schedules, school calendars, and improve overall school operations. By establishing a seamless connection between MiSiS and the Bell Schedule system, schools can enhance efficiency, accuracy, and communication related to student attendance, class timetables, and daily routines.
- o *Early Education Student Information System Migration to MiSiS:* Integrate preschool student information and early information into MiSiS. This will eliminate achievement gaps before the third grade and provide instructional support by allowing educators to identify issues and provide educational interventions.

Total Project Budget and COPs Allocation: \$1,000,000

Project Schedule: Implementation is anticipated to begin in Q1-2024 and be completed in Q4-2024.

3. Student Support Applications Modernization Project

Project Scope: Technology refresh and additional functionality for the District's Student support applications, including, but not limited to the Academic Monitoring System, LAUSD Parent Portal/Mobile App upgrade, Special Education Data Management, Student Medical Services Management System, and Universal ID for students. The scope may include, but is not limited to:

- *Academic Monitoring System (AMS):* Provide ability to disaggregate student data such as Low-Income, Emergent Bilingual, Foster Youth, African American, and Students with Disabilities, and allow for real-time assessment and an instant collection of results.
- *LAUSD Parent Portal/Mobile App:* Provide additional functionality to enhance family engagement and communication around student progress and achievement. Leverage data analytics and artificial intelligence to analyze the student's progress and engage families and students with personalized recommendations and support.
- *Special Education Data Management:* Implement a web-based software system to be utilized Districtwide for the management and tracking of online Individualized Education Programs (IEPs), Individualized Family Services Plan (IFSP), Individual Service Plan (ISP), Section 504 Plans, Transition Services, RSP (Resource Program) Substitute, Due Process, Informal Dispute Resolution, State CALPADS reporting, District Validation Review, Extended School Year, Special Education Student Transportation, IEP Translation, and tracking of related services provided to students during the course of their education.
- *Student Medical Services Management System:* Implement a web-based system to be utilized Districtwide for the management and tracking of student treatment plan, protocols, medication management, immunization compliance, nursing services, health office visits, audiological evaluation, chronic conditions, health alerts, vision/audio/dental/speech/sports physical screenings, and vital monitoring.
- *Universal ID for Students:* Provide a singular ID for students to access services such as transportation, food services, library, after school programs, and school events. This will streamline many of the processes that will greatly benefit students.

Initial Budget and COPs Allocation:	\$11,400,000
<u>Future Anticipated Allocation(s):</u>	<u>\$ 3,000,000</u>
Total Anticipated Project Budget:	\$14,400,000

Project Schedule: Implementation is anticipated to begin in Q1-2024 and be completed in Q4-2025.

4. Student Data, Analytics, Reporting and Dashboards Project

Project Scope: Modernization of the District’s student data, analytics, reporting, and dashboards systems. With a continued increase in the number of tools students use to learn, there has been a significant increase in the volume of data available to help measure and inform student growth and achievement. This project puts in place / modernizes tools to understand this data. The scope may include, but is not limited to, implementation of a Cloud-based, fully managed solution for student analytics. New features / functionalities include:

- o Learning analytics
- o Guide resources
- o Supports for administrators, schools, staff, students, and parents
- o Data drill-down by region, school, and student group level, and support the learning management needs
- o Integration of curriculum, learning, student performance, student progress and related information
- o Suitable metrics and measurements
- o Notifications for exceptions
- o Incorporation of suitable views in the current workbench and views provided to schools, including those for principals, teachers and counselors, and also aggregated views for Regions and offices, to effectively monitor and manage student progress, including English Learners, students with disabilities, students experiencing homelessness, foster youth and other focus groups

Initial Budget and COPs Allocation:	\$ 4,763,040
<u>Future Anticipated Allocation(s):</u>	<u>\$ 844,800</u>
Total Anticipated Project Budget:	\$ 5,607,840

Project Schedule: Implementation is anticipated to begin in Q1-2024 and be completed in Q3-2025.

5. Sun Valley Electric Buses and Generator Purchases Project

Project Scope: Located at 11247 Sherman Way, in the community of Sun Valley, the Sun Valley Transportation Center is one of three LAUSD transportation centers located in the San Fernando Valley serving students in the surrounding communities. The buses currently residing there are equipped with internal combustion engines powered with CNG and propane fuels. The Sun Valley Transportation Center will be the first bus yard to have all its school buses transition to electric-powered.

The project will replace all 180 school buses based at Sun Valley Transportation Center with zero-emissions electric school buses (ESBs). The ESBs will be equipped with the latest safety features, including Wi-Fi and a Global Positioning System (GPS), and will have a capacity for 42 or 75 passengers (depending on the model) and an operating range of approximately 125 miles with a full charge. Studies have shown that electric buses are more fuel efficient and significantly reduce the cost of repairs and maintenance. This can result in overall savings of up to \$1.8 million per year. The new buses are anticipated to be delivered in 2025.

As part of the project, 25 propane-powered generators will be purchased to support ESB charging until the construction and installation of permanent charging infrastructure is completed (anticipated approximately two years after the delivery of the ESBs). The generator, situated on a trailer, can fully charge up to eight buses at one time in approximately six to eight hours. The chargers can be ordered and purchased, as needed, to coincide with the projected delivery of the ESBs in 2025. These chargers will also be part of the energy contingency plan, in the event there is a widespread power outage.

This project is critical to ensuring that the new ESBs will be delivered in time to replace CNG school buses with tanks expiring in April 2025. These buses must be removed from service per State and Federal regulations upon expiration. Sufficient lead time is needed for manufacturers to build the buses and for the California Highway Patrol (CHP) to inspect the buses which may take three months after the delivery of the buses.

Total Project Budget and COPs Allocation: \$88,700,000

Project Schedule: Purchases began in Q2-2023 and are anticipated to be completed in Q4-2025.

6. Sun Valley Transportation Center Electrification Project

Project Scope: The Sun Valley Transportation Center Electrification project consists of:

- o *Charging Stations:* The installation of approximately 200 electric vehicle (EV) charging stations for school buses.
- o *Solar and Battery Storage:* Provide a new solar array canopy with battery storage.
- o *Bus Wash Building Replacement:* Replace the existing bus wash with a new prefabricated bus wash building.
- o *Paving:* Provide new asphalt overlay throughout the site with new parking striping. Provide new asphalt paving in the areas of trenching for underground conduit.
- o *Perimeter Barrier Wall:* Provide a new concrete perimeter barrier wall around the site with new security gates at the vehicle entry locations.
- o *Site Lighting & Security:* Provide new site lighting poles and provide new lighting under the solar canopy. Provide new security cameras.
- o *Landscape:* Provide a new landscape buffer on Sun Valley Magnet School property, adjacent to the new pre-cast concrete wall for noise reduction and improved aesthetics.
- o *Temporary Bus Parking:* Provide temporary offsite bus parking, as needed, during construction.

Initial Budget and COPs Allocation:	\$72,162,739
<u>Future Anticipated Funding Allocation(s):</u>	<u>\$ 7,957,901</u>
Total Anticipated Project Budget:	\$80,120,640

Project Schedule: Construction is anticipated to begin in Q4-2025 and to be completed in Q4-2026.

7. Green Schools for All Program

A multi-pronged approach, which includes various project types and funding sources, will be utilized to help meet the goal of providing 30% safe and sustainable green schoolyards at all schools, to the extent feasible based on the physical constraints of individual campuses, by 2035. In total \$139,500,000 of non-bond funds are anticipated to be invested to further this work. This action allocates \$25,000,000 of COPs, and authorizes the execution of all instruments necessary, as legally permissible, to implement the projects, including those funded with General Fund-ELOP, and to make budget modifications. As detailed below, it is anticipated that an additional funding allocation of \$25,000,000 will be requested to complete this work. Additionally, \$89,500,000 of Restricted General Fund- Expanded Learning Opportunity Program (ELOP) has been allocated for these projects.

Green Schoolyard Upgrade Projects

Project Scope/Background: The proposed projects will provide improvements to schoolyards to align with the goal of providing 30% of a school sites' schoolyard with green/natural spaces. The scope may include replacing significant areas of paved surfaces with permeable surfaces that incorporate native/drought tolerant planting, the addition of natural grass play fields, the installation of trees and other shade elements to achieve 20% shade in the schoolyard, irrigation, decomposed granite and pavers, outdoor classroom elements, as well as accessibility improvements, as required, to ensure equal access to all students. After approval of this action, individual project budgets, scopes and schedules will be developed.

Approximately \$100,000,000 of non-bond funding is anticipated to be invested in the development of 15 Green Schoolyard Upgrade projects. This action will authorize \$25,000,000 of COP funding, which will be combined with an allocation of \$50,000,000 of Restricted General Fund-ELOP, to provide an initial \$75,000,000 of Green Schoolyard Upgrade projects. This is expected to provide sufficient funding to complete pre-construction activities at all 15 sites listed below, and to complete construction at a minimum of 11 sites. It is anticipated that an additional allocation of approximately \$25,000,000 will be needed to complete all of these projects.

Board District	Region	Site Name	Green Schoolyards Index Rank
1	West	Marvin ES	81
1	South	Manchester ES	84
2	East	Bridge ES	4
2	East	Dena ES	7
3	North	Canoga Park ES	16
3	North	Sylvan Park ES	30
4	North	Vanalden ES	31
4	North	Encino ES	113
5	East	San Pedro ES	5

Board District	Region	Site Name	Green Schoolyards Index Rank
5	East	Heliotrope ES	8
6	North	Strathern ES	10
6	North	Roscoe ES	15
6	North	Arminta ES	2
7	South	Gardena ES	33
7	South	Ritter ES	34

Sites were identified using the Green Schoolyards Index, which ranks sites based on the following datasets for each site: updated schoolyard measurement, existing green/natural components, CalEnviroScreen 4.0 score, and Extreme Heat Temperature Tool. The first eight sites on the list that do not have an approved or planned project that would provide substantial greening improvements* were selected. Additionally, in an effort to provide geographic equality, at least two high-ranked sites were selected in each Board District.

*(*Project types which will provide substantial greening improvements: comprehensive modernization, major modernization, classroom replacement, Pavement and Campus Exterior Upgrade (PACEUP) projects, Green Schoolyard Improvement Projects (Non-Division of the State Architect (DSA)/Americans with Disabilities Act (ADA), and third-party funded projects).*

Green Schoolyards Improvement Projects (Non-DSA)

Project Scope/Background: In addition to Green Schoolyard Upgrade Projects, Green Schoolyard Improvement Projects will be undertaken at 34 sites with \$39,500,000 of Restricted General Fund-ELOP. These projects were identified in Summer 2023, in order to utilize, to the extent possible, funding that expires on June 30, 2024. This was prior to the development of the Green Schoolyards Index, and work has already begun. The scope of the projects consists of new plantings, trees, turf, and/or decomposed granite within existing or new planting areas, and thus will not require Division of the State Architect (DSA) approval. Based on the scoping assumptions, all projects are anticipated to significantly increase the green space, getting each school as close to 30% as feasible.

In an effort to provide a level of geographic greening equality, and recognizing there are other significant and meaningful factors beyond the condition and adequacy of school facilities, two sites were selected in each Board District (14 total) based on an assessment of elementary school sites' ranking on the Greening 1.0 Index; their 2021-22 unduplicated pupil count of free/reduced-price meals, English learners, and foster youth; and the projects planned or underway that would provide incremental greening (Outdoor Learning Environment (OLE) and PACEUP projects). Of the remaining 20 sites, 18 were identified based on the aforementioned methodology with the exclusion of geographic equality, and the remaining two were identified to address pre-existing site concerns and a reoccurring safety hazard.

The Board's authorization to execute all instruments necessary, as legally permissible, to implement the projects, including budget modifications, will help support efforts to expedite the Green Schoolyard Improvement projects (Non-DSA) at the 34 sites below.

Board District	Region	Site Name	Greening 1.0 Index Rank	Percentage of Unduplicated Pupil Count of Free/Reduced-Price Meals, English Learners & Foster Youth 2021-2022
1	South	La Salle	8	98.69%
1	South	Manhattan ES	93	97.96%
1	South	Menlo ES	37	98.60%
1	South	Woodcrest ES	60	99.15%
1	West	Wilton ES	80	95.30%
2	East	Belvedere ES	49	99.45%
2	East	Breed ES	53	97.42%
2	East	Evergreen ES	41	96.44%
2	East	Ford ES	87	95.11%
2	East	Hamasaki Magnet ES	62	92.51%
2	East	Lorena ES	62	97.92%
2	East	Marianna ES	30	96.76%
2	East	Soto ES	36	96.69%
3	North	Capistrano ES	124	75.63%
3	North	Sunny Brae ES	37	93.50%
3	West	Alta Loma ES	111	98.11%
3	West	Windsor Hills Magnet ES	644	82.71%
4	North	Garden Grove ES	225	93.40%
4	West	Stoner ES	91	91.27%
5	East	28th St. ES	43	99.03%
5	East	Hughes ES	88	94.59%
5	East	Stanford ES	51	96.48%
5	South	Norwood ES	64	96.10%
5	West	Hobart ES	84	96.26%
5	West	Hoover ES	40	99.28%
5	West	Los Angeles ES	56	98.91%
6	North	Coldwater Canyon ES	42	96.17%
6	North	Lankershim ES	86	90.99%
7	South	109th St. ES	39	96.76%
7	South	118th St. ES	71	98.65%
7	South	66th St. ES	81	98.18%
7	South	75th St. ES	33	98.15%
7	South	Griffith-Joyner ES	77	99.48%
7	South	Russell ES	92	96.56%

Initial Budget and COPs Allocation:	\$ 25,000,000
Restricted General Fund-ELOP (Allocated):	\$ 89,500,000
<u>Anticipated Future Funding Allocation(s):</u>	<u>\$ 25,000,000</u>
Total Anticipated Program Budget (all funding sources):	\$139,500,000

Program Schedule: Construction of the first project is anticipated to begin in Q1-2024 and the final project is anticipated to be completed in Q4-2027.

8. Campus Safety Systems Improvement Projects

Project Scope: Design and install new video camera and intrusion alarm systems for 719 school sites, 291 of which are included in the initial phase of this work ([site list](#)). The scope may include, but is not limited to the design and installation of video camera systems for each individual campus, based on current design standards that are specified in technical design guidelines:

- o Campus Perimeter
- o Entrance (Main, Parking)
- o Rear/Service Entrance/Delivery
- o Exterior Doors
- o Parking Structure
- o Bus Loading/Unloading Zones
- o Large Assembly Areas
- o Stairwells
- o Corridors
- o Valuable Resources (Storage)
- o Other site-specific critical areas

Each project will include approximately 20 camera locations at smaller schools and 30 camera locations at larger schools, with each consisting of three to four cameras, or a total of 60 to 120 cameras per school site. The “large and small” school designation will be determined by student enrollment, number of buildings, and campus layout.

The new system will include remote monitoring capabilities through LASPD’s Operations Center. In total, 719 sites have been identified for a project, and additional funding allocations will be required to complete all projects.

Initial Budget/COPs Allocation:	\$146,000,000
<u>Future Anticipated Funding Allocation(s):</u>	<u>\$210,000,000</u>
Total Anticipated Project Budget:	\$356,000,000

Project Schedule: Construction is anticipated to begin in Q1-2024, with the first 291 projects to be completed in Q1-2026, and the entire program of 719 sites anticipated to be completed in Q4-2028.

9. Cybersecurity Improvement Program

Project Scope: Delivery of Districtwide cybersecurity enhancements that address vulnerabilities identified in the 2021 Information Security Audit as well as recommendations from the Cybersecurity Task Force, which was convened in the wake of the September 2022 cyber-attack. The Cybersecurity Improvement Program includes augmentation of people, processes, and technology tools to identify and mitigate the risk of future cyber-attacks and disruption to District operations, requiring capital and reoccurring operational expenditures. The capitalizable scope may include, but is not limited to:

- o *Enhancing Network Security Models, including Identity Management to Control Account Access and Manage Digital Identities:* Implement a centralized system to manage the lifecycle of user accounts required to access District applications, including access and authorization management. This effort will modernize the current decentralized systems for managing user account passwords and workflow-based authorizations.
- o *Cloud Migration of Core Assets and Applications:* Migrate on-site core applications, including the District's enterprise resource planning tool (SAP), Student Information System (MiSiS), Special Education System (Welligent), Food Services, Transportation, and others, to the Cloud to achieve a better security posture, reduce down-time, and enhance systems' performance.
- o *Redesign and Hardening of Network Architecture and Infrastructure:* Install and implement modern Data Center firewalls and segment critical applications to inspect and block potentially malicious traffic and insider threats.
- o *Vulnerability Assessment and Threat Management for Protection and Detection:* Configure security tools for recurring enterprise-level scans of critical systems and applications to support identification, classification, prioritization, remediation, and mitigation of vulnerabilities.
- o *Security Operations Center:* Centralize application and system security alerts that may be indicators of compromise, or malicious activities. Implementation of an Artificial Intelligence platform that supports a 24x7x365 security operations center to monitor security alerts and take action as deemed necessary.

The Cybersecurity Improvement Program will be executed in multiple phases, with the first phase focused on the highest priority actions to elevate the District's security posture per Audit and Task Force findings.

Initial Budget and COPs Allocation:	\$ 72,517,106
<u>Future Anticipated Funding Allocation(s):</u>	<u>\$109,242,394</u>
Total Anticipated Capital Program Budget:	\$181,759,500

Full implementation of the Cybersecurity Improvement Program is currently estimated to require \$88,258,550 of General Funds and is included in the Capital Plan.

Project Schedule: Implementation began in Q2-2023 and is anticipated to be completed in Q2-2026.



Board of Education Report

File #: Rep-094-22/23, **Version:** 1

Define and Approve Two Early Education Center Outdoor Classroom Projects and Amend the Facilities Services Division Strategic Execution Plan to Incorporate Therein

December 13, 2022

Facilities Services Division and Early Childhood Education Division

Action Proposed:

Define and approve two Early Education Center (EEC) outdoor classroom projects at the following schools and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein. The total combined budget for the projects, as described in Attachment A is \$824,957.

1. Gratts Early Education Center
2. Estrella Early Education Center

Authorize the Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the proposed projects, including budget modifications and the purchase of equipment and materials.

Background:

The Los Angeles Unified School District (Los Angeles Unified or District) School Upgrade Program includes a spending target entitled "Early Childhood Education Facilities Upgrades and Expansions." Projects developed under this category of need are included in the Facilities Services Division Strategic Execution Plan.

The two outdoor classroom projects will create dynamic, nature-based outdoor learning spaces to enable the District's youngest learners to acquire a deep, intuitive understanding of the natural world through hands-on experiences. Each outdoor classroom may include a number of learning stations with the following components:

- Music and movement learning station
- Climbing and balance learning station
- Messy materials learning station
- Nature art learning station
- Water play learning station
- Sand play learning station
- Garden learning station
- Dirt Digging learning station
- Building materials learning station

Expected Outcomes:

Staff anticipates the Board of Education will define and approve two EEC outdoor classroom projects, as described in Attachment A, and amend the Facilities SEP to incorporate therein. Approval will authorize staff to proceed with the implementation of the proposed projects.

Board Options and Consequences:

Adoption of the proposed action will authorize staff to proceed with the expenditure of Bond Program funds to implement the proposed projects. If the proposal is not approved, Bond Program funds will not be expended, access to nature-based green space will remain limited, and early education facilities needs will remain unaddressed.

Policy Implications:

This action is consistent with the District's commitment to address unmet school facilities needs and provide students with a safe and healthy learning environment.

Budget Impact:

The total combined budget for the projects is \$824,957. The projects will be funded with Bond Program funds earmarked specifically for Early Childhood Education facilities upgrades and expansions.

Each project budget was prepared based on the current information known and assumptions about the project scope, site conditions, and market conditions. Individual project budgets will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise and will be adjusted accordingly to enable the successful completion of each project.

Student Impact:

The two outdoor classroom projects will establish nurturing, nature-based outdoor spaces that support whole-child development and learning, as well as address early education facilities needs that are necessary to improve student health, safety, and educational quality to benefit approximately 183 students.

Expected developmental outcomes include enhanced imaginative play, increased physical and mental well-being, and environmental stewardship. These outdoor classrooms will encourage and support community, student, and parent engagement through the creation of partnerships that help establish and maintain the newly developed garden spaces. These spaces can also reduce stress for staff, families, and children. Children and their parents will be able to connect with the natural world as a regular part of their healthy growth and development in the areas that lack parks and green environments.

Equity Impact:

Not Applicable

Issues and Analysis:

Staff's proposal supports the Early Childhood Education Division's commitment to providing a quality early education experience that will prepare students for success in school and life, while valuing and respecting the needs, languages, and cultures of all students, families, staff, and respective communities.

The proposed projects were identified by the Early Childhood Education Division in consultation with Local District and school site administrators. Sites were selected based upon each center's proximity and access to existing community green space, and evidence of parent, administrator, and staff commitment to the success of

File #: Rep-094-22/23, **Version:** 1

the program. Other factors considered included income level, center enrollment, community interest, and demographics.

The Office of Environmental Health and Safety will evaluate the project proposals in accordance with the California Environmental Quality Act to ensure compliance. If, through the planning and design process, it is determined that the proposed project scopes will not sufficiently address the facilities needs identified, the project scope, schedule, and budget will be revised accordingly.

Bond Oversight Committee Recommendation:

This item was considered by the School Construction Bond Citizens' Oversight Committee (BOC) at its meeting on November 3, 2022. Staff has concluded that this proposed Facilities SEP amendment is in alignment with BOC recommendations and will facilitate Los Angeles Unified's ability to successfully implement the Facilities SEP.

Attachments:

Attachment A - Two Early Education Center Outdoor Classroom Projects

Attachment B - BOC Resolution

Informatives:

None

Submitted:

10/27/22

File #: Rep-094-22/23, Version: 1

RESPECTFULLY SUBMITTED,

APPROVED BY:


ALBERTO M. CARVALHO
Superintendent


PEDRO SALCIDO
Deputy Superintendent,
Business Services & Operations

REVIEWED BY:

APPROVED BY:


DEVORA NAVERA REED
General Counsel
 Approved as to form.


MARK HOVATTER
Chief Facilities Executive
Facilities Services Division


REVIEWED BY:

APPROVED BY:


TONY ATIENZA
Director, Budget Services and Financial Planning
 Approved as to budget impact statement.


DEAN S. TAGAWA, EdD
Executive Director
Early Childhood Education Division

PRESENTED BY:


INDIA R. GRIFFIN
Director of Maintenance and Operations
Facilities Services Division



LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report
Attachment A

Two Early Education Center Outdoor Classroom Projects

1. Gratts Early Education Center Outdoor Classroom Project

- *Local District Central, Board District 2 – Rivas*
- *Project Scope* – This project will provide an outdoor classroom with learning stations, covering approximately 12,400 square feet. It will also provide solar reflective coating over the asphalt concrete and include the installation of shrubs, grass, and irrigation.
- *Project Budget:* \$474,707
- *Construction Schedule:* Q2 2024 – Q4 2024

2. Estrella Early Education Center Outdoor Classroom Project

- *Local District Central, Board District 7 – Ortiz Franklin*
- *Project Scope* – This project will provide an outdoor classroom with learning stations, covering approximately 5,750 square feet. It will also provide solar reflective coating over the asphalt concrete and include the installation of shrubs, trees, grass, irrigation, and a tricycle path.
- *Project Budget:* \$350,250
- *Construction Schedule:* Q2 2024 – Q4 2024

LOS ANGELES UNIFIED SCHOOL DISTRICT**SCHOOL CONSTRUCTION BOND CITIZENS' OVERSIGHT COMMITTEE****Margaret Fuentes, Chair**

LAUSD Student Parent

D. Michael Hamner, Vice-Chair

American Institute of Architects

Jennifer McDowell, Secretary

L.A. City Mayor's Office

Susan Linschoten, Executive Committee

L.A. Co. Auditor-Controller's Office

Scott Pansky, Executive Committee

L.A. Area Chamber of Commerce

Neelura Bell

CA Charter School Association

Jeffrey Fischbach

CA Tax Reform Assn.

Chris Hannan

L.A. Co. Federation of Labor AFL-CIO

Hyepin Im

L.A. City Controller's Office

Brian Mello

Assoc. General Contractors of CA

Dr. Clarence Montecarlo

Tenth District PTSA

William O. Ross, IV31st District PTSA**Samantha Rowles**

LAUSD Student Parent

Araceli Sandoval-Gonzalez

Early Education Coalition

Dolores Sobalvarro

AARP

Celia Ayala (Alternate)

Early Education Coalition

Chad Boggio (Alternate)

L.A. Co. Federation of Labor AFL-CIO

Peggy Robertson (Alternate)

Assoc. General Contractors of CA

Connie Yee (Alternate)

L.A. Co. Auditor-Controller's Office

Joseph P. Buchman – Legal Counsel

Burke, Williams & Sorensen, LLP

Lori Raineri and Keith Weaver – Oversight Consultants

Government Financial Strategies

Timothy Popejoy

Bond Oversight Administrator

Perla Zitle

Bond Oversight Coordinator

RESOLUTION 2022-47**BOARD REPORT NO. 094-22/23****RECOMMENDING BOARD APPROVAL TO DEFINE AND APPROVE TWO EARLY EDUCATION CENTER OUTDOOR CLASSROOM PROJECTS AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN**

WHEREAS, District Staff proposes the Board of Education (Board) define and approve two Early Education Center (EEC) outdoor classroom projects, as described in Board Report No. 094-22/23, and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein; and

WHEREAS, District Staff also requests that the Board authorize the Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s), to execute all instruments necessary to implement the proposed projects, including budget modifications and the purchase of equipment and materials; and

WHEREAS, The School Upgrade Program includes a spending target entitled "Early Childhood Education Facilities Upgrades and Expansions." Projects developed under this category of need are included in the Facilities SEP; and

WHEREAS, District Staff's proposal includes outdoor classroom projects at two school sites: Gratts EEC and Estrella EEC. These projects will convert existing asphalt and playground areas into dynamic nature-based learning environments; and

WHEREAS, The proposed projects were identified by the Early Childhood Education Division in consultation with Local District and school site administrators. Sites were selected based upon each center's proximity and access to existing community green space, and evidence of parent,

RESOLUTION 2022-47**RECOMMENDING BOARD APPROVAL TO DEFINE AND APPROVE TWO EARLY EDUCATION CENTER OUTDOOR CLASSROOM PROJECTS AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN**

administrator, and staff commitment to the success of the program. Other factors considered included income level, center enrollment, community interest, and demographics; and

WHEREAS, The total combined budget for the projects is \$824,957. The projects will be funded with Bond Program funds earmarked specifically for Early Childhood Education facilities upgrades and expansions; and

WHEREAS, This action is consistent with the Los Angeles Unified School District's (Los Angeles Unified or District) commitment to address unmet school facilities needs and provide students with a safe and healthy learning environment, as described in Los Angeles Unified local bond measures; and

WHEREAS, District Staff has concluded that this proposed Facilities SEP amendment will facilitate Los Angeles Unified's ability to successfully complete the Facilities SEP.

NOW, THEREFORE, BE IT RESOLVED THAT:

1. The School Construction Bond Citizens' Oversight Committee recommends that the Board of Education define and approve two EEC outdoor classroom projects, with a combined budget of \$824,957, and amend the Facilities SEP to incorporate therein, as described in Board Report No. 094-22/23, a copy of which is attached hereto in the form it was presented to the BOC and is incorporated herein by reference.
2. This resolution shall be transmitted to the Los Angeles Unified School District Board of Education and posted on the Oversight Committee's website.
3. The District is directed to track the above recommendation and to report on the adoption, rejection, or pending status of the recommendations as provided in section 6.2 of the Charter and Memorandum of Understanding between the Oversight Committee and the District.

ADOPTED on November 3, 2022, by the following vote:

AYES: 10

ABSTENTIONS: 0

NAYS: 0

ABSENCES: 5

/Margaret Fuentes/

Margaret Fuentes
Chair

/Michael Hamner/

D. Michael Hamner
Vice-Chair



Board of Education Report

File #: Rep-234-21/22, **Version:** 1

Define and Approve 11 Projects to Provide Critical Replacements and Upgrades of School Building/Site Systems and Components and Amend the Facilities Services Division Strategic Execution Plan to Incorporate Therein

March 8, 2022

Facilities Services Division

Action Proposed:

Define and approve 11 projects to provide critical replacements and upgrades of school building/site systems and components, as listed on Attachment A, and amend to the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein. The total combined budget for the 11 projects is \$1,677,001.

Authorize the Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the proposed projects, including budget modifications and the purchase of equipment and materials.

Background:

Priorities for the expenditure of capital funding are evaluated to ensure the District's most pressing priorities are being addressed. More than 70 percent of Los Angeles Unified School District (Los Angeles Unified or District) school buildings were built more than 50 years ago, and more than \$50 billion of unfunded school facilities needs have been identified Districtwide, and these needs grow every year. As the District's capital needs far exceed available funding, the most pressing unfunded critical needs will continue to be addressed based on an evaluation of known facilities conditions and needs at schools. Projects developed under this category of need, *Critical Replacements and Upgrades of School Building/Site Systems and Components*, will replace failing building systems projects that create safety concerns and are disruptive to school operations. Systems in the worst condition, especially those that pose a safety hazard and/or will negatively impact school operations and other building systems if not addressed, will be addressed first.

The project proposals contained in this Board Report align with these priorities. Attachment A includes:

- One (1) project to replace failing building systems that create safety concerns and are disruptive to school operations, and
- Ten (10) projects to provide new secure entry systems.

Expected Outcomes:

Staff anticipates that the Board of Education will define and approve 11 projects that address critical replacement and upgrade needs, and amend the Facilities SEP to incorporate therein. Approval will authorize staff to proceed with the implementation of the proposed projects to improve student health, safety and educational quality.

Board Options and Consequences:

Adoption of the proposed action will authorize staff to proceed with the expenditure of Bond Program funds to undertake the project proposals in accordance with the provisions set forth in Los Angeles Unified local bond measures K, R, Y, Q, and RR. If the proposed action is not approved, Bond Program funds will not be expended, and critical replacement and upgrade needs will remain unaddressed.

Policy Implications:

The proposal is consistent with the Los Angeles Unified's long-term goal to address unmet school facilities needs and significantly improve the conditions of aging and deteriorating school facilities as described in Los Angeles Unified local bond measures. Moreover, the proposed secure entrance projects support the *Protecting Our Students and School Sites* Board Resolution (Res-032-17/18).

Budget Impact:

The total combined budget for the 11 projects is \$1,677,001. The projects will be funded with Bond Program funds earmarked specifically for critical replacements and upgrades of school building/site systems and components.

Each project budget was prepared based on the current information known and assumptions about the project scope, site conditions, and market conditions. Individual project budgets will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise and will be adjusted accordingly to enable the successful completion of each project.

Student Impact:

Approval of the proposed projects enables the District to continue our ongoing efforts to undertake facilities improvements that help ensure students are provided with safe school environments that promote teaching and learning.

Equity Impact:

Please see attached statement.

Issues and Analysis:

It may be necessary to undertake feasibility studies, site analysis, scoping, and/or due diligence activities on the proposed projects prior to initiating design. As necessary, the Office of Environmental Health and Safety (OEHS) will evaluate the proposed projects in accordance with the California Environmental Quality Act (CEQA) to ensure compliance. If through the planning and design process it is determined that the proposed project scope(s) will not sufficiently address the critical needs identified, the project scope, schedule and budget will be revised accordingly.

Bond Oversight Committee Recommendations:

This item was considered by the School Construction Bond Citizen's Oversight Committee (BOC) at its meeting on February 24, 2022. Staff has concluded that this proposed Facilities SEP amendment is in alignment with BOC recommendations and will facilitate Los Angeles Unified's ability to successfully implement the Facilities SEP.

Attachments:

Attachment A: Projects That Address Critical Replacement and Upgrade Needs

Attachment B: BOC Resolution

File #: Rep-234-21/22, **Version:** 1

Informatives:

None.

Submitted:

2/18/22

File #: Rep-234-21/22, Version: 1

RESPECTFULLY SUBMITTED,

APPROVED BY:


ALBERTO M. CARVALHO
Superintendent
MEGAN K. REILLY
Deputy Superintendent

REVIEWED BY:

APPROVED BY:


DEVORA NAVERA REED
General Counsel
MARK HOVATTER
Chief Facilities Executive
Facilities Services Division

☒ Approved as to form.

REVIEWED BY:

PRESENTED BY:


TONY ATIENZA
Director, Budget Services and Financial Planning
ROBERT LAUGHTON
Director of Maintenance and Operations
Facilities Services Division

☒ Approved as to budget impact statement.

INTEROFFICE CORRESPONDENCE
Los Angeles Unified School District
FACILITIES SERVICES DIVISION
Equity Impact Statement**

TO: Members, Board of Education
 Alberto M. Carvalho, Superintendent

DATE: February 11, 2022

FROM: Mark Hovatter, Chief Facilities Executive

SUBJECT: BR-234-21/22 DEFINE AND APPROVE 11 PROJECTS TO PROVIDE CRITICAL REPLACEMENTS AND UPGRADES OF SCHOOL BUILDING/SITE SYSTEMS AND COMPONENTS AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN

Board Meeting Date:	3/8/2022
----------------------------	-----------------

Equity Impact				
Component	1	2	3	4
Recognition	Does not recognize historical inequities	Vaguely recognizes historical inequities	Affirmatively recognizes historical inequities	Actively recognizes and specifies historical inequities to correct
Resource Prioritization	Does not prioritize resources based on student need	Somewhat prioritizes resources based on student need	Prioritizes resources based on student need	Effectively prioritizes resources based on student need
Results	Unlikely to result in closed opportunity gaps and/or closing achievement gaps	May result in closed opportunity gaps and/or closing achievement gaps	Likely to result in closed opportunity gaps and/or closing achievement gaps	Extremely likely to result in closed opportunity gaps and/or closing achievement gaps

Component	Score	Score Rationale
Recognition	3	The proposed projects address the severe deterioration and/or inadequacy of these schools' building/site systems and components that result from historic underinvestment in District school facilities.
Resource Prioritization	4	Every student is entitled to a learning space that is safe, secure, and functional, and where school building systems are sound, efficient, and working. These projects address critical needs of core facilities where systems have failed and/or other pressing unmet school facilities needs. As the District's school facilities needs far exceed available funding, systems in the worst condition, especially those that pose a safety hazard and/or will negatively impact school operations and other building systems if not addressed, must be addressed first. A Districtwide Facilities Condition Assessment was conducted in which every building, space, and room in the District was catalogued and assessed. Building components/systems in the worst condition are prioritized first to ensure school facilities do not impair or impede students' ability to learn.

***Form to be completed for Districtwide or partial Districtwide Board Report items that expend resources.*

Component	Score	Score Rationale
Results	3	All students deserve the opportunity to learn in safe and well-maintained school facilities. Multiple aspects of the school environment support student learning and the proposed projects address the physical facilities aspect within this overall framework.
TOTAL	10	

Contact Person:	Telephone:	Email:
Andrea Reyes		andrea.reyes@lausd.net



LOS ANGELES UNIFIED SCHOOL DISTRICT

Board of Education Report

Projects That Address Critical Replacement and Upgrade Needs Attachment A

Project to Replace Failing Building Systems that Create Safety Concerns and are Disruptive to School Operations

1. Highland Park Continuation High School – Project to Provide New Heating, Ventilation and Air Conditioning Systems

- *Local District Central, Board District 2 – García*
- *Project Background and Scope* – This project is to provide new heating, ventilation, and air conditioning (HVAC) systems campus-wide.
- *Project Budget* -- \$1,322,177
- *Project Schedule* – Construction is anticipated to begin in Q3 2023 and conclude in Q1 2024.

Projects to Provide Secure Entry Systems

#	BD	LD	Cost Center	School	Project Budget	Anticipated Construction Start	Anticipated Construction Completion
1	1	West	1378101	54th St. ES	\$36,848	Q1 2022	Q2 2022
2	4	Northwest	1271201	Calvert Charter for Enriched Studies	\$38,040	Q1 2022	Q2 2022
3	1	South	1679501	Garcetti Learning Academy	\$30,764	Q1 2022	Q2 2022
4	2	East	1461601	Humphreys ES	\$52,300	Q1 2022	Q2 2022
5	3	Northwest	1488101	Limerick ES	\$31,516	Q1 2022	Q2 2022
6	3	Northwest	1544601	Napa ES	\$31,634	Q1 2022	Q2 2022
7	5	East	1237801	Nueva Vista ES	\$32,374	Q1 2022	Q2 2022
8	6	Northeast	1572601	O'Melveny ES	\$31,577	Q1 2022	Q2 2022
9	7	South	1602101	Parmelee ES	\$31,788	Q1 2022	Q2 2022
10	4	Northwest	1777401	Wilbur Charter for Enriched Academics	\$37,983	Q1 2022	Q2 2022
Total					\$354,824		

LOS ANGELES UNIFIED SCHOOL DISTRICT**SCHOOL CONSTRUCTION BOND CITIZENS' OVERSIGHT COMMITTEE**

Rachel Greene, Chair
Tenth District PTSA
Chris Hannan, Vice-Chair
L.A. Co. Federation of Labor AFL-CIO
Margaret Fuentes, Secretary
LAUSD Student Parent
Araceli Sandoval-Gonzalez, Executive Committee
Early Education Coalition
Alvin Trotter, Jr., Executive Committee
L.A. Area Chamber of Commerce

Joseph P. Buchman – Legal Counsel
Burke, Williams & Sorensen, LLP
Lori Raineri and Keith Weaver – Oversight Consultants
Government Financial Strategies

Tracy Bartley
31st District PTSA
Laura Baz
LAUSD Student Parent
Neelura Bell
CA Charter School Association
Jeffrey Fischbach
CA Tax Reform Assn.
D. Michael Hamner
American Institute of Architects
Hyejin Im
L.A. City Controller's Office
Susan Linschoten
L.A. Co. Auditor-Controller's Office
Dolores Sobalvarro
AARP

Roger Uy
Assoc. General Contractors of CA
Celia Ayala (Alternate)
Early Education Coalition
Chad Boggio (Alternate)
L.A. Co. Federation of Labor AFL-CIO
Dr. Clarence Montecarlo (Alternate)
Tenth District PTSA
Samantha Rowles (Alternate)
LAUSD Student Parent
Connie Yee (Alternate)
L.A. Co. Auditor-Controller's Office
Vacant
L.A. City Mayor's Office

Timothy Popejoy
Bond Oversight Administrator
Perla Zitle
Bond Oversight Coordinator

RESOLUTION 2022-11**BOARD REPORT NO. 234-21/22**

RECOMMENDING BOARD APPROVAL TO DEFINE AND APPROVE 11 PROJECTS TO PROVIDE CRITICAL REPLACEMENTS AND UPGRADES OF SCHOOL BUILDING/SITE SYSTEMS AND COMPONENTS AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN

WHEREAS, District Staff proposes that the Board of Education define and approve 11 projects that address critical replacement and upgrade needs at schools with a budget of \$1,677,001 (the "Projects") as described in Board Report 234-21/22 attached hereto, and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein, and authorize the Chief Procurement Officer and/or the Chief Facilities Executive, and/or their designee(s), to execute all instruments necessary to implement the Projects; and

WHEREAS, Projects developed under the School Upgrade Program category of need, Critical Replacements and Upgrades of School Building/Site Systems and Components, will replace failing building systems projects that create safety concerns and are disruptive to school operations; and

WHEREAS, The Projects are consistent with the Los Angeles Unified School District (Los Angeles Unified or District)'s long-term goal to address unmet school facilities needs and significantly improve the conditions of aging and deteriorating school facilities as described in Los Angeles Unified local bond measures; and

WHEREAS, District Staff has determined that the Projects are necessary to improve student health, safety and educational quality; and

Bond Oversight Committee

333 S. Beaudry Avenue, 23rd Floor, Los Angeles, CA 90017 ♦ Phone: 213. 241.5183 ♦ www.laschools.org/bond

RESOLUTION 2022-11**RECOMMENDING BOARD APPROVAL TO DEFINE AND APPROVE 11 PROJECTS TO PROVIDE CRITICAL REPLACEMENTS AND UPGRADES OF SCHOOL BUILDING/SITE SYSTEMS AND COMPONENTS AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN**

WHEREAS, the Board of Education's approval of the Projects will authorize District Staff to proceed with the expenditure of bond funds to undertake the Projects in accordance with the provisions set forth in Los Angeles Unified local bond measures K, R, Y, Q, and RR; and

WHEREAS, District staff has concluded that this proposed Facilities SEP amendment will facilitate Los Angeles Unified's ability to successfully complete the Facilities SEP.

NOW, THEREFORE, BE IT RESOLVED THAT:

1. The School Construction Citizens' Bond Oversight Committee recommends that the Board of Education define and approve 11 projects that address critical replacement and upgrade needs at schools, with a combined budget of \$1,677,001, and amend the Facilities SEP to incorporate therein, as described in Board Report 234-21/22, a copy of which is attached hereto in the form it was presented to the BOC and is incorporated herein by reference.
2. This resolution shall be transmitted to the Los Angeles Unified School District Board of Education and posted on the Oversight Committee's website.
3. The District is directed to track the above recommendation and to report on the adoption, rejection, or pending status of the recommendations as provided in section 6.2 of the Charter and Memorandum of Understanding between the Oversight Committee and the District.

ADOPTED on February 24, 2022, by the following vote:

AYES: 11

ABSTENTIONS: 0

NAYS: 0

ABSENCES: 3

/Rachel Greene/

Rachel Greene
Chair

/Margaret Fuentes/

Margaret Fuentes
Secretary



Board of Education Report

File #: Rep-075-22/23, **Version:** 1

Approve the Definition of Five Outdoor Learning Environment Projects and Amend the Facilities Services Division Strategic Execution Plan to Incorporate Therein
December 13, 2022
Facilities Services Division

Action Proposed:

Approve the definition of five outdoor learning environment projects at 52nd Street Elementary School, Birdielee V. Bright Elementary School, Commonwealth Avenue Elementary School, Humphreys Avenue Elementary School, and Lockwood Avenue Elementary School, as described in Exhibit A, and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein. The combined budget for the five outdoor learning environment projects is \$11,894,670.

Authorize the Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the projects including budget modifications.

Background:

On August 24, 2021, the Board of Education (Board) adopted an update to the School Upgrade Program (SUP) to integrate Measure RR funding and priorities into its operational framework and approved the Measure RR Implementation Plan (Implementation Plan) to help guide the identification of sites and development of project proposals (Board Report No. 027-21/22). The Implementation Plan included, among other things, the development of Safe and Welcoming Outdoor Learning Spaces Projects, also referred to as Outdoor Learning Environment Projects (Project).

The proposed Projects include, but are not limited to, removal of excess relocatable buildings and adjacent asphalt to provide additional green space on the school by constructing an approximately 2,000 square foot outdoor learning space with landscaping, shaded seating areas, shade structure, internet connectivity, sink if infrastructure is already in place, and accessibility improvements.

The proposed Projects are identified utilizing the Los Angeles Unified Greening Index (Greening Index) for a ranking of campuses with the greatest need for enhanced greening and the application of Electronic Capacity Assessment Review (ECAR) data to determine campuses with excess portable classrooms that can be removed without a demand to replace the classroom capacity.

The Greening Index was developed utilizing data measuring two types of need:

1. Community-based need was measured using data from the Los Angeles Countywide Parks and Recreation Needs Assessment, a comprehensive study of the diverse parks and recreation facilities throughout LA County's cities and unincorporated communities, prepared by the Los Angeles County Department of Parks and Recreation.

2. Los Angeles Unified's campus specific need was measured by the percentage of hardscape versus greenspace within each school site excluding high school athletic fields.

Expected Outcomes:

Approval of the proposed five outdoor learning environment project definitions, and amendment to the Facilities SEP to incorporate therein. The approval will enable staff to proceed with the design and construction of the proposed Projects.

Board Options and Consequences:

Adoption of the proposed action will authorize staff to proceed with the expenditure of Bond Program funds and begin the environmental reviews and clearances, design, procurement, construction, and other activities necessary to implement the proposed Projects.

If the proposal is not approved, the activities discussed above will not commence and the schools will not benefit from the creation of these outdoor learning spaces being proposed.

Policy Implications:

The proposal does not impact Los Angeles Unified policy. It furthers implementation of the update to the SUP to integrate Measure RR funding and priorities into its operational framework (Board Report No. 027-21/22) adopted by the Board on August 24, 2021. Furthermore, the proposal is consistent with the District's long-term goal to address unmet school facilities needs, improve the conditions of aging and deteriorating school facilities, and provide students with safe and healthy outdoor learning environments. The action aligns with the Green Schools for All: Equitable Funding and Expansion of Green Spaces across District Campuses Board Resolution (Res 002-22/23), adopted on September 27, 2022, that reinforces Los Angeles Unified's commitment to creating green learning spaces.

Budget Impact:

The combined project budget for the five outdoor learning environment projects is \$11,894,670. The Projects will be funded by Bond Program funds in the School Upgrade Program targeted for major modernizations, upgrades, and reconfiguration to school campuses.

The project budgets were prepared based on the current information known, and assumptions about the project scope, site conditions, and market conditions. The project budgets will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise and will be adjusted accordingly to enable the successful completion of the proposed Projects.

Student Impact:

The outdoor learning environments projects, once completed, will help ensure that approximately 2,243 students attending these five schools are provided with safe, welcoming, and sustainable outdoor learning environments that support student-centered, experiential, and engaged learning.

Equity Impact:

Not Applicable.

Issues and Analysis:

The intent of the outdoor learning environment projects is to provide safe, welcoming, and sustainable outdoor learning environments at schools most in need of greening resources to support instruction.

The principal project planning tenets are:

1. Design, size, and elements vary across elementary, middle, and high schools.
2. Accommodate general classroom use for cross disciplinary lessons.
3. Provide informal gathering spaces and/or play spaces for elementary school.
4. Provide overflow seating for nearby library/multipurpose rooms.
5. Provide space for outdoor performances/speakers.
6. Provide outdoor study areas adjacent to classrooms.
7. Planted areas may be utilized by class curriculum.

Bond Oversight Committee Recommendations:

This item was considered by the School Construction Bond Citizens' Oversight Committee (BOC) at its meeting on November 3, 2022. Staff has concluded that this proposed Facilities SEP amendment is in alignment with BOC recommendations and will facilitate Los Angeles Unified's ability to successfully complete the Facilities SEP.

Attachments:

Attachment A - Scope, Budget, and Schedule for Five Outdoor Learning Environment Projects

Attachment B - BOC Resolution

Informatives:

None

Submitted:

11/30/22

File #: Rep-075-22/23, Version: 1

RESPECTFULLY SUBMITTED,

APPROVED BY:



ALBERTO M. CARVALHO
Superintendent



PEDRO SALCIDO
Deputy Superintendent,
Business Services & Operations

REVIEWED BY:

APPROVED BY:



DEVORA NAVERA REED
General Counsel



MARK HOVATTER
Chief Facilities Executive
Facilities Services Division

☒ Approved as to form.

REVIEWED BY:

PRESENTED BY:



TONY ATIENZA
Director, Budget Services and Financial Planning



AARON BRIDGEWATER
Director of Facilities Planning & Development
Facilities Services Division

☒ Approved as to budget impact statement.



LOS ANGELES UNIFIED SCHOOL DISTRICT

Board of Education Report

Attachment A

Scope, Budget, and Schedule for Five Outdoor Learning Environment Projects

1. 52nd Street Elementary School Outdoor Learning Environment Project

South Mid-City Community of Schools, Local District West, Board District 1 (Dr. George McKenna)

Project Background and Scope: 52nd Street Elementary School serves students in pre-kindergarten through 5th grade. As of the 2021-2022 Electronic Capacity Assessment Review (E-CAR), the school served 581 students. 52nd Street ES is a historically significant school site.

The project includes, but is not limited to:

- Removal of one bungalow building (2 classrooms) and adjacent asphalt.
- Construction of an approximately 2,000 square foot outdoor learning space.
- Landscaping.
- Shaded seating areas.
- Shade structure.
- Internet connectivity.
- Sink – if infrastructure is already in place.
- Improvements to ensure compliance with local, state, and federal requirements including from the Americans with Disabilities Act (ADA), Division of the State Architect (DSA), California Environmental Quality Act (CEQA) and Department of Toxic Substances Control (DTSC).

Project Budget: \$2,032,616

Project Schedule: Construction is anticipated to begin in Q2-2024 and be completed in Q3-2025.



LOS ANGELES UNIFIED SCHOOL DISTRICT

Board of Education Report

Attachment A

Scope, Budget, and Schedule for Five Outdoor Learning Environment Projects

2. Birdielee V. Bright Elementary School Outdoor Learning Environment Project

LA Mid-City Community of Schools, Local District West, Board District 1 (Dr. George McKenna)

Project Background and Scope: Birdielee V. Bright Elementary School serves students in kindergarten through 5th grade. As of the 2021-2022 E-CAR, the school served 401 students.

The project includes, but is not limited to:

- Removal of one bungalow building (3 classrooms) and adjacent asphalt.
- Construction of an approximately 4,000 square foot outdoor learning space and a 14,600 square feet grass field.
- Landscaping.
- Shaded seating areas.
- Shade structure.
- Internet connectivity.
- Sink – if infrastructure is already in place.
- Improvements to ensure compliance with local, state, and federal requirements including from the ADA, DSA, CEQA and DTSC.

Project Budget: \$3,532,341

Project Schedule: Construction is anticipated to begin in Q2-2024 and be completed in Q4-2025.



LOS ANGELES UNIFIED SCHOOL DISTRICT

Board of Education Report

Attachment A

Scope, Budget, and Schedule for Five Outdoor Learning Environment Projects

3. Commonwealth Avenue Elementary School Outdoor Learning Environment Project

MacArthur Park Community of Schools, Local District Central, Board District 2 (Rocio Rivas)

Project Background and Scope: Commonwealth Avenue Elementary School serves students in pre-kindergarten through 5th grade. As of the 2021-2022 E-CAR, the school served 473 students.

The project includes, but is not limited to:

- Removal of one bungalow building (2 classrooms) and adjacent asphalt.
- Construction of an approximately 2,000 square foot outdoor learning space.
- Landscaping.
- Shaded seating areas.
- Shade structure.
- Internet connectivity.
- Sink – if infrastructure is already in place.
- Improvements to ensure compliance with local, state, and federal requirements including from the ADA, DSA, CEQA and DTSC.

Project Budget: \$2,032,616

Project Schedule: Construction is anticipated to begin in Q2-2024 and be completed in Q3-2025.



LOS ANGELES UNIFIED SCHOOL DISTRICT

Board of Education Report

Attachment A

Scope, Budget, and Schedule for Five Outdoor Learning Environment Projects

4. Humphreys Avenue Elementary School Outdoor Learning Environment Project

East Los Angeles Community of Schools, Local District East, Board District 2 (Rocio Rivas)

Project Background and Scope: Humphreys Avenue Elementary School serves students in pre-kindergarten through 5th grade. As of the 2021-2022 E-CAR, the school served 436 students. Humphreys Avenue Elementary School is a historically significant school site.

The project includes, but is not limited to:

- Removal of one bungalow building (2 classrooms) and adjacent asphalt.
- Construction of an approximately 2,000 square foot outdoor learning space.
- Landscaping.
- Shaded seating areas.
- Shade structure.
- Internet connectivity.
- Sink – if infrastructure is already in place.
- Improvements to ensure compliance with local, state, and federal requirements including from the ADA, DSA, CEQA and DTSC.

Project Budget: \$2,032,616

Project Schedule: Construction is anticipated to begin in Q2-2024 and be completed in Q3-2025.



LOS ANGELES UNIFIED SCHOOL DISTRICT Board of Education Report

Attachment A

Scope, Budget, and Schedule for Five Outdoor Learning Environment Projects

5. Lockwood Avenue Elementary School Outdoor Learning Environment Project

Glassell Park/Los Feliz Community of Schools, Local District Central, Board District 2 (Rocio Rivas)

Project Background and Scope: Lockwood Avenue Elementary School serves students in pre-kindergarten through 6th grade. As of the 2021-2022 E-CAR, the school served 352 students. Lockwood Avenue Elementary School is a historically significant school site.

The project includes, but is not limited to:

- Removal of two portable buildings (4 classrooms) and adjacent asphalt.
- Construction of an approximately 2,000 square foot outdoor learning space.
- Landscaping.
- Shaded seating areas.
- Shade structure.
- Internet connectivity.
- Sink – if infrastructure is already in place.
- Improvements to ensure compliance with local, state, and federal requirements including from the ADA, DSA, CEQA and DTSC.

Project Budget: \$2,264,481

Project Schedule: Construction is anticipated to begin in Q2-2024 and be completed in Q4-2025.

LOS ANGELES UNIFIED SCHOOL DISTRICT

SCHOOL CONSTRUCTION BOND CITIZENS' OVERSIGHT COMMITTEE

Margaret Fuentes, Chair

LAUSD Student Parent

D. Michael Hamner, Vice-Chair

American Institute of Architects

Jennifer McDowell, Secretary

L.A. City Mayor's Office

Susan Linschoten, Executive Committee

L.A. Co. Auditor-Controller's Office

Scott Pansky, Executive Committee

L.A. Area Chamber of Commerce

Neelura Bell

CA Charter School Association

Jeffrey Fischbach

CA Tax Reform Assn.

Chris Hannan

L.A. Co. Federation of Labor AFL-CIO

Hyepin Im

L.A. City Controller's Office

Brian Mello

Assoc. General Contractors of CA

Dr. Clarence Monteclaro

Tenth District PTSA

William O. Ross, IV31st District PTSA**Samantha Rowles**

LAUSD Student Parent

Araceli Sandoval-Gonzalez

Early Education Coalition

Dolores Sobalvarro

AARP

Celia Ayala (Alternate)

Early Education Coalition

Chad Boggio (Alternate)

L.A. Co. Federation of Labor AFL-CIO

Peggy Robertson (Alternate)

Assoc. General Contractors of CA

Connie Yee (Alternate)

L.A. Co. Auditor-Controller's Office

Joseph P. Buchman – Legal Counsel

Burke, Williams & Sorensen, LLP

Lori Raineri and Keith Weaver – Oversight**Consultants**

Government Financial Strategies

Timothy Popejoy

Bond Oversight Administrator

Perla Zitle

Bond Oversight Coordinator

RESOLUTION 2022-48

BOARD REPORT 075-22/23

RECOMMENDING BOARD APPROVAL OF THE DEFINITION OF FIVE OUTDOOR LEARNING ENVIRONMENT PROJECTS AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN

WHEREAS, District Staff proposes that the Board of Education (Board) approve the definition of five outdoor learning environment projects at 52nd Street Elementary School, Birdielee V. Bright Elementary School, Commonwealth Elementary School, Humphreys Avenue Elementary School, and Lockwood Avenue Elementary School (Project), as described in Exhibit A to Board Report No. 075-22/23, amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein, and authorize the Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the projects including budget modifications; and

WHEREAS, The proposed Projects include, but are not limited to, removal of excess relocatable buildings and adjacent asphalt to provide additional green space on the school by constructing an approximately 2,000 square foot outdoor learning space with landscaping, shaded seating areas, shade structure, internet connectivity, sink if infrastructure is already in place, and accessibility improvements; and

WHEREAS, The proposed Projects are identified utilizing the Los Angeles Unified Greening Index (Greening Index) for a ranking of campuses with the greatest need for enhanced greening and the application of Electronic Capacity Assessment Review (ECAR) data to determine campuses with excess portable classrooms that can be removed without a demand to replace the classroom capacity; and

WHEREAS, The Greening Index was developed utilizing data measuring two types of need:

RESOLUTION 2022-48**RECOMMENDING BOARD APPROVAL OF THE DEFINITION OF FIVE OUTDOOR LEARNING ENVIRONMENT PROJECTS AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN**

1. Community-based need was measured using data from the Los Angeles Countywide Parks and Recreation Needs Assessment, a comprehensive study of the diverse parks and recreation facilities throughout LA County's cities and unincorporated communities, prepared by the Los Angeles County Department of Parks and Recreation.
2. Los Angeles Unified's campus specific need was measured by the percentage of hardscape versus greenspace within each school site excluding high school athletic fields

WHEREAS, The combined budget for the five outdoor learning environment projects is \$11,894,670 and will be funded by Bond Program funds targeted in the School Upgrade Program for major modernizations, upgrades, and reconfigurations to school campuses; and

WHEREAS, District Staff has concluded that this proposed Facilities SEP amendment will facilitate Los Angeles Unified's ability to successfully complete the Facilities SEP.

NOW, THEREFORE, BE IT RESOLVED THAT:

1. The School Construction Bond Citizens' Oversight Committee recommends that the Board of Education approve the definition of five outdoor learning environment projects at 52nd Street Elementary School, Birdielee V. Bright Elementary School, Commonwealth Elementary School, Humphreys Avenue Elementary School, and Lockwood Avenue Elementary School with a combined budget of \$11,894,670, and amend the Facilities SEP to incorporate therein, as described in Board Report No. 075-22/23, a copy of which is attached hereto in the form it was presented to the BOC and is incorporated herein by reference.
2. This resolution shall be transmitted to the Los Angeles Unified School District Board of Education and posted on the Oversight Committee's website.
3. The District is directed to track the above recommendation and to report on the adoption, rejection, or pending status of the recommendations as provided in section 6.2 of the Charter and Memorandum of Understanding between the Oversight Committee and the District

ADOPTED on November 3, 2022, by the following vote:

AYES: 10

ABSTENTIONS: 0

NAYS: 0

ABSENCES: 5

/Margaret Fuentes/

Margaret Fuentes
Chair

/Michael Hamner/

D. Michael Hamner
Vice-Chair



Board of Education Report

File #: Rep-281-22/23, Version: 2

Approve the Redefinition of the Fairfax High School Major Modernization Project, the Definition of the James J. McBride Special Education Center - Career and Transition Center West / Grand View Boulevard Elementary School Campus Improvement Project, and Amend the Facilities Services Division Strategic Execution Plan to Incorporate Therein

June 13, 2023

Facilities Services Division

Action Proposed:

Approve the redefinition of the Fairfax High School Major Modernization Project, define the James J. McBride Special Education Center - Career and Transition Center West / Grand View Boulevard Elementary School Campus Improvement Project, and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein as follows:

1. Fairfax High School Major Modernization Project (FHS Project):

The Board of Education (Board) previously approved site due diligence, planning, and feasibility activities for the FHS Project. The redefinition action, if approved, will incorporate the full scope, budget, and schedule required to address the most critical physical conditions and essential safety issues at the school site. The FHS Project includes but is not limited to:

- Construction of approximately five specialty classrooms and support spaces, new gymnasium, and new maintenance and operations building.
- Demolition of the existing gymnasium, shop building, and maintenance and operations building.
- Exterior painting of all remaining buildings to provide a uniform appearance.
- Associated landscape, hardscape, parking improvements, and infrastructure upgrades including, but not limited to, sanitary sewer, water, storm water, and electrical utilities.
- Interim facilities, as required.
- Requirements from the Americans with Disabilities Act (ADA), Division of the State Architect (DSA), California Environmental Quality Act (CEQA), Department of Toxic Substances Control (DTSC), or other improvements to ensure compliance with local, state, and federal requirements.
- The third-party funded DSA-approved design for the New Art Gallery and Classroom Building in the construction bid documents as an alternate. Construction authorization is contingent on the identification of funding, which could include external and/or District sources.

The budget for the redefined FHS Project is \$148,789,344. Construction is anticipated to begin in the second quarter of 2026 and be completed in the fourth quarter of 2029.

2. James J. McBride Special Education Center - Career and Transition Center West / Grand View Boulevard Elementary School Campus Improvement Project (Campus Improvement Project):

The Campus Improvement Project supports the unification of Career and Transition Center West (CTC West) with the James J. McBride Special Education Center (McBride). The facilities improvements provided by the Campus Improvement Project are necessary to relocate CTC West from the Fairfax High School campus to McBride. The Campus Improvement Project includes consolidating the adjacent Grand View Boulevard Elementary School (Grand View) Extended Transitional Kindergarten (ETK)/Transitional Kindergarten (TK) through 5th grade programs on the Grand View west site and creating a boundary between McBride/CTC West and Grand View. The Campus Improvement Project includes, but is not limited to:

- Construction of an approximately 3,000 square foot lunch shelter, renovation of classrooms and restrooms, and site fencing/gates and storm/sewer infrastructure upgrades to accommodate the relocated CTC West programs.
- Upgrade existing classrooms to support relocated elementary grade classes, address uncertified/deteriorated relocatable buildings, remove two classrooms in relocatable buildings, and install one new modular building with two classrooms, restrooms, and storage space to support the students with extensive needs, and upgrade outdoor areas with green landscaping to accommodate the consolidation of Grand View.
- Upgrade portions of the Grand View north parking lot to replace parking in the Grand View south parking lot.
- Provide chain link fencing and gates between McBride/CTC West and Grand View.
- Associated landscape, hardscape, and utilities improvements.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

The proposed Campus Improvement Project budget is \$16,912,842. Construction is anticipated to begin in the second quarter of 2025 and be completed in the second quarter of 2026.

Authorize the Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the projects including budget modifications.

Background:

On August 24, 2021, the Board adopted an update to the School Upgrade Program (SUP) to integrate Measure RR funding and priorities into its operational framework and approved the Measure RR Implementation Plan (Implementation Plan) to help guide the identification of sites and development of project proposals. The Implementation Plan included, among other things, the development of seven major modernization projects, one in each Board District, and funding identified for projects that either upgrade and/or alter school facilities to support efforts to realign and/or unify schools and programs.

On October 12, 2021, the Board approved the project definition for the due diligence, planning, and feasibility activities necessary to propose scope recommendations, budget, and schedule for a major modernization project at Fairfax High School. In the first quarter of 2022, staff commenced studying the site's physical conditions by gathering and analyzing significant data and information including, but not limited to, seismic and historic evaluations, site surveys and infrastructure analysis (including topographic, geological, and utility surveys), and educational programming.

CTC West is currently co-located on the Fairfax High School site and provides the transition program for

students in Region West who are on the alternate curriculum and have completed four years of high school. The CTC West and McBride programs are operated by the same administration with shared operational resources. Grand View provides inclusive programming for elementary aged students on an alternate curriculum.

Fairfax High School is located within the boundaries of Fairfax Community of Schools, Region West, and Board District 4 (Nick Melvoin) and provides a 9th - 12th grade high school program. The site spans 23.63 acres and has two portable buildings and 11 permanent buildings including three buildings listed or eligible for listing on the Assembly Bill 300 2002 Seismic Safety Inventory of California Public Schools Report (AB300 List). Two buildings, the Auditorium Building constructed in 1923 and the Administration and Classroom Building constructed in 1969, are individually eligible for listing in the California Register and for designation in the City of Los Angeles. A portion of the campus has been identified eligible as a historic district consisting of nine contributing buildings, two contributing arcades, and three contributing courtyards with a period of significance from 1967-1969. The buildings were constructed between 1923 and 1969. As of the 2022-2023 Electronic Capacity Assessment Review (E-CAR), the school served 1640 students and the projected enrollment for planning purposes is 1800 students.

McBride is located within the boundaries of Venice Community of Schools, Region West, and Board District 4 and provides a 6th - 12th grade special education program. As of the 2022-2023 E-CAR, the school served 28 students.

CTC West is located within the boundaries of Venice Community of Schools, Region West, and Board District 4 and currently provides programming on the Fairfax High School campus for 120 students.

Grand View is located within the boundaries of Venice Community of Schools, Region West, and Board District 4 and provides an ETK/TK - 5th grade elementary school program. As of the 2022-2023 E-CAR, the school served 504 students.

Bond Oversight Committee Recommendations:

This item was considered by the School Construction Bond Citizens' Oversight Committee (BOC) at its meeting on May 18, 2023. Staff has concluded that this proposed Facilities SEP amendment is in alignment with BOC recommendations and will facilitate Los Angeles Unified's ability to successfully complete the Facilities SEP.

Expected Outcomes:

Approval of the proposed FHS Project redefinition, Campus Improvement Project definition, and amendment to the Facilities SEP to incorporate therein. The approval will enable staff to proceed with the implementation of the proposed projects and realign the programs on each school site to further support the instructional programs and school operations.

The projects, once completed, will help ensure that students attending these schools are provided with safe and healthy environments that promote learning. The projects will also decrease the demand for repair and maintenance and alleviate the burden placed on school-site administration and custodial staff. While the projects are underway, the local economy will benefit from tax revenue and new jobs.

Board Options and Consequences:

Adoption of the proposed action will authorize staff to proceed with the expenditure of Bond Program funds and begin the environmental reviews and clearances, design, procurement, and other activities necessary to implement the proposed projects.

If staff's proposal is not approved, the activities discussed above will not commence and Fairfax High School will continue to operate with buildings, grounds, and site infrastructure that have critical physical conditions that may pose a health and safety risk; limit or constrain program accessibility; or negatively impact the school's ability to deliver the instructional program or operate efficiently. Additionally, students attending CTC West and McBride will not benefit from the efficiency of shared resources and administrators provided by the reconfiguration of their programs on a single site. Grand View will not benefit from a consolidation of their classroom spaces and the upgrades to classrooms for students with extensive needs. Furthermore, students, staff, and the community will not benefit from the significant proposed facilities improvements.

Policy Implications:

The proposal does not impact Los Angeles Unified policy. It furthers implementation of the update to the SUP to integrate Measure RR funding and priorities into its operational framework. Furthermore, the proposal is consistent with the District's long-term goal to address unmet school facilities needs and significantly improve the conditions of aging and deteriorating school facilities as described in the District's local bond measures K, R, Y, Q, and RR.

Budget Impact:

The combined budget for the projects is \$165,702,186. The projects will be funded by Bond Program funds targeted in the SUP for major modernizations, upgrades, and reconfigurations to school campuses.

The project budgets were prepared based on the current information known, and assumptions about the project scopes, site conditions, and market conditions. The project budgets will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise and will be adjusted accordingly to enable the successful completion of the projects.

Student Impact:

The major modernization project, once completed, will help ensure that students attending Fairfax High School are provided with a safe and healthy environment that promotes learning. Additionally, students attending CTC West and McBride will benefit from the reconfiguration of their programs on a single site, sharing resources and administrators, and the facilities upgrades to support their specialized programs. Grand View will benefit from the consolidation of their classroom spaces and the facilities improvements to provide new classrooms and support spaces for students with extensive needs.

Equity Impact:

The intent of the major modernization project is to address buildings and grounds that pose a safety concern and have the greatest need for upgrades with emphasis placed on seismic safety, reducing Los Angeles Unified's reliance on relocatable buildings, and addressing the most critical/severe physical conditions. While the project may be extensive in nature, less critical items may not be addressed. This approach allows the District to reach more schools with the limited funding available.

Issues and Analysis:

Fairfax High School currently has 112 classrooms per the 2022-23 E-CAR including 11 classrooms occupied by CTC West. The FHS Project includes the demolition of the shop building, which currently houses Fairfax High School's weight room, dance room, drama classroom, ceramics, instrumental music, sports medicine, and six classrooms occupied by CTC West. The FHS Project will demolish the shop building and replace the specialty classrooms in new buildings, and the Campus Improvement Project will provide the facilities improvements necessary to allow for CTC West to relocate and unify with McBride.

The Grand View instructional programs currently located on the Grand View east site will be relocated to new and existing spaces on the Grand View west site allowing for CTC West to relocate to the Grand View east portion of the site. The Community of Schools Administrator Offices and non-Grand View programs will no longer be allocated space at Grand View to facilitate the capacity needs required by the reconfiguration.

The recommended scope, schedule and budget for the design and construction of the proposed major modernization project at Fairfax High School was developed based on lessons learned from developing previous modernization projects, the Core Principles to Scoping Major Modernization Projects (Core Principles), and DSA directives. Utilizing the Core Principles helps ensure a consistent, transparent, and equitable approach in the planning, design, and construction of major modernization projects. Staff applied the Core Principles and considered the school site's most critical and significant issues, the opportunity to make the greatest improvement to the school site with the least amount of impact to school operations and considers the future development and improvement of the site.

The updated Core Principles are as follows:

1. Buildings meeting Assembly Bill 300 criteria for seismic evaluation may be addressed, to the extent feasible, with a focus on those determined to have a high seismic vulnerability, through retrofit, removal, or seismic modernization, which will be determined based on an assessment of the seismic vulnerability of the building(s), the historic context of the building/site, actual or potential impact to the learning environment, site layout, and the approach that best ensures compliance with DSA requirements.
2. The buildings, grounds and site infrastructure that have significant/severe physical conditions that already do or are highly likely in the near future to pose a health and safety risk, or negatively impact a school's ability to deliver the instructional program and/or operate may be addressed by repair or replacement.
3. The District's reliance on relocatable buildings, especially for K-12 instruction, should be reduced.
4. Necessary and prioritized upgrades will be made throughout priority school sites in order to comply with the program accessibility requirements of the ADA Title II Regulations, and the District's Self-Evaluation and Transition Plan under Title II of the ADA.
5. The exterior conditions of the school site will be enhanced including landscape and hardscape improvements around new buildings and/or areas impacted by construction and the painting of building exteriors throughout the school site.
6. Outdoor learning environments will be developed where the site layout and project planning provide the opportunity.

The FHS Project will be fully coordinated with other ongoing projects at Fairfax High School as they move forward. Staff will implement all opportunities to minimize construction impacts on the school's operations and explore design and construction cost and schedule efficiencies.

The Office of Environmental Health and Safety will evaluate the proposed projects in accordance with CEQA.

File #: Rep-281-22/23, Version: 2

Attachments:

Exhibit A - BOC Resolution

Previously adopted Board Reports referenced in the Background section:

- Adopted August 24, 2021: [Board Report No. 027-21/22](https://drive.google.com/file/d/1LJdE5OA6AmwRpIHiY7TIHh0J36i8z5XG/view?usp=sharing)
<<https://drive.google.com/file/d/1LJdE5OA6AmwRpIHiY7TIHh0J36i8z5XG/view?usp=sharing>>
- Adopted October 12, 2021: [Board Report No. 085-21/22](https://drive.google.com/file/d/1mSb_auoCgjTXx-geDugKB--go9cYmRmi/view?usp=sharing)
<https://drive.google.com/file/d/1mSb_auoCgjTXx-geDugKB--go9cYmRmi/view?usp=sharing>

Informatives:

None

Submitted:

05/11/2023

RESPECTFULLY SUBMITTED,



ALBERTO M. CARVALHO
Superintendent

APPROVED BY:



PEDRO SALCIDO
Deputy Superintendent, Business Services and Operations

REVIEWED BY:



DEVORA NAVERA REED
General Counsel


☒ Approved as to form.

APPROVED BY:



MARK HOVATTER
Chief Facilities Executive
Facilities Services Division

REVIEWED BY:



TONY ATIENZA
Director, Budget Services and Financial Planning

☒ Approved as to budget impact statement.

PRESENTED BY:



AARON BRIDGEWATER
Director of Facilities Planning & Development
Facilities Services Division

SCHOOL CONSTRUCTION BOND CITIZENS' OVERSIGHT COMMITTEE

Margaret Fuentes, Chair
 LAUSD Student Parent
D. Michael Hamner, FAIA, Vice-Chair
 American Institute of Architects
Jennifer McDowell, Secretary
 L.A. City Mayor's Office
Scott Pansky, Executive Committee
 L.A. Area Chamber of Commerce

Neelura Bell
 CA Charter School Association
Robert Campbell
 L.A. Co. Auditor-Controller's Office
Jeffrey Fischbach
 CA Tax Reform Assn.
Chris Hannan
 L.A. Co. Federation of Labor AFL-CIO
Hyepin Im
 L.A. City Controller's Office
Brian Mello
 Assoc. General Contractors of CA
Dr. Clarence Monteclaro
 Tenth District PTSA

William O. Ross IV
 31st District PTSA
Samantha Rowles
 LAUSD Student Parent
Araceli Sandoval-Gonzalez
 Early Education Coalition
Dolores Sobalvarro
 AARP
Celia Ayala (Alternate)
 Early Education Coalition
Chad Boggio (Alternate)
 L.A. Co. Federation of Labor AFL-CIO
Connie Yee (Alternate)
 L.A. Co. Auditor-Controller's Office

Joseph P. Buchman – Legal Counsel
 Burke, Williams & Sorensen, LLP
Lori Raineri and Keith Weaver – Oversight Consultants
 Government Financial Strategies Joint Powers Authority

Timothy Popejoy
 Bond Oversight Administrator
Perla Zitle
 Bond Oversight Coordinator

RESOLUTION 2023-17

BOARD REPORT 281-22/23

RECOMMENDING BOARD APPROVAL OF THE REDEFINITION OF THE FAIRFAX HIGH SCHOOL MAJOR MODERNIZATION PROJECT, THE DEFINITION OF THE JAMES J. MCBRIDE SPECIAL EDUCATION CENTER – CAREER AND TRANSITION CENTER WEST / GRAND VIEW BOULEVARD ELEMENTARY SCHOOL CAMPUS IMPROVEMENT PROJECT, AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN

WHEREAS, District Staff proposes that the Board of Education (Board) approve the redefinition of the Fairfax High School Major Modernization Project (FHS Project), define the James J. McBride Special Education Center – Career and Transition Center West / Grand View Boulevard Elementary School Campus Improvement Project (Campus Improvement Project), as described in Board Report 281-22/23, and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein, and authorize the Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the projects including budget modifications; and

WHEREAS, The budget for the redefined FHS Project is \$148,789,344. Construction is anticipated to begin in the second quarter of 2026 and be completed in the fourth quarter of 2029; and

WHEREAS, The redefinition action, if approved, will incorporate the full scope, budget, and schedule required to address the most critical physical conditions and essential safety issues at Fairfax High School. The FHS Project includes but is not limited to:

- Construction of approximately five specialty classrooms and support spaces, new gymnasium, and new maintenance and operations building.
- Demolition of the existing gymnasium, shop building, and maintenance and operations building.

RESOLUTION 2023-17**RECOMMENDING BOARD APPROVAL OF THE REDEFINITION OF THE FAIRFAX HIGH SCHOOL MAJOR MODERNIZATION PROJECT, THE DEFINITION OF THE JAMES J. MCBRIDE SPECIAL EDUCATION CENTER – CAREER AND TRANSITION CENTER WEST / GRAND VIEW BOULEVARD ELEMENTARY SCHOOL CAMPUS IMPROVEMENT PROJECT, AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN**

- Exterior painting of all remaining buildings to provide a uniform appearance.
- Associated landscape, hardscape, parking improvements, and infrastructure upgrades including, but not limited to, sanitary sewer, water, storm water, and electrical utilities.
- Interim facilities, as required.
- Requirements from the Americans with Disabilities Act (ADA), Division of the State Architect (DSA), California Environmental Quality Act (CEQA), Department of Toxic Substances Control (DTSC), or other improvements to ensure compliance with local, state, and federal requirements.

WHEREAS, The Campus Improvement Project supports the unification of Career and Transition Center West (CTC West) with the James J. McBride Special Education Center (McBride). The facilities improvements provided by the Campus Improvement Project are necessary to relocate CTC West from the Fairfax High School campus to McBride. The Campus Improvement Project includes consolidating the adjacent Grand View Boulevard Elementary School (Grand View) Extended Transitional Kindergarten (ETK)/Transitional Kindergarten (TK) through 5th grade programs on the Grand View west site and creating a boundary between McBride/CTC West and Grand View. The Campus Improvement Project includes, but is not limited to:

- Construction of an approximately 3,000 square foot lunch shelter, renovation of classrooms and restrooms, and site fencing/gates and storm/sewer infrastructure upgrades to accommodate the relocated CTC West programs.
- Upgrade existing classrooms to support relocated elementary grade classes, address uncertified/deteriorated relocatable buildings, remove two classrooms in relocatable buildings, and install one new modular building with two classrooms, restrooms, and storage space to support the students with extensive needs, and upgrade outdoor areas with green landscaping to accommodate the consolidation of Grand View.
- Upgrade portions of the Grand View north parking lot to replace parking in the Grand View reconfigured south parking lot.
- Provide chain link fencing and gates between McBride/CTC West and Grand View.
- Associated landscape, hardscape, and utilities improvements.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

The proposed Campus Improvement Project budget is \$16,912,842. Construction is anticipated to begin in the second quarter of 2025 and be completed in the second quarter of 2026; and

WHEREAS, The combined budget for the projects is \$165,702,186. The projects will be funded by Bond Program funds targeted in the SUP for major modernizations, upgrades, and reconfigurations to school campuses; and

WHEREAS, Fairfax High School currently has 112 classrooms per the 2022-23 E-CAR including 11 classrooms occupied by CTC West. The FHS Project includes the demolition of the shop building, which currently houses Fairfax High School's weight room, dance room, drama classroom, ceramics, instrumental music, sports medicine, and six classrooms occupied by CTC West. The FHS Project will demolish the shop

RESOLUTION 2023-17**RECOMMENDING BOARD APPROVAL OF THE REDEFINITION OF THE FAIRFAX HIGH SCHOOL MAJOR MODERNIZATION PROJECT, THE DEFINITION OF THE JAMES J. MCBRIDE SPECIAL EDUCATION CENTER – CAREER AND TRANSITION CENTER WEST / GRAND VIEW BOULEVARD ELEMENTARY SCHOOL CAMPUS IMPROVEMENT PROJECT, AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN**

building and replace the specialty classrooms in new buildings, and the Campus Improvement Project will provide the facilities improvements necessary to allow for CTC West to relocate and unify with McBride; and

WHEREAS, The Grand View instructional programs currently located on the Grand View east site will be relocated to new and existing spaces on the Grand View west site allowing for CTC West to relocate to the Grand View east portion of the site. The Community of Schools Administrator Offices and non-Grand View programs will no longer be allocated space at Grand View to facilitate the capacity needs required by the reconfiguration; and

WHEREAS, District Staff has concluded that this proposed Facilities SEP amendment will facilitate Los Angeles Unified's ability to successfully complete the Facilities SEP.

NOW, THEREFORE, BE IT RESOLVED THAT:

1. The School Construction Bond Citizens' Oversight Committee recommends that the Board of Education approve the redefinition of the Fairfax High School Major Modernization Project, define the James J. McBride Special Education Center – Career and Transition Center West / Grand View Boulevard Elementary School Campus Improvement Project with a combined budget of \$165,702,186 and amend the Facilities SEP to incorporate therein, as described in Board Report No. 281-22/23, a copy of which is attached hereto in the form it was presented to the BOC and is incorporated herein by reference.
2. This resolution shall be transmitted to the Los Angeles Unified School District Board of Education and posted on the Oversight Committee's website.
3. The District is directed to track the above recommendation and to report on the adoption, rejection, or pending status of the recommendations as provided in section 6.2 of the Charter and Memorandum of Understanding between the Oversight Committee and the District

ADOPTED on May 18, 2023, by the following vote:

AYES: 10

ABSTENTIONS: 0

NAYS: 0

ABSENCES: 5

/Margaret Fuentes/

Margaret Fuentes
Chair

/Michael Hamner/

D. Michael Hamner
Vice-Chair



Board of Education Report

File #: Rep-211-23/24, Version: 1

Approve the Definition of Three Classroom Replacement Projects and Amend the Facilities Services Division Strategic Execution Plan to Incorporate Therein

March 12, 2024

Facilities Services Division

Action Proposed:

Approve the definition of three Classroom Replacement Projects at the Carson High School Complex, Clover Avenue Elementary School, and James Madison Middle School (Projects), as described in Exhibit A, and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein. The combined budget for the proposed Projects is \$312,214,453.

Authorize the Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the proposed projects including budget modifications and the purchase of equipment and materials.

Background:

On August 24, 2021, the Board of Education (Board) adopted an update to the School Upgrade Program (SUP) to integrate Measure RR funding and priorities into its operational framework. The updated SUP framework and the Measure RR Implementation Plan (Implementation Plan) help guide the identification of sites and development of project proposals. The Implementation Plan included, among other priorities, the development of projects for relocatable classroom replacements.

School sites with an enrollment of more than 400 students, an instructional program with a facilities space need for at least eight classrooms in permanent buildings, and at least four classrooms in relocatable buildings that are not certified by the Division of the State Architect (DSA) were identified. School sites with the most DSA uncertified classrooms and serving the most students across Los Angeles Unified's geographic Regions and Board Districts were prioritized for a proposed Project. Relocatable classroom replacement projects will reduce Los Angeles Unified's reliance on relocatable buildings, restore play space, increase green schoolyards, eliminate health and safety concerns, and/or reduce Maintenance and Operations costs.

The proposed Projects will provide new classrooms and support spaces in permanent buildings that support the student learning environment and enable Los Angeles Unified to remove relocatable buildings that are not certified by DSA. The proposed Projects also include upgrades to outdoor spaces to align with Los Angeles Unified's goal to have 30% green schoolyards, exterior painting of existing permanent buildings and structures to create a cohesive aesthetic across each campus, accessibility improvements, and other required code upgrades.

The development of each proposed Project considered site accessibility, safety, supervision, optimal site configuration and utilization, play space, enrollment projections, educational programs, and operational impacts during construction.

File #: Rep-211-23/24, Version: 1

The school sites are located in Board Districts 1 (George McKenna), 6 (Kelly Gonez), and 7 (Tanya Ortiz Franklin).

Bond Oversight Committee Recommendations:

This item was considered by the School Construction Bond Citizens' Oversight Committee (BOC) at its meeting on February 29, 2024. The presentation that was provided is included as Exhibit C. Staff has concluded that this proposed Facilities SEP amendment is in alignment with BOC recommendations and will facilitate Los Angeles Unified School District's ability to successfully complete the Facilities SEP.

Expected Outcomes:

Approval of the three proposed Classroom Replacement Projects and amendment to the Facilities SEP to incorporate therein. The approval will enable staff to proceed with the design and construction of the proposed Projects.

The new facilities, once completed, will provide facilities that support education programs and student academic achievement. The proposed Projects will also decrease demands for repair and maintenance, alleviate the burden on custodial staff, and benefit the local economy by creating tax revenue and new jobs.

Board Options and Consequences:

Adoption of the proposed action will authorize staff to proceed with the expenditure of Bond Program funds and begin the environmental reviews and clearances, design, procurement, construction, and other activities necessary to implement the proposed Projects.

If the proposal is not approved, the Projects will not commence, and the schools will not benefit from the classroom replacement and associated campus upgrades being proposed.

Policy Implications:

The proposal does not impact Los Angeles Unified policy. The proposed Projects support the implementation of the update to the SUP to integrate Measure RR funding and priorities into its operational framework. Furthermore, the proposal is consistent with the District's long-term goal to address unmet school facilities needs and significantly improve the conditions of aging and deteriorating school facilities as described in the District's local bond measures K, R, Y, Q, and RR. The proposed action advances Los Angeles Unified's 2022-2026 Strategic Plan Pillar 4 Operational Effectiveness/Modernizing Infrastructure by replacing existing relocatable buildings with new permanent buildings.

Budget Impact:

The combined budget for the three proposed Classroom Replacement Projects is \$312,214,453. The proposed Projects will be funded by Bond Program funds in the SUP targeted for major modernizations, upgrades, and reconfiguration to school campuses.

The project budgets were prepared based on the current information known, and assumptions about the proposed project scope, site conditions, and market conditions. The project budgets will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise and will be adjusted accordingly to enable the successful completion of the proposed Projects.

Student Impact:

The proposed Classroom Replacement Projects, once completed, will help ensure approximately 4,080 students attending these three campuses are provided with safe, welcoming, and state-of-the-art learning environments

File #: Rep-211-23/24, Version: 1

that support student-centered and engaged learning. The classroom replacements will also allow schools to attract and retain future students, which builds school pride and enhances opportunities to create a positive school culture.

Equity Impact:

The school sites were prioritized based on the number of relocatable buildings that are not certified by DSA and those serving the most students.

Issues and Analysis:

Staff will implement all opportunities to minimize construction impacts on school operations and existing education programs.

The Office of Environmental Health and Safety (OEHS) will evaluate the proposed Projects in accordance with the California Environmental Quality Act (CEQA).

Attachments:

Exhibit A: Scope, Budget, and Schedule for Three Classroom Replacement Projects

Exhibit B: BOC Resolution

Exhibit C: BOC Presentation


Informatives:

None

Submitted:

02/02/24

File #: Rep-211-23/24, Version: 1

RESPECTFULLY SUBMITTED,**APPROVED BY:**



ALBERTO M. CARVALHO
Superintendent



PEDRO SALCIDO
Deputy Superintendent, Business Services and Operations

REVIEWED BY:**APPROVED BY:**


DEVORA NAVERA REED
General Counsel



KRISZTINA TOKES
Chief Facilities Executive
Facilities Services Division

☒ Approved as to form.

REVIEWED BY:**PRESENTED BY:**


NOLBERTO DELGADILLO
Deputy Chief Business Officer, Finance



AARON BRIDGEWATER
Director of Facilities Planning & Development
Facilities Services Division

☒ Approved as to budget impact statement.

1. Carson High School Complex – Classroom Replacement Project

Region South, Board District 7 (Tanya Ortiz Franklin)

Project Background and Scope:

The Carson High School Complex (Complex) spans 29.23 acres and serves students in grades 9-12. The Complex is comprised of the following schools: Carson High STEAM School, Academies of Education and Empowerment, Academy of Medical Arts, Carson High School Musical Entertainment & Digital Arts Magnet, and Eagle Tree Continuation High School. As of the 2023-2024 Electronic Capacity Assessment Review (E-CAR), the Complex served approximately 2,350 students and the projected enrollment for planning purposes is approximately 2,280 students. Eagle Tree Continuation High School serves an additional 60 students annually. The Complex has 20 existing relocatable buildings, 19 of which are not certified by the Division of the State Architect (DSA), containing 37 classrooms.

The proposed project includes, but is not limited to:

- Construction of approximately 30 classrooms, support and administrative spaces, and covered walkways.
- Replacement of the existing relocatable buildings at Eagle Tree Continuation High School.
- Replacement of the existing softball field impacted by the project development.
- Demolition and/or removal of 20 existing relocatable buildings containing 37 classrooms and associated support spaces.
- Improvements necessary to meet the District's goal for schoolyards to be 30% green/natural.
- Site improvements include new parking, utility upgrades, landscaping, hardscaping, fencing and gates, security enhancements, and accessibility upgrades.
- Painting the exterior of existing buildings and structures.
- Installation and removal of interim facilities necessary to support school programs during construction.
- Requirements from the Americans with Disabilities Act (ADA), DSA, California Environmental Quality Act (CEQA), Department of Toxic Substances Control (DTSC), or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$145,644,050

Project Schedule: Construction activities are anticipated to begin in Q4-2027 and be completed in Q4-2030.

2. Clover Avenue Elementary School – Classroom Replacement Project

Region West, Board District 1 (Dr. George McKenna)

Project Background and Scope:

Clover Avenue Elementary School spans 7.75 acres and serves students in kindergarten through 5th grade. As of the 2023-2024 E-CAR, the school served 497 students and the projected enrollment for planning purposes is approximately 450 students. The school has 12 existing relocatable buildings containing 20 classrooms that are not certified by DSA.

The proposed project includes, but is not limited to:

- Construction of approximately 19 classrooms, support spaces, and covered walkways.
- Demolition and/or removal of 12 existing relocatable buildings containing 20 classrooms and associated support spaces, a permanent restroom building, a permanent storage building, and shade structures.
- Improvements necessary to meet the District's goal for schoolyards to be 30% green/natural.
- Site improvements include new parking, utility upgrades, new playground areas, a kindergarten play structure, landscaping, hardscaping, fencing and gates, security enhancements, and accessibility upgrades.
- Painting the exterior of existing buildings and structures.
- Installation and removal of interim facilities necessary to support school programs during construction.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$105,819,442

Project Schedule: Construction activities are anticipated to begin in Q4-2027 and be completed in Q4-2030.

3. James Madison Middle School – Classroom Replacement Project

Region North, Board District 6 (Kelly Gonez)

Project Background and Scope:

James Madison Middle School spans 19.37 acres and serves students in grades 6-8. The campus is comprised of the following schools and academies: James Madison Middle School; Computer Science and Engineering Design Magnet; Medical, Math and Science Magnet; School for Advanced Studies; and Discover Media Arts and Communication Academy. As of the 2023-2024 E-CAR, the campus served 1,234 students and the projected enrollment for planning purposes is approximately 1,200 students. The campus has 17 existing relocatable buildings, 14 of which are not certified by DSA, containing 28 classrooms.

The proposed project includes, but is not limited to:

- Construction of approximately nine classrooms, support spaces, and covered walkways.
- Demolition and/or removal of 17 relocatable buildings containing 28 classrooms and associated support spaces.
- Improvements necessary to meet the District's goal for schoolyards to be 30% green/natural.
- Site improvements include new parking, utility upgrades, new playground areas, landscaping, hardscaping, fencing and gates, security enhancements, and accessibility upgrades.
- Painting the exterior of existing buildings and structures.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$60,750,961

Project Schedule: Construction activities are anticipated to begin in Q4-2027 and be completed in Q2-2030.

LOS ANGELES UNIFIED SCHOOL DISTRICT

SCHOOL CONSTRUCTION BOND CITIZENS' OVERSIGHT COMMITTEE

Margaret Fuentes, Chair
LAUSD Student Parent
D. Michael Hamner, FAIA, Vice-Chair
American Institute of Architects
Dr. Samantha Rowles, Secretary
LAUSD Student Parent
Robert Campbell, Executive Committee
L.A. Co. Auditor-Controller's Office
Scott Pansky, Executive Committee
L.A. Area Chamber of Commerce

Neelura Bell
CA Charter School Association
Chad Boggio
L.A. Co. Federation of Labor AFL-CIO
Jeffrey Fischbach
CA Tax Reform Assn.
Aleigh Lewis
L.A. City Controller's Office
Patrick MacFarlane
Early Education Coalition
Jennifer McDowell
L.A. City Mayor's Office

Brian Mello
Assoc. General Contractors of CA
Dr. Clarence Monteclaro
Tenth District PTSA
William O. Ross IV
31st District PTSA
Santa Ramirez (Alternate)
Tenth District PTSA
Connie Yee (Alternate)
L.A. Co. Auditor-Controller's Office
Vacant
AARP

Joseph P. Buchman – Legal Counsel
Burke, Williams & Sorensen, LLP
Lori Raineri and Keith Weaver – Oversight Consultants
Government Financial Services Joint Powers Authority

Timothy Popejoy
Bond Oversight Administrator
Perla Zitle
Bond Oversight Coordinator

RESOLUTION 2024-06

BOARD REPORT 211-23/24

RECOMMENDING BOARD APPROVAL TO DEFINE AND APPROVE THREE CLASSROOM REPLACEMENT PROJECTS AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN

WHEREAS, Los Angeles Unified School District (Los Angeles Unified) Staff proposes that the Board of Education (Board) define and approve three Classroom Replacement Projects (Projects) at the Carson High School Complex, Clover Avenue Elementary School, and James Madison Middle School, and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein, as described in Board Report No. 211-23/24; and

WHEREAS, Los Angeles Unified Staff also requests that the Board authorize the Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the proposed projects including budget modifications and the purchase of equipment and materials; and

WHEREAS, Relocatable classroom replacement projects have been prioritized within the School Upgrade Program (SUP) to reduce Los Angeles Unified's reliance on relocatable buildings, restore play space, increase green schoolyards, eliminate health and safety concerns, and/or reduce Maintenance and Operations costs; and

WHEREAS, The combined project budget for the three proposed Projects is \$312,214,453. The proposed Projects will be funded by Bond Program funds targeted in the School Upgrade Program for major renovations, modernizations, and reconfigurations to school campuses; and

WHEREAS, The school sites were prioritized based on the campuses with the largest number of relocatable classrooms that are not certified by the Division of the State Architect (DSA) and those serving the most students; and

RESOLUTION 2024-06**RECOMMENDING BOARD APPROVAL TO DEFINE AND APPROVE THREE CLASSROOM REPLACEMENT PROJECTS AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN**

WHEREAS, The three proposed Projects will provide new classrooms and support spaces in permanent buildings that improve the student learning environment and enable Los Angeles Unified to remove relocatable buildings that are not certified by the DSA. The proposed Projects also include upgrades to outdoor spaces to align with Los Angeles Unified's goal to have 30% green schoolyards, exterior painting of existing permanent buildings and structures to create a cohesive aesthetic across each campus, accessibility improvements, and other required code upgrades; and

WHEREAS, The development of each proposed project considered site accessibility, safety, supervision, optimal site configuration and utilization, play space, enrollment projections, educational programs, and operational impacts during construction; and

WHEREAS, the District Office of General Counsel has reviewed the proposed Projects and determined that it may proceed to the Bond Oversight Committee for its consideration for recommendation to the Board of Education; and

WHEREAS, Los Angeles Unified Staff has concluded that this proposed Facilities SEP amendment will facilitate Los Angeles Unified's ability to successfully implement the Facilities SEP.

NOW, THEREFORE, BE IT RESOLVED THAT:

1. The School Construction Citizens' Bond Oversight Committee recommends that the Board of Education adopt District staff's proposal to amend the FSD SEP to approve project definitions for three Classroom Replacement Projects at the Carson High School Complex, Clover Avenue Elementary School, and James Madison Middle School, as defined in Board Report 211-23/24, a copy of which is attached hereto in the form it was presented to the BOC and is incorporated herein by reference.
2. This resolution shall be transmitted to the Los Angeles Unified School District Board of Education and posted on the Oversight Committee's website.
3. Los Angeles Unified is directed to track the above recommendation and to report on the adoption, rejection, or pending status of the recommendations as provided in section 6.2 of the Charter and Memorandum of Understanding between the BOC and Los Angeles Unified.

ADOPTED on February 29, 2024, by the following vote:

AYES: 11

ABSTENTIONS: 0

NAYS: 0

ABSENCES: 3

/Margaret Fuentes/

Margaret Fuentes
Chair

/Michael Hamner/

D. Michael Hamner
Vice-Chair

Classroom Replacement Projects

Bond Oversight Committee
Meeting

February 29, 2024



Background

- August 2021 – Facilities School Upgrade Program was approved, which included \$720 Million for Relocatable Classroom Replacement Projects
- Projects will replace existing relocatable buildings with new permanent buildings based on the capacity needs



Credit: TSK Architect/davisREED and Hongjoo Kim

Prioritization Methodology

1. Establish an Eligibility List – 69 school sites

- Minimum Qualifying Requirements per School Site:
 - Enrollment of more than 400 students
 - At least 8 classrooms are needed to meet the school's capacity demands in permanent buildings
 - At least 4 classrooms in relocatable buildings that are not certified by DSA
- Sustainable Schools
- No major investments in new/upgraded classrooms

2. Establish a Priority List

- Prioritize school sites with the most DSA uncertified classrooms and serving the most students
- Rank school sites by Region and at least one project per Board District

Priority School Sites

School Site	Region	Board District	Enrollment (2023–2024)
Bell High School	East	5	2,269
Carson High School Complex	South	7	2,354*
Clover Avenue Elementary School	West	1	497
Leo Politi Elementary School	West	2	556
Limerick Avenue Elementary School	North	3	646
James Madison Middle School	North	6	1,234
Third Street Elementary School	West	4	693

~165 new classrooms to replace DSA uncertified classrooms
~8,250 students positively impacted

**Eagle Tree Continuation High School is not included in the total enrollment, which currently serves an additional 30–90 students annually.*

Scoping Tenets


- Remove relocatable buildings and replace the capacity needed in new permanent buildings
- Remove all classrooms in relocatable buildings that are not DSA certified
- Upgrade outdoor spaces to align with the District's goal to have 30% green schoolyards
- Accessibility improvements (as necessary per DSA requirements)
- Paint exterior of existing permanent buildings



Credit: TSK Architect/davisREED and Hongjoo Kim

Project Location Map

- 1. **Carson High School Complex**
Region South
Board District 7
- 2. **Clover Avenue Elementary School**
Region West
Board District 1
- 3. **James Madison Middle School**
Region North
Board District 6

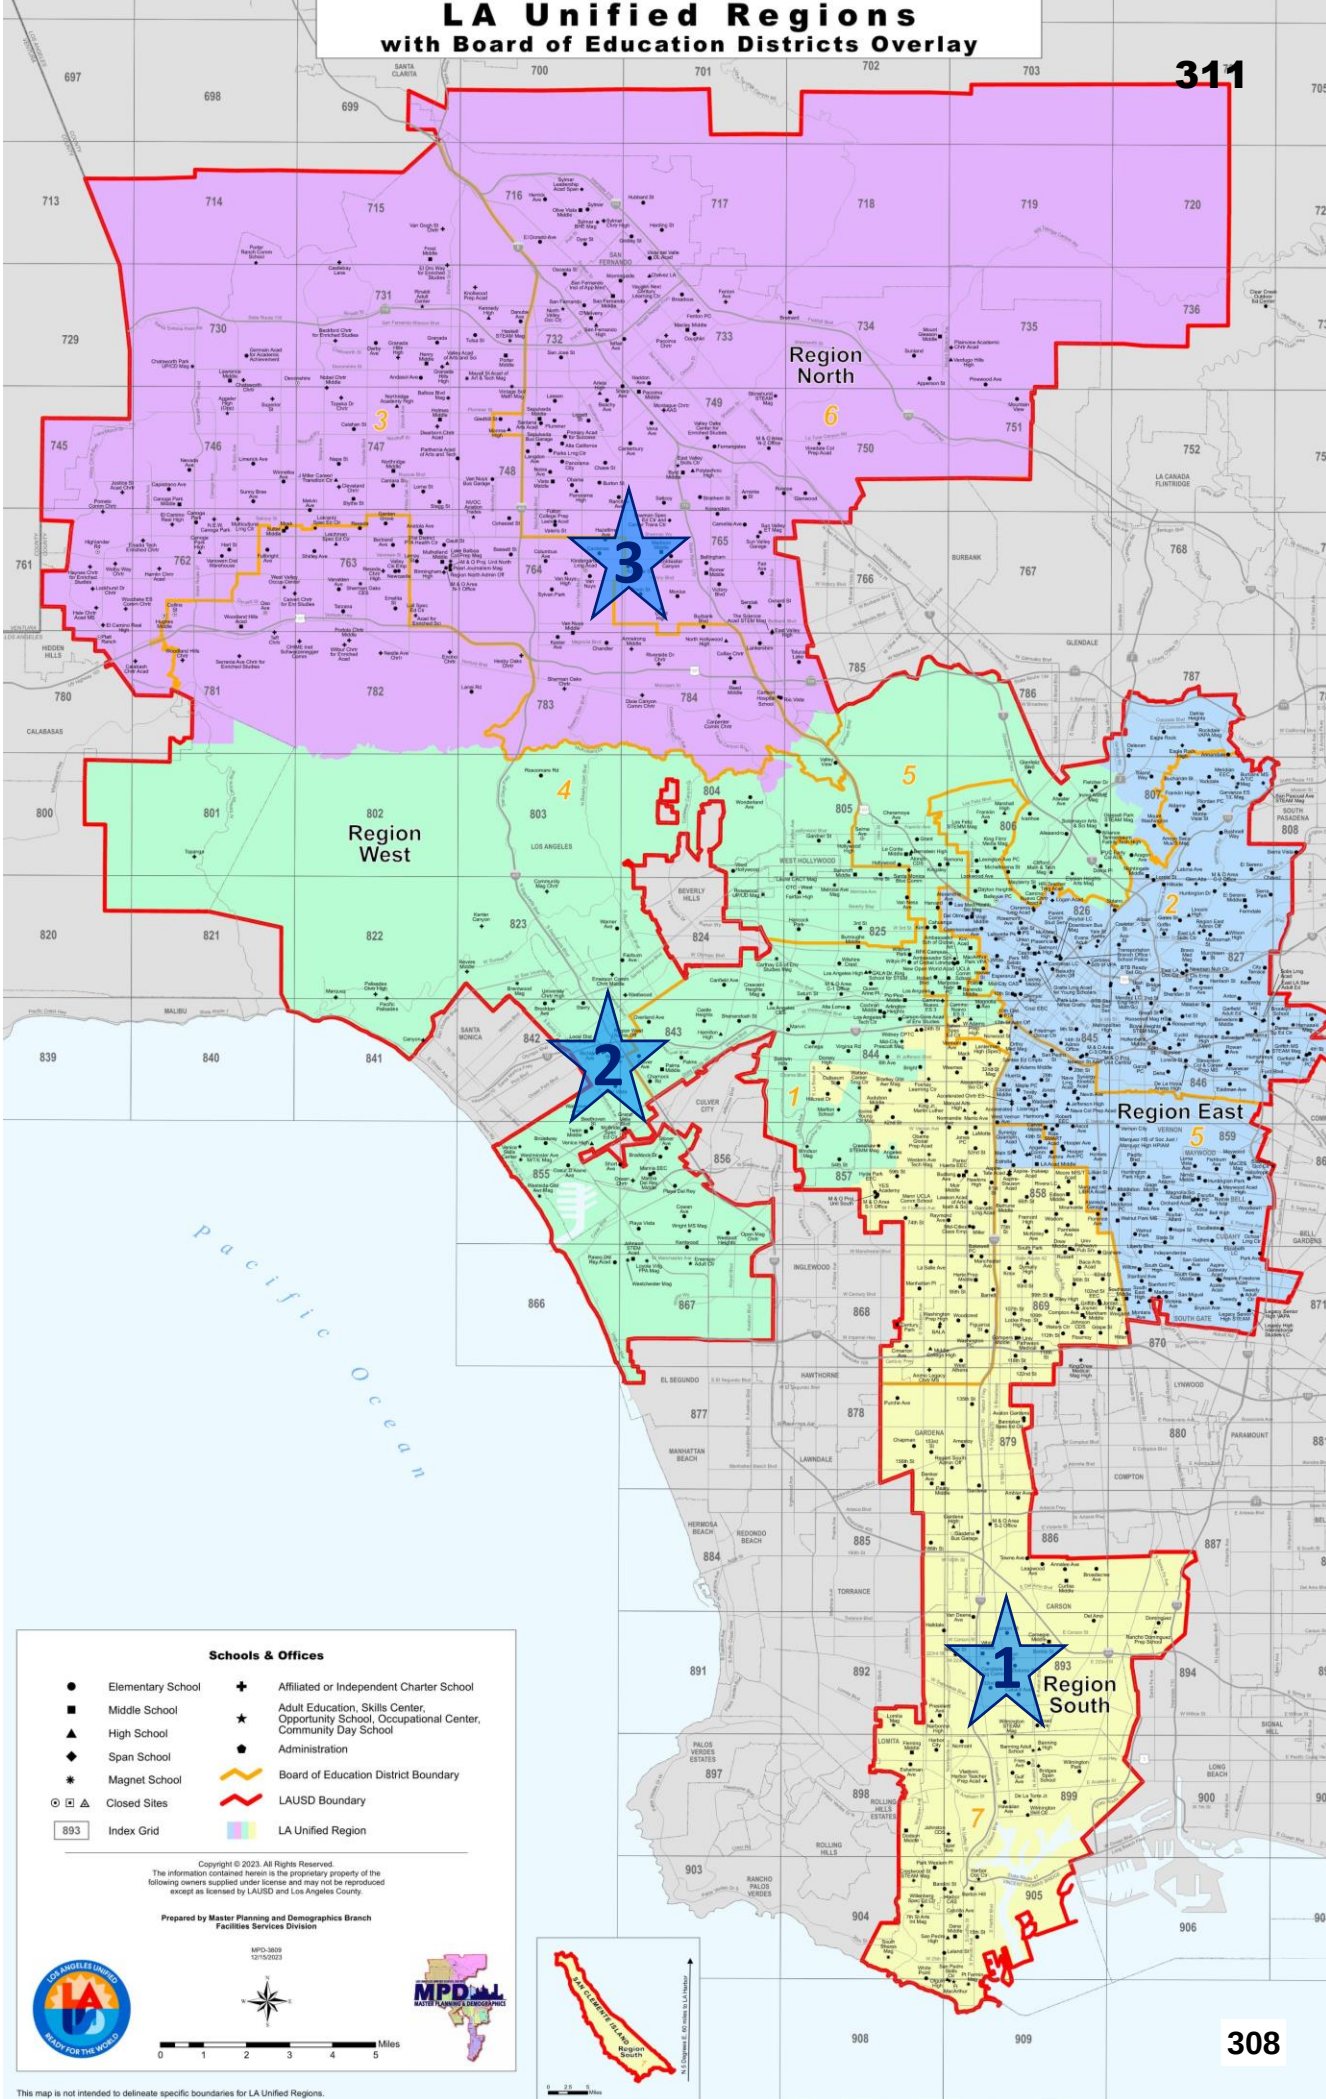

Carson High School Complex* Classroom Replacement

REGION SOUTH

BOARD DISTRICT 7

BOARD MEMBER TANYA ORTIZ FRANKLIN

Project Scope

- Construction of approximately 30 classrooms, support and administrative spaces, and covered walkways.
- Replacement of the existing relocatable buildings at Eagle Tree Continuation High School.
- Replacement of the existing softball field impacted by the project development.
- Demolition and/or removal of 20 existing relocatable buildings containing 37 classrooms and associated support spaces.
- Improvements necessary to meet the District’s goal for schoolyards to be 30% green/natural.
- Site improvements include new parking, utility upgrades, landscaping, hardscaping, fencing and gates, security enhancements, and accessibility upgrades.
- Painting the exterior of existing buildings and structures.
- Installation and removal of interim facilities necessary to support school programs during construction.
- Requirements from the Americans with Disabilities Act (ADA), Division of the State Architect (DSA), California Environmental Quality Act (CEQA), Department of Toxic Substances Control (DTSC), or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget


\$145,644,050

Anticipated Construction Schedule


Start: Q4-2027

Completion: Q4-2030

**Carson High School Complex includes the following schools: Carson High STEAM School, Carson High School Musical Entertainment and Digital Arts Magnet, Academies of Education and Empowerment, Academy of Medical Arts, and Eagle Tree Continuation High School*

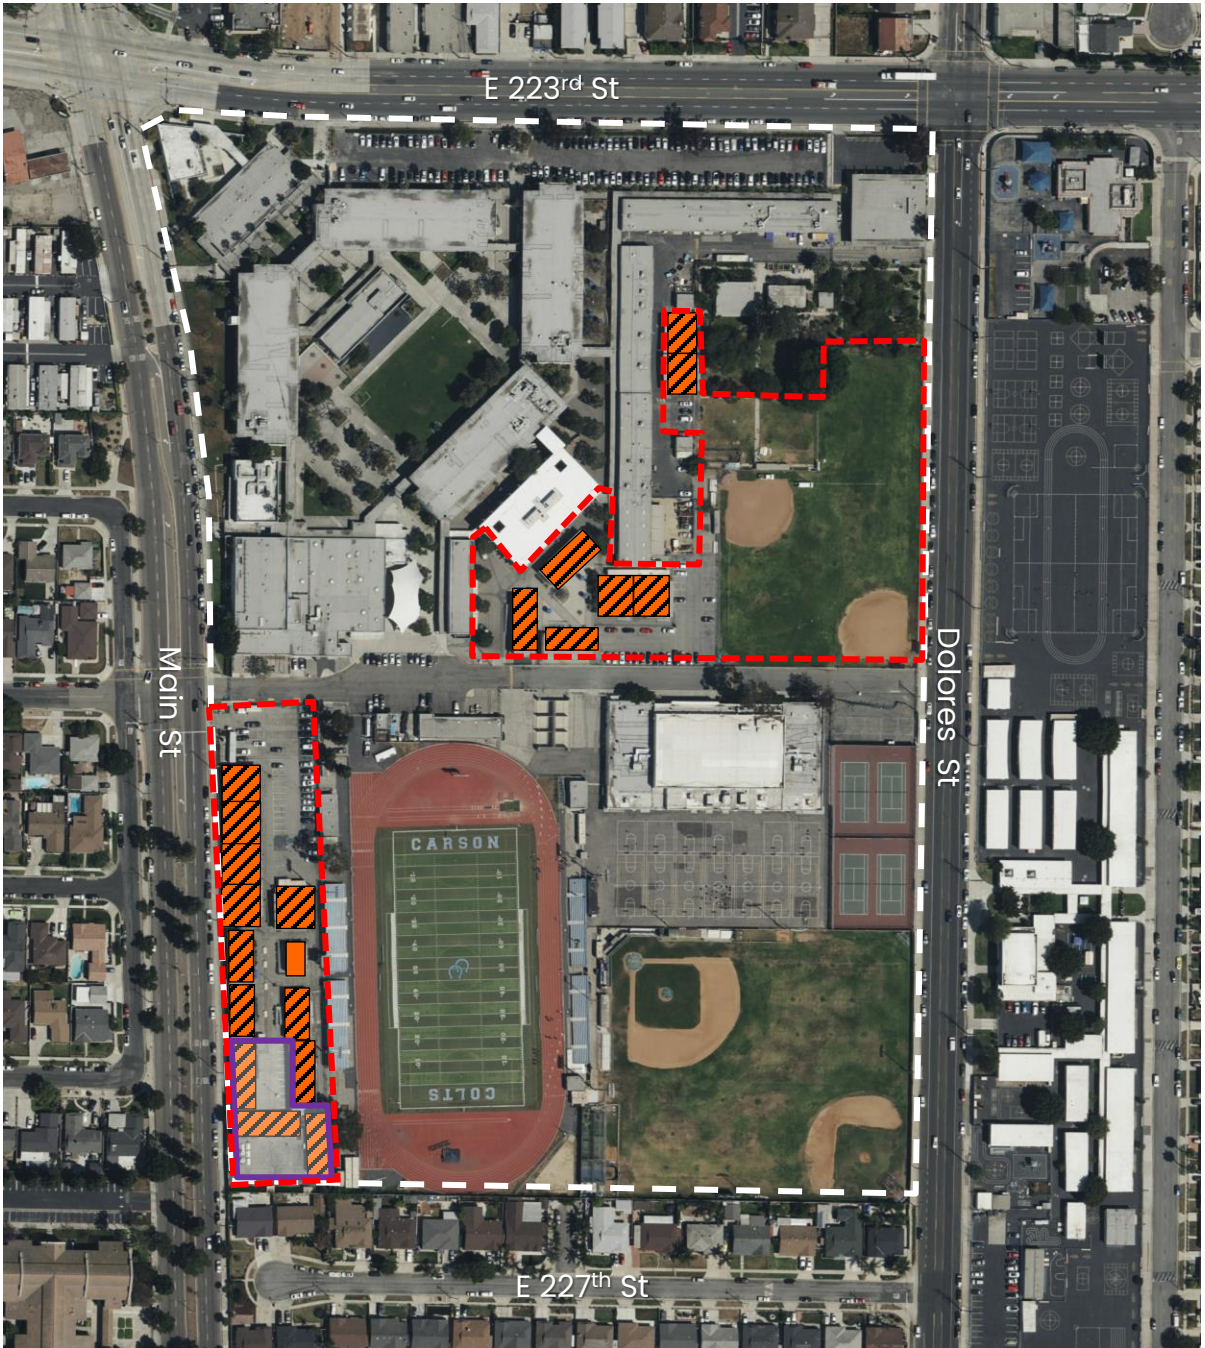

- Development Zone
- Relocatable Building to be Removed
- Relocatable Building to Remain
- DSA Uncertified
- Permanent Building to be Removed
- Eagle Tree Continuation High School



Clover Avenue Elementary School Classroom Replacement

REGION WEST

BOARD DISTRICT 1

BOARD MEMBER DR. GEORGE MCKENNA

Project Scope

- Construction of approximately 19 classrooms, support spaces, and covered walkways.
- Demolition and/or removal of 12 existing relocatable buildings containing 20 classrooms and associated support spaces, a permanent restroom building, a permanent storage building, and shade structures.
- Improvements necessary to meet the District's goal for schoolyards to be 30% green/natural.
- Site improvements include new parking, utility upgrades, new playground areas, a Kindergarten play structure, landscaping, hardscaping, fencing and gates, security enhancements, and accessibility upgrades.
- Painting the exterior of existing buildings and structures.
- Installation and removal of interim facilities necessary to support school programs during construction.
- Requirements from the Americans with Disabilities Act (ADA), Division of the State Architect (DSA), California Environmental Quality Act (CEQA), Department of Toxic Substances Control (DTSC), or other improvements to ensure compliance with local, state, and federal requirements.


Project Budget

\$105,819,442


Anticipated Construction Schedule

Start: Q4-2027

Completion: Q4-2030

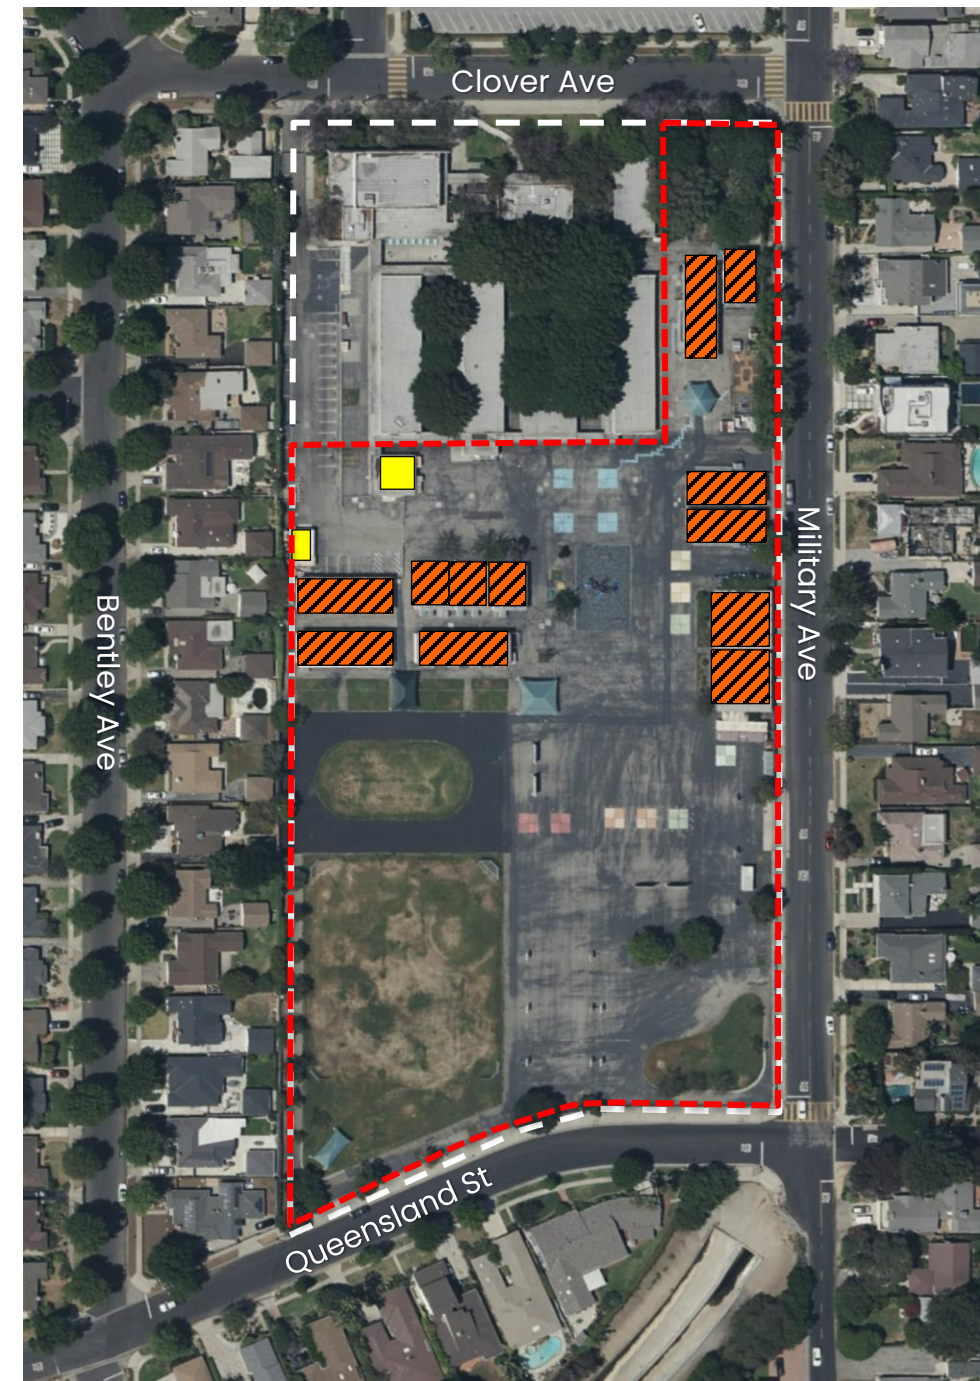

- Development Zone
- Relocatable Building to be Removed
- Relocatable Building to Remain
- DSA Uncertified
- Permanent Building to be Removed



James Madison Middle School Classroom Replacement

REGION NORTH

BOARD DISTRICT 6

BOARD MEMBER KELLY GONEZ

Project Scope

- Construction of approximately 9 classrooms, support spaces, and covered walkways.
- Demolition and/or removal of 17 relocatable buildings containing 28 classrooms and associated support spaces.
- Improvements necessary to meet the District's goal for schoolyards to be 30% green/natural.
- Site improvements include new parking, utility upgrades, new playground areas, landscaping, hardscaping, fencing and gates, security enhancements, and accessibility upgrades.
- Painting the exterior of existing buildings and structures.
- Requirements from the Americans with Disabilities Act (ADA), Division of the State Architect (DSA), California Environmental Quality Act (CEQA), Department of Toxic Substances Control (DTSC), or other improvements to ensure compliance with local, state, and federal requirements.


Project Budget

\$60,750,961

Anticipated Construction Schedule


Start: Q4-2027

Completion: Q2-2030

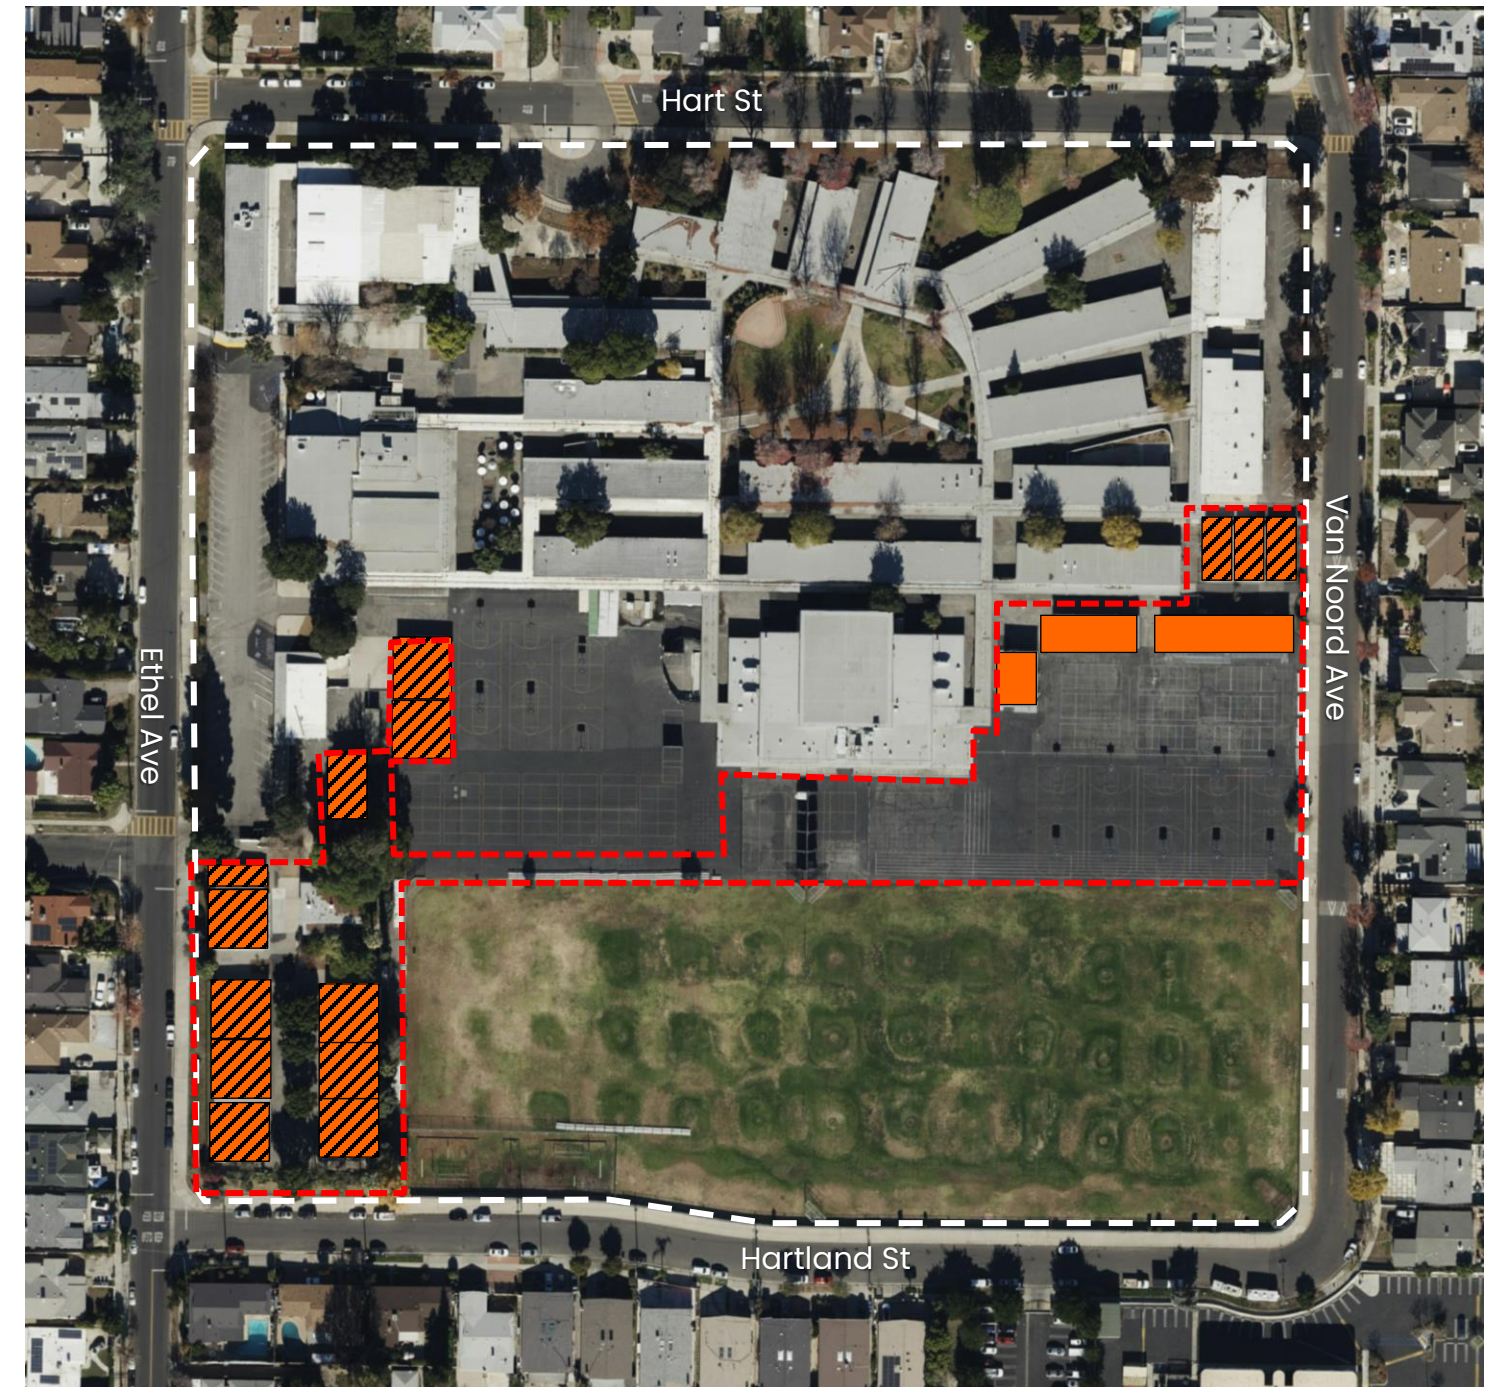

- Development Zone
- Relocatable Building to be Removed
- Relocatable Building to Remain
- DSA Uncertified
- Permanent Building to be Removed

N



Questions?



Credit: John Friedman Alice Kimm Architects and Geronimo Concrete, Inc.



Credit: GGA+ and Kemp Bros. Construction, Inc.



Board of Education Report

File #: Rep-007-22/23, Version: 1

Define and Approve Six Accessibility Enhancement Projects, One Barrier Removal Project, and Amend the Facilities Services Division Strategic Execution Plan to Incorporate Therein

August 30 2022

Facilities Services Division and Division of Special Education

Action Proposed:

Define and approve six accessibility enhancement projects, at the schools listed below, as described in Exhibit A, to support the implementation of the Board of Education (Board)-approved Self-Evaluation and Transition Plan under the Americans with Disabilities Act (ADA) and one ADA barrier removal project at Glenn Hammond Curtiss Middle School (Curtiss MS), and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein:

1. 7th Street Elementary Arts Integration Magnet (7th St EAIM)
2. Arminta Street Elementary School (Arminta ES)
3. Atwater Avenue Elementary School (Atwater ES)
4. Chatsworth Park Elementary Urban Planning California Distinguished Magnet (Chatsworth Park EUPCDM)
5. Christopher Columbus Middle School (Columbus MS)
6. Florence Nightingale Middle School (Nightingale MS)

The total combined budget for the seven proposed projects is \$47,811,123

Authorize the Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the projects including budget modifications and the purchase of equipment and materials.

Background:

On October 10, 2017, the Board approved the Self-Evaluation and Transition Plan (Transition Plan) under the Americans with Disabilities Act (ADA) to further Los Angeles Unified efforts to comply with ADA Title II program accessibility requirements (Board Report No. 124-17/18). The Transition Plan outlined Los Angeles Unified's proposed approach to providing program accessibility, which considers the characteristics of Los Angeles Unified, student population, variety of educational programs, as well as the existing level of accessibility. The Transition Plan established a specific approach and goals for achieving program accessibility within eight years through facility modifications and operational means.

Under the Transition Plan, each school is assigned to one of three levels of accessibility (Category One, Two, or Three) based on assessments of more than two dozen criteria, including school programs, matriculation options, feeder pattern, geographic location, known (or anticipated/matriculating) population of students with disabilities or parents/guardians with disabilities, type of instructional model, and public input. The assigned category reflects the level of accessibility the site needs to meet. Schools that do not yet meet the criteria for their assigned category will undergo accessibility improvements and are prioritized for project development based on the criteria mentioned above. The three categories of accessibility are as follows:

- Category One: These are “key” schools and will have the highest level of access, generally in accordance with applicable physical accessibility standards. Category 1A will provide “full accessibility” for the schools that were built to new construction standards, while Category 1B will provide “high accessibility” for schools that have been altered with some limited exceptions.
- Category Two: These will be “program-accessible” schools. The core spaces and features of these schools would be made accessible; in addition, program accessibility would be provided to all programs and activities at the school.
- Category Three: These schools will have “core access,” which means that the core spaces (certain common spaces) would be made accessible, to ensure a basic level of access to the building. These include, for example, parking, the main entrance and main office, assembly areas, and some restrooms.

The six school sites for which an accessibility enhancement project is being proposed do not yet meet their assigned category/level of accessibility and thus require facilities improvements. The scope, schedule, and budget for each proposed project reflects the existing known conditions at each school site and the improvements necessary to meet each schools’ assigned category of accessibility. The conditions of significance include acreage, topography, building square footage, existence of multi-story buildings, age of buildings, as well as the number of schools, programs, features and activities at a school site.

A need to accommodate students and staff with disabilities to access the main entrance, multipurpose room, and restroom facilities at Curtiss MS has been identified. Facilities staff was previously delegated authority to execute and expend Bond Program funds for Rapid Access Program (RAP) projects in response to an individual student’s need for programmatic access. These projects require minor installments and adjustments to facilities to ensure a barrier-free learning environment, do not require Division of the State Architect (DSA) approval and thus can be completed “rapidly” and have a project budget that does not exceed \$250,000. The proposed ADA barrier removal project at Curtiss MS does not meet the parameters of the RAP due to its scope and budget. As such, staff is presenting the project proposal to the Board for approval.

Expected Outcomes:

Define and approve six accessibility enhancement projects and one ADA barrier removal project, as detailed in Exhibit A, and adopt the proposed amendment to the Facilities SEP to incorporate therein. Approval will authorize staff to proceed with the implementation of the proposed projects.

Board Options and Consequences:

Adoption of the proposed action will authorize staff to proceed with the expenditure of Bond Program funds to immediately begin designing the proposed projects at seven school sites.

If the Board does not approve the proposal, staff will be unable to initiate the six proposed accessibility enhancement projects, which are necessary to achieve program accessibility as outlined in the Transition Plan, and the ADA barrier removal project at Curtiss MS, which is required for compliance with Section 504 of the Rehabilitation Act and the ADA.

Policy Implications:

The proposal furthers implementation of the Transition Plan. As outlined in the Transition Plan, at Category One, Two and Three schools, an appropriate number of classrooms will be identified to serve as accessible

learning spaces, some of which may require facility improvements to meet the criteria for their assigned accessibility category.

Any potential future room changes by Administrators or Principals will be reviewed by the Division of Special Education, the ADA Compliance Administrator, and the Facilities Services Division to ensure that new accessibility problems are not created as a result of the classroom moves. This will be done in close coordination with school staff to ensure disruptions are minimized.

Budget Impact:

The total combined budget, as currently estimated, for the seven proposed projects is \$47,811,123. The projects will be funded with Bond Program funds earmarked specifically for ADA Transition Plan Implementation.

Each project budget was prepared based on the current information known, and assumptions about the project scope, site conditions, and market conditions. Individual project budgets will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise and will be adjusted accordingly to enable the successful completion of each project.

Student Impact:

The seven proposed projects will remove barriers to program accessibility for students and qualified members of the community and ensure that all have an equal opportunity to access programs and activities at each campus.

Equity Impact:

Please see attached impact statement.

Issues and Analysis:

Both Title II of the ADA and Section 504 of the Rehabilitation Act of 1973 impose broad-reaching prohibitions against discrimination on the basis of disability. As to facilities, a key requirement for both the ADA and Section 504 is program accessibility: programs, benefits, services, and activities provided by public entities must be accessible to people with disabilities. This means that a qualified individual with a disability is not to be discriminated against because the entity's facilities are inaccessible; however, this does not necessarily mean that all facilities must be accessible. While both laws do require that newly constructed and altered facilities meet stringent accessibility requirements, they do not require that all existing facilities meet those standards, so long as the programs and services provided in those facilities are made accessible to people with disabilities. A program or service can be made accessible by relocating it, providing it in a different manner, or utilizing some other strategy to ensure that people with disabilities have an equal opportunity to benefit from the entity's programs and activities. These proposed projects are in alignment with Los Angeles Unified's implementation of the Board-approved Self-Evaluation and Transition Plan.

Curtiss MS has been assigned a Category Two accessibility level pursuant to the Transition Plan. Staff considered the possibility of reprioritizing the school on the Transition Plan list and proposing a more robust scope that would address all programmatic access requirements. However, it was determined that constructing two concrete ramps to provide students and staff with direct access to the entrance of the school, multipurpose room, and upgrading two restroom facilities was an immediate and pressing priority, and additional accessibility improvements could be undertaken under a new project and at a later date, as anticipated under the Transition Plan.

The Office of Environmental Health and Safety (OEHS) will evaluate the proposed projects in accordance with the California Environmental Quality Act (CEQA).

Bond Oversight Committee Recommendations:

This item was considered by the School Construction Bond Citizens' Oversight Committee (BOC) at its meeting on August 11, 2022. Staff has concluded that this proposed Facilities SEP amendment is in alignment with BOC recommendations and will facilitate Los Angeles Unified's ability to successfully complete the Facilities SEP.

Attachments:

Exhibit A - Define and Approve Six Accessibility Enhancement Projects and One Barrier Removal Project
Exhibit B - Student Eligibility by Program at Seven Schools
Exhibit C - BOC Resolution


Informatives:

None.

Submitted:

8/3/2022

RESPECTFULLY SUBMITTED,


ALBERTO M. CARVALHO
Superintendent

APPROVED BY:


MEGAN K. REILLY
Deputy Superintendent


REVIEWED BY:


DEVORA NAVERA REED
General Counsel Approved as to form.

APPROVED BY:


MARK HOVATTER
Chief Facilities Executive
Facilities Services Division

REVIEWED BY:


TONY ATIENZA
Director, Budget Services and Financial Planning Approved as to budget impact statement.

APPROVED BY:


ANTHONY AGUILAR
Chief of Special Education, Equity and Access

PRESENTED BY:


AARON BRIDGEWATER
Director of Facilities Planning and Development
Facilities Services Division



LOS ANGELES UNIFIED SCHOOL DISTRICT

Board of Education Report

Exhibit A

Define and Approve Six Accessibility Enhancement Projects and One Barrier Removal Project

1. 7th Street Elementary Arts Integration Magnet Accessibility Enhancement Project

San Pedro Community of Schools, Local District South, Board District 7 (Tanya Ortiz Franklin)

Project Background and Scope: The 7th Street Elementary Arts Integration Magnet site spans 6.06 acres and is comprised of a K-5 magnet school program. The building area is approximately 48,543 square feet and includes two multi-story permanent buildings, one single-story permanent building, and eight relocatable buildings. The permanent buildings were constructed between 1963 and 1976. As of the 2021-2022 Electronic Capacity Assessment Review (E-CAR), the school served 271 students and currently 55 have been identified as having a disability.

The site has been assigned a Category Two accessibility level. In order to meet the criteria for Category Two, various upgrades to six buildings are required, including: corrections, installation or replacement of one elevator with covered bridge, one new wheelchair lift, one concrete ramp, nine restroom upgrades, one sink/cabinet, one stage adapt, 13 path of travel upgrades, two railings/wing guards, two drinking fountain upgrades, three assembly seat upgrades, one assistive listening device, other miscellaneous upgrades, and any other required improvements or mitigations to ensure compliance with local, state and/or federal facilities requirements.

Project Budget: \$9,065,859

Project Schedule: Construction is anticipated to begin in Q3-2024 and be completed in Q1-2026.

2. Arminta Street Elementary School Accessibility Enhancement Project

Sun Valley Community of Schools, Local District Northeast, Board District 6 (Kelly Gonez)

Project Background and Scope: The Arminta Street Elementary School site spans 5.17 acres and is comprised of a traditional K-5 elementary school program. The building area is approximately 38,987 square feet and includes seven single-story permanent buildings, one multi-story permanent building and 11 relocatable buildings. The permanent buildings were constructed in 1953. As of the 2021-2022 E-CAR, the school served 346 students and currently 59 have been identified as having a disability.

The site has been assigned a Category Two accessibility level. In order to meet the criteria for Category Two, various upgrades to 16 buildings are required, including: corrections, installation or replacement of three assembly seat upgrades, one assistive listening device, one cafeteria counter, one concrete ramp, 11 TMP ramps, six drinking fountain upgrades, 19 accessible path of travel upgrades, 12 railings/wing guards, 10 restroom upgrades, one stage adapt, one new wheelchair lift, other miscellaneous upgrades, and any other required improvements or mitigations to ensure compliance with local, state and/or federal facilities requirements.

Project Budget: \$7,947,569

Project Schedule: Construction is anticipated to begin in Q3-2024 and be completed in Q1-2026.



LOS ANGELES UNIFIED SCHOOL DISTRICT

Board of Education Report

Exhibit A

Define and Approve Six Accessibility Enhancement Projects and One Barrier Removal Project

3. Atwater Avenue Elementary School Accessibility Enhancement Project

Glassell Park / Los Feliz Community of Schools, Local District Central, Board District 5 (Jackie Goldberg)

Project Background and Scope: The Atwater Avenue Elementary School site spans 3.92 acres and is comprised of two K-6 schools/programs, a traditional elementary school program and a dual language two-way immersion Spanish program. The building area is approximately 41,729 square feet and includes two single-story permanent buildings, one multi-story permanent building and nine relocatable buildings. The permanent buildings were constructed between 1960 and 1975. As of the 2021-2022 E-CAR, the school served 283 students and currently 67 have been identified as having a disability.

The site has been assigned a Category Three accessibility level. In order to meet the criteria for Category Three, various upgrades to seven buildings are required, including: corrections, installation or replacement of one assistive listening device, one automatic door opener, one cafeteria counter, one concrete ramp, five drinking fountain upgrades, one existing elevator upgrade, two parking lot upgrades, 20 accessible path of travel upgrades, nine railings/wing guards, eight restroom upgrades, one sink/cabinet, one stage adapt, one new wheelchair lift, one TMP ramp, other miscellaneous upgrades, and any other required improvements or mitigations to ensure compliance with local, state and/or federal facilities requirements.

Project Budget: \$5,010,938

Project Schedule: Construction is anticipated to begin in Q3-2024 and be completed in Q1-2026.

4. Chatsworth Park Elementary Urban Planning/California Distinguished Magnet Accessibility Enhancement Project

Canoga Park / Chatsworth Community of Schools, Local District Northwest, Board District 3 (Scott Schmerelson)

Project Background and Scope: The Chatsworth Park Elementary Urban Planning/California Distinguished Magnet site spans 5.76 acres and is comprised of a K-5 magnet school program. The building area is approximately 32,650 square feet and includes four single-story permanent buildings, one multi-story permanent building and seven relocatable buildings. The permanent buildings were constructed between 1935 and 1959, with some identified as historical resources. As of the 2021-2022 E-CAR, the school served 375 students and currently 34 have been identified as having a disability.

The site has been assigned a Category Two accessibility level. In order to meet the criteria for Category Two, various upgrades to five buildings are required, including: corrections, installation, or replacement of three assembly seat upgrades, two assistive listening devices, three concrete ramps, two drinking fountain upgrades, one playground component/matting, five accessible path of travel upgrades, seven railings/wing guards, seven restroom upgrades, two sinks/cabinets, one stage adapt, one new wheelchair lift, other miscellaneous upgrades, and any other required improvements or mitigations to ensure compliance with local, state and/or federal facilities requirements.

Project Budget: \$5,622,671

Project Schedule: Construction is anticipated to begin in Q3-2024 and be completed in Q1-2026



LOS ANGELES UNIFIED SCHOOL DISTRICT

Board of Education Report

Exhibit A

Define and Approve Six Accessibility Enhancement Projects and One Barrier Removal Project

5. Christopher Columbus Middle School Accessibility Enhancement Project

Canoga Park / Chatsworth Community of Schools, Local District Northwest, Board District 3 (Scott Schmerelson)

Project Background and Scope: The Christopher Columbus Middle School site spans 19.96 acres and is comprised of four 6-8 schools/programs, a traditional middle school program, a medical/math/science magnet program, a media arts/communication magnet program, and a co-located charter school program. The building area is approximately 131,128 square feet and includes 18 single-story permanent buildings, four multi-story permanent buildings, and two relocatable buildings. The permanent buildings were constructed between 1959 and 1965. As of the 2021-2022 E-CAR, the school served 649 students and currently 114 have been identified as having a disability.

The site has been assigned a Category Two accessibility level. In order to meet the criteria for Category Two, various upgrades to 21 buildings are required, including: corrections, installation, or replacement of five assistive listening devices, one automatic door opener, one cafeteria counter, six concrete ramps, 15 drinking fountain upgrades, two locker upgrades, one parking lot upgrade, 78 accessible path of travel upgrades, 13 railings/wing guards, 19 restroom upgrades, two sinks/cabinets, one stage adapt, one new wheelchair lift, other miscellaneous upgrades, and any other required improvements or mitigations to ensure compliance with local, state and/or federal facilities requirements.

Project Budget: \$12,002,244

Project Schedule: Construction is anticipated to begin in Q3-2024 and be completed in Q1-2026.

6. Florence Nightingale Middle School Accessibility Enhancement Project

Lincoln Heights / El Sereno Community of Schools, Local District East, Board District 2 (Mónica García)

Project Background and Scope: The Florence Nightingale Middle School site spans 8.85 acres and is comprised of four 6-8 schools/programs, one traditional middle school program, a medicine/health/kinesiology magnet program, a business entrepreneurship technology magnet program, and a gifted stem magnet program. The building area is approximately 154,568 square feet and includes three single-story permanent buildings, and nine multi-story buildings. The permanent buildings were constructed between 1937 and 1971, with some identified as historical resources. As of the 2021-2022 E-CAR, the school served 809 students and currently 146 have been identified as having a disability.

The site has been assigned a Category Three accessibility level. In order to meet the criteria for Category Three, various upgrades to nine buildings are required, including: corrections, installation, or replacement of three assembly seat upgrades, one assistive listening device, four automatic door openers, two concrete ramps, three drinking fountain upgrades, 12 accessible path of travel upgrades, four railings/wing guards, seven restroom upgrades, one stage adapt, one new wheelchair lift, other miscellaneous upgrades, and any other required improvements or mitigations to ensure compliance with local, state and/or federal facilities requirements.

Project Budget: \$5,651,586

Project Schedule: Construction is anticipated to begin in Q3-2024 and be complete in Q1-2026.



LOS ANGELES UNIFIED SCHOOL DISTRICT Board of Education Report

Exhibit A

Define and Approve Six Accessibility Enhancement Projects and One Barrier Removal Project

7. Glenn Hammond Curtiss Middle School Barrier Removal Project

Carson Community of Schools, Local District South, Board District 7 (Tanya Ortiz Franklin)

Project Background and Scope: The Glenn Hammond Curtiss Middle School site spans 19.88 acres and is comprised of three 6-8 schools/programs, a traditional middle school program, a science/technology/engineering/art/mathematics magnet program, and a co-located charter school program. The building area is approximately 159,950 square feet and includes three single-story permanent buildings, four multi-story buildings, and five relocatable buildings. The permanent buildings were constructed in 1969. As of the 2021-2022 E-CAR, the school served 359 students and currently 59 have been identified as having a disability.

This is an Americans with Disabilities Act barrier removal project to accommodate students and staff with disabilities to access the main entrance, multipurpose room, and restroom facilities at the school. The project will include the construction of two concrete ramps, two restroom upgrades, and any other required improvements or mitigations to ensure compliance with local, state and/or federal facilities requirements.

Project Budget: \$2,510,256

Project Schedule: Construction is anticipated to begin in Q1-2024 and be completed in Q4-2024.

Exhibit B

Student Eligibility by Program at Seven Schools

Disability Category	7th St EAIM	Arminta ES	Atwater ES	Chatsworth Park EUPCDM	Columbus MS	Nightingale MS	Curtiss MS
Orthopedic Impairment (OI)	<11	0	<11	<11	<11	<11	0
Other Health Impairment (OHI)	<11	<11	<11	<11	13	22	<11
Established Medical Disability (EMD)	0	0	0	0	0	0	0
Visual Impairment (VI)	0	0	0	0	0	0	0
Autism (AUT)	29	<11	30	<11	26	23	12
Deaf Blindness (DB)	0	0	0	0	0	0	0
Deafness (DEAF)	0	0	0	0	<11	0	0
Deferred Eligibility (Preschool Only)	0	0	0	0	0	0	0
Emotional Disturbance (ED)	<11	0	0	0	<11	<11	<11
Hard of Hearing (HH)	0	0	0	0	<11	<11	0
Intellectual Disability (ID)	<11	0	<11	0	<11	<11	0
Multiple Disabilities Hearing (MDH)	0	0	0	0	0	0	0
Multiple Disabilities Orthopedic (MDO)	0	0	0	0	0	0	0
Multiple Disabilities Vision (MDV)	0	0	0	0	0	0	0
Specific Learning Disability (SLD)	<11	14	11	14	58	88	36
Speech or Language Impairment (SLI)	<11	29	14	<11	<11	<11	<11
Traumatic Brain Injury (TBI)	0	0	0	0	0	0	0
Grand Total	55	59	67	34	114	146	59

To ensure confidentiality of individual student results and compliance with Los Angeles Unified policy and State guidelines, data is suppressed if the number of students included in calculations is less than 11.

LOS ANGELES UNIFIED SCHOOL DISTRICT

SCHOOL CONSTRUCTION BOND CITIZENS' OVERSIGHT COMMITTEE

Margaret Fuentes, Chair

LAUSD Student Parent

D. Michael Hamner, Vice-Chair

American Institute of Architects

Jennifer McDowell, Secretary

L.A. City Mayor's Office

Susan Linschoten, Executive Committee

L.A. Co. Auditor-Controller's Office

Scott Pansky, Executive Committee

L.A. Area Chamber of Commerce

Jeffrey Fischbach

CA Tax Reform Assn.

Chris Hannan

L.A. Co. Federation of Labor AFL-CIO

Hyepin Im

L.A. City Controller's Office

Samantha Rowles

LAUSD Student Parent

Araceli Sandoval-Gonzalez

Early Education Coalition

Dolores Sobalvarro

AARP

Celia Ayala (Alternate)

Early Education Coalition

Chad Boggio (Alternate)

L.A. Co. Federation of Labor AFL-CIO

Connie Yee (Alternate)

L.A. Co. Auditor-Controller's Office

Vacant31st District PTSA**Vacant**

Assoc. General Contractors of CA

Vacant

CA Charter School Association

Vacant

Tenth District PTSA

Joseph P. Buchman – Legal Counsel

Burke, Williams & Sorensen, LLP

Lori Raineri and Keith Weaver – Oversight**Consultants**

Government Financial Strategies

Timothy Popejoy

Bond Oversight Administrator

Perla Zitle

Bond Oversight Coordinator

RESOLUTION 2022-36

BOARD REPORT NO. 007-22/23

**RECOMMENDING BOARD APPROVAL TO DEFINE AND APPROVE SIX ACCESSIBILITY
ENHANCEMENT PROJECTS, ONE BARRIER REMOVAL PROJECT, AND AMEND THE
FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE
THEREIN**

WHEREAS, Los Angeles Unified School District (District) Staff proposes that the Board of Education (Board) define and approve six accessibility enhancement projects, at the schools listed below, to support the implementation of the Board-approved Self-Evaluation and Transition Plan under the Americans with Disabilities Act (ADA) and one ADA barrier removal project at Glenn Hammond Curtiss Middle School (Curtiss MS), and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) accordingly as described in Board Report No. 007-22/23:

1. 7th Street Elementary Arts Integration Magnet (7th St EAIM)
2. Arminta Street Elementary School (Arminta ES)
3. Atwater Avenue Elementary School (Atwater ES)
4. Chatsworth Park Elementary Urban Planning California Distinguished Magnet (Chatsworth Park EUPCDM)
5. Christopher Columbus Middle School (Columbus MS)
6. Florence Nightingale Middle School (Nightingale MS); and

WHEREAS, District Staff also requests that the Board authorize the Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the projects including budget modifications and the purchase of equipment and materials; and

WHEREAS, Under the Transition Plan, each school is assigned to one of three levels of accessibility (Category One, Two, or Three) based on assessments of more than two dozen criteria, including school programs,

RESOLUTION 2022-36**RECOMMENDING BOARD APPROVAL TO DEFINE AND APPROVE SIX ACCESSIBILITY ENHANCEMENT PROJECTS, ONE BARRIER REMOVAL PROJECT, AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN**

matriculation options, feeder pattern, geographic location, known (or anticipated/matriculating) population of students with disabilities or parents/guardians with disabilities, type of instructional model, and public input. The assigned category reflects the level of accessibility the site needs to meet. Schools that do not yet meet the criteria for their assigned category will undergo accessibility improvements and are prioritized for project development based on the criteria mentioned above. The three categories of accessibility are as follows:

- Category One: These are “key” schools and will have the highest level of access, generally in accordance with applicable physical accessibility standards. Category 1A will provide “full accessibility” for the schools that were built to new construction standards, while Category 1B will provide “high accessibility” for schools that have been altered with some limited exceptions; and
- Category Two: These will be “program-accessible” schools. The core spaces and features of these schools would be made accessible; in addition, program accessibility would be provided to all programs and activities at the school; and
- Category Three: These schools will have “core access,” which means that the core spaces (certain common spaces) would be made accessible, to ensure a basic level of access to the building. These include, for example, parking, the main entrance and main office, assembly areas, and some restrooms; and

WHEREAS, The six school sites for which an accessibility enhancement project is being proposed do not yet meet their assigned category/level of accessibility and thus require facilities improvements. The scope, schedule, and budget for each proposed project reflects the existing known conditions at each school site and the improvements necessary to meet each schools’ assigned category of accessibility. The conditions of significance include acreage, topography, building square footage, existence of multi-story buildings, age of buildings, as well as the number of schools, programs, features and activities at a school site; and

WHEREAS, A need to accommodate students and staff with disabilities to access the main entrance, multipurpose room, and restroom facilities at Curtiss MS has been identified. Facilities staff was previously delegated authority to execute and expend Bond Program funds for Rapid Access Program (RAP) projects in response to an individual student’s need for programmatic access. These projects require minor installments and adjustments to facilities to ensure a barrier-free learning environment, do not require Division of the State Architect (DSA) approval and thus can be completed “rapidly” and have a project budget that does not exceed \$250,000. The proposed ADA barrier removal project at Curtiss MS does not meet the parameters of the RAP due to its scope and budget. As such, staff is presenting the project proposal to the Board for approval; and

WHEREAS, The total combined budget, as currently estimated, for the seven proposed projects is \$47,811,123 and will be funded with Bond Program funds earmarked specifically for ADA Transition Plan Implementation; and

WHEREAS, Construction of the six accessibility enhancement projects are anticipated to begin in the third quarter of 2024 and be completed in the first quarter of 2026. Construction of the Curtiss MS ADA barrier removal project is anticipated to begin in the first quarter of 2024 and be completed in the fourth quarter of 2024; and

RESOLUTION 2022-36

RECOMMENDING BOARD APPROVAL TO DEFINE AND APPROVE SIX ACCESSIBILITY ENHANCEMENT PROJECTS, ONE BARRIER REMOVAL PROJECT, AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN

WHEREAS, District Staff has determined that the Projects are necessary to improve student health, safety, and educational quality; and

WHEREAS, District Staff has concluded that this proposed Facilities SEP amendment will facilitate Los Angeles Unified’s ability to successfully complete the Facilities SEP.

NOW, THEREFORE, BE IT RESOLVED THAT:

1. The School Construction Bond Citizens' Oversight Committee recommends that the Board define and approve six accessibility enhancement projects to support the implementation of the Board-approved Self-Evaluation and Transition Plan under the ADA and one ADA barrier removal project, and amend the Facilities SEP, accordingly, as described in Board Report No. 007-22/23, a copy of which is attached hereto in the form it was presented to the BOC and is incorporated herein by reference.
2. This resolution shall be transmitted to the Los Angeles Unified School District Board and posted on the Bond Oversight Committee’s website
3. Los Angeles Unified is directed to track the above recommendation and to report on the adoption, rejection, or pending status of the recommendations as provided in section 6.2 of the Charter and Memorandum of Understanding between the Bond Oversight Committee and Los Angeles Unified

ADOPTED on August 11, 2022, by the following vote:

AYES: 8

ABSTENTIONS: 0

NAYS: 0

ABSENCES: 3

/Margaret Fuentes/

Margaret Fuentes
Chair

/Michael Hamner/

D. Michael Hamner
Vice-Chair



Board of Education Report

File #: Rep-271-19/20, **Version:** 1

Amendment to the Facilities Services Division Strategic Execution Plan to Define and Approve Two Projects that Address Critical School Repair Needs

March 10, 2020

Facilities Services Division

Action Proposed:

Staff proposes that the Board of Education approve an amendment to the Facilities Services Division (FSD) Strategic Execution Plan (SEP) to define and approve two projects that address critical school repair needs, as listed on Attachment A. Staff further proposes that the Board authorize the Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the proposed projects, including budget modifications and the purchase of equipment and materials. The total combined budget for the two projects is \$16,584,266.

Background:

As the District's capital needs far exceed available funding, priorities for the expenditure of capital funding are evaluated to ensure the District's most pressing priorities are being addressed. Based on an evaluation of known facilities conditions and needs at schools, the following types of projects have been identified as the most pressing unfunded critical school repair and safety needs that should continue to be addressed within the limited funding available:

- Failing, deteriorated, and outdated building systems and components
- School buildings, rooms and/or facilities deemed unsafe for occupancy
- Other critical health and safety concerns, urgent/emergency conditions, and/or health and safety code compliance issues that may arise

The project proposals contained in this Board Report align with these identified types of pressing critical school repair and safety conditions. The list consists of roofing and water damage repair projects. Attachment A provides additional details pertaining to the proposed projects.

Expected Outcomes:

Staff anticipates that the Board of Education will approve the proposed action to define and approve two projects to address critical school repair needs that will improve student health, safety and educational quality.

Board Options and Consequences:

A "yes" vote will authorize staff to proceed with the expenditure of bond funds to undertake the project proposals in accordance with the provisions set forth in Measures K, R, Y and Q. If the proposed action is not approved, bond funds will not be expended and critical school repair needs will remain unaddressed.

Policy Implications:

The action is consistent with the District's commitment to address unmet school facilities needs and provide students with a safe and healthy learning environment. Moreover, the proposal is aligned with the Board-adopted Facilities Bond Program strategy to address unfunded and pressing school facilities needs related to safety, compliance, and instructional requirements (Board Report No. 048-17/18).

Budget Impact:

The total combined budget for the two projects is \$16,584,266. The projects will be funded with Bond Program funds earmarked specifically for critical school repair and safety improvements to school building components.

Each project budget was prepared based on the current information known and assumptions about the project scope, site conditions, and market conditions. Individual project budgets will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise, and will be adjusted accordingly to enable the successful completion of each project.

Student Impact:

Continuing our efforts to undertake critical school repair and safety improvement projects is a vital component to the District's ability to provide safe school environments that promote teaching and learning.

Issues and Analysis:

It may be necessary to undertake feasibility studies, site analysis, scoping, and/or due diligence activities on the proposed projects prior to initiating design. As necessary, the Office of Environmental Health and Safety (OEHS) will evaluate the proposed projects in accordance with the California Environmental Quality Act (CEQA) to ensure compliance. If through the planning and design process it is determined that the proposed project scope(s) will not sufficiently address the critical need identified, the project scope, schedule and budget will be revised accordingly.

Bond Oversight Committee Recommendations:

This item was considered by the BOC at its meeting on February 27, 2020. Staff has concluded that this proposed FSD SEP amendment will facilitate implementation of the FSD SEP, and therefore, it will not adversely affect the District's ability to successfully complete the FSD SEP.

Attachments:

Attachment A - Project Definitions for Two Projects that Address Critical School Repair Needs
Attachment B - BOC Resolution

Informatives:

None.

Submitted:

2/21/20

File #: Rep-271-19/20, Version: 1

RESPECTFULLY SUBMITTED,



AUSTIN BEUTNER
Superintendent

APPROVED BY:



MEGAN K. REILLY
Deputy Superintendent
Office of the Deputy Superintendent

REVIEWED BY:



DAVID HOLMQUIST
General Counsel

APPROVED BY:



MARK HOVATTER
Chief Facilities Executive
Facilities Services Division

☒ Approved as to form.

REVIEWED BY:



TONY ATIENZA
Director, Budget Services and Financial Planning

PRESENTED BY:



ROBERT LAUGHTON
Director of Maintenance & Operations
Facilities Services Division

☒ Approved as to budget impact statement.



LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report
Attachment A

1. Marvin Elementary School – Project to Provide New Paving

- *Local District West, Board District 1 – McKenna*
- *Project Background and Scope* – This project is to provide approximately 100,000 square feet of new asphalt paving at the main playground, kindergarten playground and parking area, including the replacement of concrete sidewalks, curbs, and gutters. The scope of work also includes greening areas, a reading garden, along with path of travel and accessibility upgrades.
- *Project Budget* -- \$10,142,391
- *Project Schedule* – Construction is anticipated to begin in Q3 2021 and conclude in Q3 2022.

2. Saturn Street Elementary School – Project to Provide New Paving

- *Local District West, Board District 1 – McKenna*
- *Project Background and Scope* – This project is to provide approximately 73,500 square feet of new asphalt paving campus-wide, including greening areas and a new parking area. The scope of work also includes accessibility upgrades to the boys' and girls' restrooms.
- *Project Budget* -- \$6,441,875
- *Project Schedule* – Construction is anticipated to begin in Q4 2021 and conclude in Q3 2022.

SCHOOL CONSTRUCTION BOND CITIZENS' OVERSIGHT COMMITTEE

Rachel Greene, Chair

Tenth District PTSA

Bevin Ashenmiller, Vice-Chair

LAUSD Student Parent

Karen Krygier, Secretary

L.A. City Controller's Office

Araceli Sandoval-Gonzalez, Executive Committee

Early Education Coalition

Tracy Bartley31st District PTSA**Jeffrey Fischbach**

CA Tax Reform Assn.

Melanie Freeland

American Institute of Architects

Margaret Fuentes

LAUSD Student Parent

Greg Good

L.A. City Mayor's Office

Chris Hannan

L.A. Co. Federation of Labor AFL-CIO

Michael Keeley

CA Charter School Association

Scott Pansky

L.A. Area Chamber of Commerce

Dolores Sobalvarro

AARP

Guy Zelenski

L.A. Co. Auditor-Controller's Office

Celia Ayala (Alternate)

Early Education Coalition

Connie Yee (Alternate)

L.A. Co. Auditor-Controller's Office

Jose Zambrano (Alternate)

Tenth District PTSA

(Vacant)

Assoc. General Contractors of CA

Joseph P. Buchman – Legal Counsel

Burke, Williams & Sorensen, LLP

Lori Raineri and Keith Weaver – Oversight Consultants

Government Financial Strategies

Timothy Popejoy

Bond Oversight Administrator

Perla Zitle

BOC Staff

RESOLUTION 2020-6

BOARD REPORT NO. 271-19/20

**AMENDMENT TO THE FACILITIES SERVICES DIVISION STRATEGIC
EXECUTION PLAN TO DEFINE AND APPROVE TWO PROJECTS THAT
ADDRESS CRITICAL SCHOOL SAFETY AND REPAIR NEEDS**

WHEREAS, District Staff proposes that the Board of Education approve an amendment to the Facilities Services Division (FSD) Strategic Execution Plan (SEP) to define and approve two projects that address critical school repair needs with a budget of \$16,584,266 (the "Projects") as described in Board Report 271-19/20 attached hereto; and authorize the Chief Procurement Officer and/or the Chief Facilities Executive, and/or his designee(s), to execute all instruments necessary to implement the proposed projects; and

WHEREAS, District Staff has determined that the Projects are necessary to improve student health, safety and educational quality; and

WHEREAS, District Staff has determined that the Projects will help facilitate the implementation of the Facilities Bond Program strategy to address unfunded and pressing school facilities related to safety, compliance, and instructional requirements; and

WHEREAS, the Projects are consistent with the District's commitment to address unmet school facilities needs and provide students with a safe and healthy learning environment; and

WHEREAS, the Board of Education's approval of the Projects will authorize District Staff to proceed with the expenditure of bond funds to undertake the Projects in accordance with the provisions set forth in Measures K, R, Y and Q; and

Bond Oversight Committee

RESOLUTION 2020-6
AMENDMENT TO THE FACILITIES SERVICES DIVISION STRATEGIC
EXECUTION PLAN TO DEFINE AND APPROVE TWO PROJECTS THAT ADDRESS
CRITICAL SCHOOL SAFETY AND REPAIR NEEDS

WHEREAS, District Staff has concluded that the proposed SEP amendment will facilitate implementation of the FSD SEP, and therefore, it will not adversely affect the District's ability to successfully complete the FSD SEP.

NOW, THEREFORE, BE IT RESOLVED THAT:

1. The School Construction Citizens' Bond Oversight Committee recommends that the Board of Education adopt an amendment to the Facilities Services Division (FSD) Strategic Execution Plan (SEP) to define and approve two projects that address critical school safety and repair needs, with a budget of \$16,584,266, as defined in Board Report 271-19/20, a copy of which is attached hereto in the form it was presented to the BOC and is incorporated herein by reference.
2. This resolution shall be transmitted to the Los Angeles Unified School District Board of Education and posted on the Oversight Committee's website.
3. The District is directed to track the above recommendation and to report on the adoption, rejection, or pending status of the recommendations as provided in section 6.2 of the Charter and Memorandum of Understanding between the Oversight Committee and the District.

ADOPTED on February 27, 2020, by the following vote:


AYES: 11

ABSTENTIONS: 0

NAYS: 0

ABSENCES: 3


 Rachel Greene
 Chair


 Bevin Ashenmiller
 Vice-Chair



Board of Education Report

File #: Rep-024-23/24, Version: 2

Capital Plan Projects

December 12, 2023

Office of the Chief Business Officer

Action Proposed:

Approve the use of \$423.5 million of Certificates of Participation (COP) to fund all or a portion of nine Capital Plan projects and/or programs, to be undertaken at one or more sites, the scope schedule and budget of which is outlined in Attachment A, and authorize the Superintendent and/or his designee(s) to execute all instruments necessary, as legally permissible, to implement the initial Capital Plan projects and/or programs, including budget modifications.

Some of the listed projects may require additional funding to fully complete, however this proposal is to authorize COP expenditures in the amount equal to what was generated by the August 2023 issuance, which was authorized by the Board of Education (Board) in June 2023. The funding strategy for some projects may include the use of various General Fund sources.

Background:

On June 13, 2023, the Board authorized a resolution approving the execution and delivery of COPs in the not-to-exceed amount of \$500 million (Board Report No. 300-22/23). In August 2023, the Office of the Chief Business Officer (CBO) sold COPs generating \$423.5 million to fund critical unmet needs of our school support facilities, as well as high-priority school facility needs for which sufficient bond funding is not currently available.

Under the leadership of the Chief Business Officer, a five-year capital plan covering fiscal years 2023-24 through 2027-2028 is being developed. Projects and/or programs were proposed as priority projects from various divisions, and only individual projects over \$1 million for which sufficient bond funds are not currently available and/or eligible were considered. All projects were reviewed by a steering committee comprised of various District senior executives using criteria including health and safety, regulatory compliance, alignment to the Strategic Plan, and economic impact. This work resulted in the identification of 12 priority projects and/or programs with an approximate budget of \$1.3 billion, approximately \$1.1 billion of which was identified for COPs proceeds. Requests to authorize future sales of COPs are anticipated to be proposed to the Board in subsequent years. The projects and/or programs being proposed for funding are a result of this work. All 12 identified projects and/or programs are listed below:

1. Enrollment Modernization Project
2. Student Information Systems Upgrades Project
3. Student Support Applications Modernization*
4. Student Data Analytics, Reporting and Dashboards Project*
5. Sun Valley Electric Buses and Generator Purchases Project
6. Sun Valley Transportation Center Electrification Project*
7. Green Schools for All Program*

8. Campus Security Systems Improvements*
9. Cybersecurity Improvements*
10. Gardena Area Transportation Center and Electric Bus Charging**
11. Gardena Area Electric Bus and Generator Purchases**
12. Procurement Services Support Center Upgrades: Electrification and Industrial Fans**

*Based on current scope and budget estimates, anticipated to require additional funding to fully complete/implement.

**No funding is being requested as part of this action; however, their current total estimated budget is part of the \$1.3 billion Capital Plan estimate.

The project budgets were prepared based on current information, and assumptions about the project scope, site conditions, and market conditions. The project budgets will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise and will be adjusted accordingly to enable the successful completion of the proposed projects.

Expected Outcomes:

The Board will approve nine Capital Plan projects and/or programs, allowing the District to move forward with needed capital improvements.

Board Options and Consequences:

Upon Board approval, staff will be authorized to proceed with the expenditure of COP funds and all other activities necessary to implement the proposed projects. If the proposed action is not approved, the District will not move forward with the projects.

Policy Implications:

This does not impact existing policy.

Budget Impact:

The 2023-24 Budget included the annual debt service for the 2023 COPs and non-capital costs for the projects. In Fiscal Year 2024, the annual debt service cost is estimated at \$11.3 million, and from FY 2025-FY 2038 the estimated annual cost is \$33.4 million. The debt service will be paid out of the District's General Fund. Furthermore, some projects will require additional funding to fully complete and/or implement. Sources of funds may vary. These additional costs are estimated to be approximately \$800 million, with the majority of funds, approximately \$650 million, expected to be funded by future COP issuances, and approximately \$89.5 million from Restricted General Fund-Expanded Learning Opportunity Program (ELOP).

A portion of the scope of five projects was temporarily front funded with operational budget with the intent to reimburse with COP proceeds once approved for specific projects. With the Board's approval of the Capital Plan projects, any prior expenditures will be transferred to the proposed projects. The projects that received some front funding are:

- Sun Valley Electric Buses and Generator Purchases Project: due to the high demand for electric school buses and to account for additional time needed to fulfill an order of 180 buses.
- Sun Valley Transportation Center Electrification Project: to help meet the District's electrification goals.
- Campus Safety Systems Improvement Projects at 291 Sites (Phase 1): due to a need to address student

safety as quickly as possible at priority school sites.

- Cybersecurity Improvement Program: due to an urgent need to begin implementing cybersecurity enhancements throughout the District.

If future COPs issuances and/or other funding sources are authorized for Capital Plan projects, all funding sources will be integrated into the Capital Plan sources of funds to support funding flexibility and efficiency and the effective implementation of the Capital Plan.

Student Impact:

Projects will improve the educational opportunities for students. The cybersecurity project will reduce risks associated with students' personal information and coursework. Similarly, the campus security project will provide a safer physical environment for students. Electrification of the school bus fleet will reduce the long-term operating costs and improve air quality.

Equity Impact:

Component	Score	Score Rationale
Recognition	2	Some of the projects are influenced by equity.
Resource Prioritization	4	Implementation of many of the projects will be conducted such that underserved populations will be a priority.
Results	3	Many of the projects, including electrification of the fleet, are expected to benefit those most impacted by historic health inequities.
TOTAL	9	

Issues and Analysis:

Projects may be undertaken at multiple District sites and/or may include various phases. Exhibit A outlines the scope of work proposed to be undertaken within the initial COPs issuance of \$423.5 million. Three of the nine projects are anticipated to be completed in their entirety, and six projects include an additional phase(s) of scope requiring further funding or a future allocation of funds to complete the initial phase as scoped.

Staff expects to return to the Board at a later date for authorization to sell additional COPs to fund projects at other District sites, additional project phases, and/or new Capital Plan projects.

Attachments:


Attachment A - Capital Plan Projects - scope, schedule, and budget

Informatives:

None.

Submitted:


12/8/2023

RESPECTFULLY SUBMITTED,



ALBERTO M. CARVALHO
Superintendent

APPROVED BY:


PEDRO SALCIDO
Deputy Superintendent, Business Services and Operations

REVIEWED BY:


DEVORA NAVERA REED
General Counsel

APPROVED & PRESENTED BY:


DAVID D. HART
Chief Business Officer

☒ Approved as to form.

REVIEWED BY:


NOLBERTO DELGADILLO
Deputy Chief Business Officer, Finance

☒ Approved as to budget impact statement.

**LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report**

Attachment A: Capital Plan Projects: Scope, Schedule, and Budget

1. Enrollment Modernization Project

Project Scope: Includes creation of an efficient process for families to apply, register and enroll their children in District schools by eliminating many of the forms parents currently must submit, transitioning from a manual, paper-based process to an automated one. This initiative will be accomplished via multiple projects in coordination with various business owners and stakeholders. One of the projects under this initiative is:

- o Configure online enrollment system to be mobile friendly.
- o Implement changes identified in Board Resolution (Res-044-18/19) "Everyone Counts", which requests that additional ethnicities be added to District applications to further disaggregate data for Asian, Pacific Islander, and other ethnic groups.
- o Enhancements to applications including, but not limited to, enrollment applications, MiSiS, SAP, Focus reports, data warehouse (IODS).
- o Develop new reports and dashboards for internal use as needed.
- o Develop new reports for external Federal and State reporting as needed.

Total Project Budget and COPs Allocation: \$2,000,000

Project Schedule: Implementation is anticipated to begin in Q1-2024 and be completed in Q4-2024.

2. Student Information Systems Upgrades Project

Project Scope: Includes updates to the District's student information system, including integration with the Bell Schedule, Household Hub (a system of record for parent information), and Early Education Student Information System. The scope may include, but is not limited to:

- o *Household Hub Integration:* Integrate the household hub with all District applications that use parent information. This includes the Parent Portal, Early Ed Student Information System (EESIS), Unified Enrollment, Cafeteria Management Services (CMS), etc.

This project will also support non-application needs such as reducing mailings (e.g., a single magnet flier can be sent to a household with multiple District students), providing wrap-around services for families (e.g., chronic absenteeism, mental health, etc.), and data analysis.

Furthermore, the project will address creation of a common path for updating parent information and sharing the household hub information. Options for cleaning existing parent information and sharing the cleansed data across the applications will also be explored.

- o *My Integrated Student Information System (MiSiS) with Bell Schedule:* Optimize the management of student schedules, school calendars, and improve overall school operations. By establishing a seamless connection between MiSiS and the Bell Schedule system, schools can enhance efficiency, accuracy, and communication related to student attendance, class timetables, and daily routines.
- o *Early Education Student Information System Migration to MiSiS:* Integrate preschool student information and early information into MiSiS. This will eliminate achievement gaps before the third grade and provide instructional support by allowing educators to identify issues and provide educational interventions.

Total Project Budget and COPs Allocation: \$1,000,000

Project Schedule: Implementation is anticipated to begin in Q1-2024 and be completed in Q4-2024.

3. Student Support Applications Modernization Project

Project Scope: Technology refresh and additional functionality for the District's Student support applications, including, but not limited to the Academic Monitoring System, LAUSD Parent Portal/Mobile App upgrade, Special Education Data Management, Student Medical Services Management System, and Universal ID for students. The scope may include, but is not limited to:

- o *Academic Monitoring System (AMS):* Provide ability to disaggregate student data such as Low-Income, Emergent Bilingual, Foster Youth, African American, and Students with Disabilities, and allow for real-time assessment and an instant collection of results.
- o *LAUSD Parent Portal/Mobile App:* Provide additional functionality to enhance family engagement and communication around student progress and achievement. Leverage data analytics and artificial intelligence to analyze the student's progress and engage families and students with personalized recommendations and support.
- o *Special Education Data Management:* Implement a web-based software system to be utilized Districtwide for the management and tracking of online Individualized Education Programs (IEPs), Individualized Family Services Plan (IFSP), Individual Service Plan (ISP), Section 504 Plans, Transition Services, RSP (Resource Program) Substitute, Due Process, Informal Dispute Resolution, State CALPADS reporting, District Validation Review, Extended School Year, Special Education Student Transportation, IEP Translation, and tracking of related services provided to students during the course of their education.
- o *Student Medical Services Management System:* Implement a web-based system to be utilized Districtwide for the management and tracking of student treatment plan, protocols, medication management, immunization compliance, nursing services, health office visits, audiological evaluation, chronic conditions, health alerts, vision/audio/dental/speech/sports physical screenings, and vital monitoring.
- o *Universal ID for Students:* Provide a singular ID for students to access services such as transportation, food services, library, after school programs, and school events. This will streamline many of the processes that will greatly benefit students.

Initial Budget and COPs Allocation:	\$11,400,000
<u>Future Anticipated Allocation(s):</u>	<u>\$ 3,000,000</u>
Total Anticipated Project Budget:	\$14,400,000

Project Schedule: Implementation is anticipated to begin in Q1-2024 and be completed in Q4-2025.

4. Student Data, Analytics, Reporting and Dashboards Project

Project Scope: Modernization of the District’s student data, analytics, reporting, and dashboards systems. With a continued increase in the number of tools students use to learn, there has been a significant increase in the volume of data available to help measure and inform student growth and achievement. This project puts in place / modernizes tools to understand this data. The scope may include, but is not limited to, implementation of a Cloud-based, fully managed solution for student analytics. New features / functionalities include:

- o Learning analytics
- o Guide resources
- o Supports for administrators, schools, staff, students, and parents
- o Data drill-down by region, school, and student group level, and support the learning management needs
- o Integration of curriculum, learning, student performance, student progress and related information
- o Suitable metrics and measurements
- o Notifications for exceptions
- o Incorporation of suitable views in the current workbench and views provided to schools, including those for principals, teachers and counselors, and also aggregated views for Regions and offices, to effectively monitor and manage student progress, including English Learners, students with disabilities, students experiencing homelessness, foster youth and other focus groups

Initial Budget and COPs Allocation:	\$ 4,763,040
<u>Future Anticipated Allocation(s):</u>	<u>\$ 844,800</u>
Total Anticipated Project Budget:	\$ 5,607,840

Project Schedule: Implementation is anticipated to begin in Q1-2024 and be completed in Q3-2025.

5. Sun Valley Electric Buses and Generator Purchases Project

Project Scope: Located at 11247 Sherman Way, in the community of Sun Valley, the Sun Valley Transportation Center is one of three LAUSD transportation centers located in the San Fernando Valley serving students in the surrounding communities. The buses currently residing there are equipped with internal combustion engines powered with CNG and propane fuels. The Sun Valley Transportation Center will be the first bus yard to have all its school buses transition to electric-powered.

The project will replace all 180 school buses based at Sun Valley Transportation Center with zero-emissions electric school buses (ESBs). The ESBs will be equipped with the latest safety features, including Wi-Fi and a Global Positioning System (GPS), and will have a capacity for 42 or 75 passengers (depending on the model) and an operating range of approximately 125 miles with a full charge. Studies have shown that electric buses are more fuel efficient and significantly reduce the cost of repairs and maintenance. This can result in overall savings of up to \$1.8 million per year. The new buses are anticipated to be delivered in 2025.

As part of the project, 25 propane-powered generators will be purchased to support ESB charging until the construction and installation of permanent charging infrastructure is completed (anticipated approximately two years after the delivery of the ESBs). The generator, situated on a trailer, can fully charge up to eight buses at one time in approximately six to eight hours. The chargers can be ordered and purchased, as needed, to coincide with the projected delivery of the ESBs in 2025. These chargers will also be part of the energy contingency plan, in the event there is a widespread power outage.

This project is critical to ensuring that the new ESBs will be delivered in time to replace CNG school buses with tanks expiring in April 2025. These buses must be removed from service per State and Federal regulations upon expiration. Sufficient lead time is needed for manufacturers to build the buses and for the California Highway Patrol (CHP) to inspect the buses which may take three months after the delivery of the buses.

Total Project Budget and COPs Allocation: \$88,700,000

Project Schedule: Purchases began in Q2-2023 and are anticipated to be completed in Q4-2025.

6. Sun Valley Transportation Center Electrification Project

Project Scope: The Sun Valley Transportation Center Electrification project consists of:

- o *Charging Stations:* The installation of approximately 200 electric vehicle (EV) charging stations for school buses.
- o *Solar and Battery Storage:* Provide a new solar array canopy with battery storage.
- o *Bus Wash Building Replacement:* Replace the existing bus wash with a new prefabricated bus wash building.
- o *Paving:* Provide new asphalt overlay throughout the site with new parking striping. Provide new asphalt paving in the areas of trenching for underground conduit.
- o *Perimeter Barrier Wall:* Provide a new concrete perimeter barrier wall around the site with new security gates at the vehicle entry locations.
- o *Site Lighting & Security:* Provide new site lighting poles and provide new lighting under the solar canopy. Provide new security cameras.
- o *Landscape:* Provide a new landscape buffer on Sun Valley Magnet School property, adjacent to the new pre-cast concrete wall for noise reduction and improved aesthetics.
- o *Temporary Bus Parking:* Provide temporary offsite bus parking, as needed, during construction.

Initial Budget and COPs Allocation:	\$72,162,739
<u>Future Anticipated Funding Allocation(s):</u>	<u>\$ 7,957,901</u>
Total Anticipated Project Budget:	\$80,120,640

Project Schedule: Construction is anticipated to begin in Q4-2025 and to be completed in Q4-2026.

7. Green Schools for All Program

A multi-pronged approach, which includes various project types and funding sources, will be utilized to help meet the goal of providing 30% safe and sustainable green schoolyards at all schools, to the extent feasible based on the physical constraints of individual campuses, by 2035. In total \$139,500,000 of non-bond funds are anticipated to be invested to further this work. This action allocates \$25,000,000 of COPs, and authorizes the execution of all instruments necessary, as legally permissible, to implement the projects, including those funded with General Fund-ELOP, and to make budget modifications. As detailed below, it is anticipated that an additional funding allocation of \$25,000,000 will be requested to complete this work. Additionally, \$89,500,000 of Restricted General Fund- Expanded Learning Opportunity Program (ELOP) has been allocated for these projects.

Green Schoolyard Upgrade Projects

Project Scope/Background: The proposed projects will provide improvements to schoolyards to align with the goal of providing 30% of a school sites' schoolyard with green/natural spaces. The scope may include replacing significant areas of paved surfaces with permeable surfaces that incorporate native/drought tolerant planting, the addition of natural grass play fields, the installation of trees and other shade elements to achieve 20% shade in the schoolyard, irrigation, decomposed granite and pavers, outdoor classroom elements, as well as accessibility improvements, as required, to ensure equal access to all students. After approval of this action, individual project budgets, scopes and schedules will be developed.

Approximately \$100,000,000 of non-bond funding is anticipated to be invested in the development of 15 Green Schoolyard Upgrade projects. This action will authorize \$25,000,000 of COP funding, which will be combined with an allocation of \$50,000,000 of Restricted General Fund-ELOP, to provide an initial \$75,000,000 of Green Schoolyard Upgrade projects. This is expected to provide sufficient funding to complete pre-construction activities at all 15 sites listed below, and to complete construction at a minimum of 11 sites. It is anticipated that an additional allocation of approximately \$25,000,000 will be needed to complete all of these projects.

Board District	Region	Site Name	Green Schoolyards Index Rank
1	West	Marvin ES	81
1	South	Manchester ES	84
2	East	Bridge ES	4
2	East	Dena ES	7
3	North	Canoga Park ES	16
3	North	Sylvan Park ES	30
4	North	Vanalden ES	31
4	North	Encino ES	113
5	East	San Pedro ES	5

Board District	Region	Site Name	Green Schoolyards Index Rank
5	East	Heliotrope ES	8
6	North	Strathern ES	10
6	North	Roscoe ES	15
6	North	Arminta ES	2
7	South	Gardena ES	33
7	South	Ritter ES	34

Sites were identified using the Green Schoolyards Index, which ranks sites based on the following datasets for each site: updated schoolyard measurement, existing green/natural components, CalEnviroScreen 4.0 score, and Extreme Heat Temperature Tool. The first eight sites on the list that do not have an approved or planned project that would provide substantial greening improvements* were selected. Additionally, in an effort to provide geographic equality, at least two high-ranked sites were selected in each Board District.

*(*Project types which will provide substantial greening improvements: comprehensive modernization, major modernization, classroom replacement, Pavement and Campus Exterior Upgrade (PACEUP) projects, Green Schoolyard Improvement Projects (Non-Division of the State Architect (DSA)/Americans with Disabilities Act (ADA), and third-party funded projects).*

Green Schoolyards Improvement Projects (Non-DSA)

Project Scope/Background: In addition to Green Schoolyard Upgrade Projects, Green Schoolyard Improvement Projects will be undertaken at 34 sites with \$39,500,000 of Restricted General Fund-ELOP. These projects were identified in Summer 2023, in order to utilize, to the extent possible, funding that expires on June 30, 2024. This was prior to the development of the Green Schoolyards Index, and work has already begun. The scope of the projects consists of new plantings, trees, turf, and/or decomposed granite within existing or new planting areas, and thus will not require Division of the State Architect (DSA) approval. Based on the scoping assumptions, all projects are anticipated to significantly increase the green space, getting each school as close to 30% as feasible.

In an effort to provide a level of geographic greening equality, and recognizing there are other significant and meaningful factors beyond the condition and adequacy of school facilities, two sites were selected in each Board District (14 total) based on an assessment of elementary school sites' ranking on the Greening 1.0 Index; their 2021-22 unduplicated pupil count of free/reduced-price meals, English learners, and foster youth; and the projects planned or underway that would provide incremental greening (Outdoor Learning Environment (OLE) and PACEUP projects). Of the remaining 20 sites, 18 were identified based on the aforementioned methodology with the exclusion of geographic equality, and the remaining two were identified to address pre-existing site concerns and a reoccurring safety hazard.

The Board's authorization to execute all instruments necessary, as legally permissible, to implement the projects, including budget modifications, will help support efforts to expedite the Green Schoolyard Improvement projects (Non-DSA) at the 34 sites below.

Board District	Region	Site Name	Greening 1.0 Index Rank	Percentage of Unduplicated Pupil Count of Free/Reduced-Price Meals, English Learners & Foster Youth 2021-2022
1	South	La Salle	8	98.69%
1	South	Manhattan ES	93	97.96%
1	South	Menlo ES	37	98.60%
1	South	Woodcrest ES	60	99.15%
1	West	Wilton ES	80	95.30%
2	East	Belvedere ES	49	99.45%
2	East	Breed ES	53	97.42%
2	East	Evergreen ES	41	96.44%
2	East	Ford ES	87	95.11%
2	East	Hamasaki Magnet ES	62	92.51%
2	East	Lorena ES	62	97.92%
2	East	Marianna ES	30	96.76%
2	East	Soto ES	36	96.69%
3	North	Capistrano ES	124	75.63%
3	North	Sunny Brae ES	37	93.50%
3	West	Alta Loma ES	111	98.11%
3	West	Windsor Hills Magnet ES	644	82.71%
4	North	Garden Grove ES	225	93.40%
4	West	Stoner ES	91	91.27%
5	East	28th St. ES	43	99.03%
5	East	Hughes ES	88	94.59%
5	East	Stanford ES	51	96.48%
5	South	Norwood ES	64	96.10%
5	West	Hobart ES	84	96.26%
5	West	Hoover ES	40	99.28%
5	West	Los Angeles ES	56	98.91%
6	North	Coldwater Canyon ES	42	96.17%
6	North	Lankershim ES	86	90.99%
7	South	109th St. ES	39	96.76%
7	South	118th St. ES	71	98.65%
7	South	66th St. ES	81	98.18%
7	South	75th St. ES	33	98.15%
7	South	Griffith-Joyner ES	77	99.48%
7	South	Russell ES	92	96.56%

Initial Budget and COPs Allocation:	\$ 25,000,000
Restricted General Fund-ELOP (Allocated):	\$ 89,500,000
<u>Anticipated Future Funding Allocation(s):</u>	<u>\$ 25,000,000</u>
Total Anticipated Program Budget (all funding sources):	\$139,500,000

Program Schedule: Construction of the first project is anticipated to begin in Q1-2024 and the final project is anticipated to be completed in Q4-2027.

8. Campus Safety Systems Improvement Projects

Project Scope: Design and install new video camera and intrusion alarm systems for 719 school sites, 291 of which are included in the initial phase of this work ([site list](#)). The scope may include, but is not limited to the design and installation of video camera systems for each individual campus, based on current design standards that are specified in technical design guidelines:

- o Campus Perimeter
- o Entrance (Main, Parking)
- o Rear/Service Entrance/Delivery
- o Exterior Doors
- o Parking Structure
- o Bus Loading/Unloading Zones
- o Large Assembly Areas
- o Stairwells
- o Corridors
- o Valuable Resources (Storage)
- o Other site-specific critical areas

Each project will include approximately 20 camera locations at smaller schools and 30 camera locations at larger schools, with each consisting of three to four cameras, or a total of 60 to 120 cameras per school site. The “large and small” school designation will be determined by student enrollment, number of buildings, and campus layout.

The new system will include remote monitoring capabilities through LASPD’s Operations Center. In total, 719 sites have been identified for a project, and additional funding allocations will be required to complete all projects.

Initial Budget/COPs Allocation:	\$146,000,000
<u>Future Anticipated Funding Allocation(s):</u>	<u>\$210,000,000</u>
Total Anticipated Project Budget:	\$356,000,000

Project Schedule: Construction is anticipated to begin in Q1-2024, with the first 291 projects to be completed in Q1-2026, and the entire program of 719 sites anticipated to be completed in Q4-2028.

9. Cybersecurity Improvement Program

Project Scope: Delivery of Districtwide cybersecurity enhancements that address vulnerabilities identified in the 2021 Information Security Audit as well as recommendations from the Cybersecurity Task Force, which was convened in the wake of the September 2022 cyber-attack. The Cybersecurity Improvement Program includes augmentation of people, processes, and technology tools to identify and mitigate the risk of future cyber-attacks and disruption to District operations, requiring capital and reoccurring operational expenditures. The capitalizable scope may include, but is not limited to:

- o *Enhancing Network Security Models, including Identity Management to Control Account Access and Manage Digital Identities:* Implement a centralized system to manage the lifecycle of user accounts required to access District applications, including access and authorization management. This effort will modernize the current decentralized systems for managing user account passwords and workflow-based authorizations.
- o *Cloud Migration of Core Assets and Applications:* Migrate on-site core applications, including the District's enterprise resource planning tool (SAP), Student Information System (MiSiS), Special Education System (Welligent), Food Services, Transportation, and others, to the Cloud to achieve a better security posture, reduce down-time, and enhance systems' performance.
- o *Redesign and Hardening of Network Architecture and Infrastructure:* Install and implement modern Data Center firewalls and segment critical applications to inspect and block potentially malicious traffic and insider threats.
- o *Vulnerability Assessment and Threat Management for Protection and Detection:* Configure security tools for recurring enterprise-level scans of critical systems and applications to support identification, classification, prioritization, remediation, and mitigation of vulnerabilities.
- o *Security Operations Center:* Centralize application and system security alerts that may be indicators of compromise, or malicious activities. Implementation of an Artificial Intelligence platform that supports a 24x7x365 security operations center to monitor security alerts and take action as deemed necessary.

The Cybersecurity Improvement Program will be executed in multiple phases, with the first phase focused on the highest priority actions to elevate the District's security posture per Audit and Task Force findings.

Initial Budget and COPs Allocation:	\$ 72,517,106
<u>Future Anticipated Funding Allocation(s):</u>	<u>\$109,242,394</u>
Total Anticipated Capital Program Budget:	\$181,759,500

Full implementation of the Cybersecurity Improvement Program is currently estimated to require \$88,258,550 of General Funds and is included in the Capital Plan.

Project Schedule: Implementation began in Q2-2023 and is anticipated to be completed in Q2-2026.



Board of Education Report

File #: Rep-247-24/25, Version: 1
In Control: Business & Finance Division

Agenda Date: 3/11/2025

Align Funding Strategies for Three School Facilities Projects/Programs Funded by Certificates of Participation (COPs 2023 Series A) with the School Upgrade Program Framework and Measure US Priorities and Implementation Strategies

Business & Finance Division

Facilities Services Division

Information Technology Services

Transportation Services Division

Brief Description:

(Align Funding Strategies for Three School Facilities Projects/Programs Funded by Certificates of Participation (COPs 2023 Series A) with the School Upgrade Program Framework and Measure US Priorities and Implementation Strategies) Recommends approval of the following actions to align funding strategies for three school facilities projects/programs funded by 2023 Series A Certificates of Participation (2023 COP) proceeds with the School Upgrade Program framework and Measure US priorities and implementation strategies.

Action Proposed:

Approve the following actions to align funding strategies for three school facilities projects/programs funded by 2023 COPs proceeds with the School Upgrade Program framework and Measure US priorities and implementation strategies:

1. Approve up-to \$250,000,000 in direct reallocations from three School Upgrade Program categories (Measure US proceeds specifically) of capital need to defease a portion of the 2023 COPs associated with three school facilities projects, as shown in Exhibit A (Updated School Upgrade Program).
2. Approve the allocation of \$251,880,057¹ of 2023 COPs proceeds into the School Upgrade Program, as shown in Exhibit A, to fund the underlying scope of the three school facilities projects.
3. Approve Strategic Execution Plan (SEP) amendments (Information Technology Services (ITS), Transportation Services Division (Transportation) and Facilities Services Division (Facilities)) to incorporate the three projects, Campus Safety Systems Improvements Program (Phase 1- 291 sites), Sun Valley electric school buses (180 buses), and Green Schoolyard Upgrade projects (15 projects), therein, as shown in Exhibit B, including allocating \$17,827,000 of Bond Program funds targeted in the School Upgrade Program for major modernizations, upgrades, and reconfigurations to school campus to fund construction activities for all 15 Green Schoolyard Upgrade projects.

¹\$251,880,057 represents the total COPs allocation for eligible project/program scope. It is more than the up-to \$250,000,000 of direct reallocations for defeasance because debt service was paid in 2023-2024, thereby reducing the amount that can be defeased.

4. Authorize the Chief Procurement Officer, the Chief Facilities Executive, the Chief Information Officer, and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the projects including budget modifications and the purchase of equipment and materials.

Background:

On June 13, 2023, the Board authorized a resolution approving the execution and delivery of COPs in the not-to-exceed amount of \$500,000,000 (Board Report No. 300-22/23). In August 2023, the 2023 COPs were sold generating \$423,500,000 to fund critical unmet needs of school support facilities and high-priority school facility needs for which sufficient bond funding was not available, in alignment with the Strategic Plan and Board of Education (Board) priorities. On December 12, 2023, the Board approved the use of \$423,500,000 of 2023 COPs proceeds to fund all or a portion of nine high-priority Capital Plan projects and/or programs, to be undertaken at one or more sites (Board Report No. 024-23/24).

Approximately one year after the 2023 COPs were sold, the Board authorized the placement of Measure US, a \$9,000,000,000 local public schools safety and upgrades measure on the November 5, 2024, general election ballot (Board Report No. 029-24/25). Measure US contained an explicit provision (Part Three of the Bond Project List-Miscellaneous) that funds from the Measure could be used to defease the portion of 2023 COPs attributable to projects authorized to be financed under the Measure (i.e. bond eligible projects). On November 5, 2024, voters authorized Measure US with 68.02% of the votes cast in support of the measure.

LA Unified is projected to meet its financial obligations in Fiscal Year 2025 and in the two subsequent fiscal years, and the Board will be requested to certify the District's financial condition as "Positive" at second interim financial report. However, to maintain a positive General Fund Unrestricted ending balance in the current three-year multi-year projection period, it is still anticipated that funds will need to be transferred from Local Reserve Fund 17 to the General Fund in FY26 and FY27, thereby reducing Local Reserves to 2% in FY27. Moreover, the estimated Cost-of-Living Adjustment (COLA) decrease in the Governor's proposed 2025-26 budget proposal, from 2.93% to 2.43% is estimated to have a \$29,000,000 impact on LA Unified in FY26.

With the approval of Measure US and the worsening of economic and budget conditions, the 2023 COPs Capital Plan projects/programs were recently evaluated against the Measure US priorities and implementation plan. Three of the projects/programs were identified as aligning with the priorities and implementation strategies and the historic use of local bond proceeds:

- Sun Valley Electric School Buses Project (180 buses)
- Green Schoolyard Upgrades (15 projects)
- Campus Information Technology (IT) Safety Systems Improvements Program (Phase 1: 291 sites)

Over the next 14 years, the District is required to pay an estimated \$504,000,000 in debt service on the 2023 COPs from the General Fund for all nine projects. \$11,300,000 of debt service was included in the 2023-24 budget, and for subsequent years the estimated annual payment is \$36,000,000. The next principal payment is due on October 1, 2025. Of the total estimated debt service, approximately \$303,000,000 is attributable to the three bond eligible projects/programs listed above, with an estimated annual debt service of \$21,600,000.

The proposal to align funding strategies for three school facilities projects/programs funded with 2023 COPs proceeds with the School Upgrade Program framework and Measure US priorities and implementation

strategies is being made to provide relief to the General Fund.

Bond Oversight Committee Recommendations:

This item was considered by the School Construction Bond Citizens' Oversight Committee (BOC) at its meeting on February 27, 2025. Pursuant to the Memorandum of Understanding (MOU) with the BOC, the District provided the BOC with the opportunity to consider the bond funded proposal and make a recommendation to the Board as to whether to approve or disapprove the proposal prior to presenting the item to the Board for final action. Following discussion, a vote was taken which resulted in 5 ayes, 4 nays, two abstentions, and two absences, as referenced in Exhibit C. Having fulfilled the requirements under the MOU, the proposal will proceed to the Board without a BOC recommendation. The presentation that was provided is included as Exhibit D.

Expected Outcomes:

Approval of four actions to align funding strategies for three school facilities projects/programs funded with 2023 COPs proceeds with the School Upgrade Program framework and Measure US priorities and implementation strategies. Actions include approval of up to \$250,000,000 in direct reallocations from Measure US to defease a portion of the 2023 COPs which are associated with three school facilities projects/programs: Sun Valley Electric School Buses Project, Green Schoolyard Upgrades (15 projects), and the Campus IT Safety Systems Improvements Program (Phase 1: 291 sites).

Board Options and Consequences:

If the Board approves the recommendation, savings to the General Fund of \$303,000,000 will be achieved. If the Board does not approve the recommended action, the savings will not be realized, and debt service will be paid through the General Fund. The estimated annual General Fund debt service for the three identified eligible projects/programs is \$21,600,000.

Policy Implications:

This action is compliant with Section 4.08 of the District's Debt Management Policy.

Budget Impact:

Because the GO Bonds will refund a significant portion (approximately 59.5%) of the 2023 COPs, the District's General Fund will be relieved of most of the debt service for the 2023 COPs. The identified projects will be funded with proceeds of the 2023 COPs and refinanced with bond proceeds, and debt service will be repaid by ad valorem property tax revenues, not the District's General Fund revenues. The refinancing, if approved, will achieve General Fund debt service savings of \$303,000,000 over the next 14 years (approximately \$21,600,000 per year and \$65,000,000 over the next three years of the multi-year projection). There are seven projects funded by the 2023 COPs which are not included in this refunding proposal. The District will continue to pay debt service of nearly \$207,000,000 from the General Fund for these projects.

The combined cost to defease the outstanding 2023 COPs associated with the three identified school facilities projects/programs is estimated to not-to-exceed \$250,000,000. The defeasance will be funded by Bond Program funds targeted in the School Upgrade Program, specifically associated with Measure US, for the replacement of aging and outdated school buses (\$75,000,000), IT infrastructure and system upgrades: comprehensive enhancements to school audio systems (\$104,500,000) and IT Safety Upgrades: video camera systems to improve safety of campus infrastructure (\$70,500,000). If less than \$250,000,000 is ultimately required to defease the applicable portion of the 2023 COPs for eligible projects, the remaining funds will be returned to their respective ITS School Upgrade Program category of need.

The original combined budget for the Green Schoolyard Upgrades was estimated at \$100,000,000 in December 2023. An initial funding allocation of \$75,000,000 was provided, which was expected to provide sufficient funding to complete pre-construction activities at all 15 sites and construction at a minimum of 11 sites. The funding strategy consisted of \$25,000,000 of 2023 COPs proceeds, an allocation of \$50,000,000 of Restricted General Fund-Expanded Learning Opportunities Program (ELO-P) funds, and a future allocation of \$25,000,000 to complete all the projects.

In aligning these 15 projects with the School Upgrade Program framework and Measure US priorities and implementation strategies, the combined total project budget is being updated to \$92,827,000 to reflect current information known, and assumptions about the project scope, site conditions, and market conditions. The project budgets will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise and will be adjusted accordingly to enable the successful completion of the projects.

Additionally, \$17,827,000 of bond program funds targeted in the School Upgrade Program for major modernizations, upgrades, and reconfigurations to school campuses is being allocated to fund construction activities for all 15 projects. Facilities staff, in collaboration with the Division of Instruction and the Office of the Chief Financial Officer, will continue to assess opportunities to leverage ELO-P entitlements on an annual basis to support these 15 Green Schoolyard Upgrade Projects. If ultimately there is an insufficient amount of ELO-P funds available, additional bond program funds will be allocated to complete these 15 projects.

Student Impact:

The proposal to defease a portion of the 2023 COPs with Measure US proceeds will provide General Fund relief by reducing General Fund debt service costs, thereby improving the position of the District's General Fund over the current three-year multi-year projection period.

Equity Impact:

N/A

Issues and Analysis:

The District is facing fiscal pressure on its operating funds due to a variety of factors including declining enrollment, expiration of ESSER funding, and the devastating wildfires. Defeasing a portion of the 2023 COPs for eligible projects now will save the General Fund \$303,000,000. However, if the District waits until 2033 when the longest-term debts can be paid off (maturities can be called), the savings to the General Fund would decline at the rate of \$21,600,000 per year for seven years (\$152,000,000 in total).

The cash from the original 2023 COPs proceeds will continue to be spent on the projects originally approved in 2023, and Measure US bond proceeds will be placed in an escrow account and used to pay the annual debt service on up-to \$250,000,000 of eligible 2023 COPs until 2033 when the bonds can be called. The 2023 COPs proceeds will be incorporated into the ITS, Transportation, and Facilities SEPs to support project/program implementation. Project/program expenditures and schedule updates will be reported in the same manner as bond funded projects.

As noted earlier, refinancing a portion of the 2023 COPs necessitates the reallocation of Measure US spending targets within the School Upgrade Program. The strategy proposed maintains funding for school greening and building resiliency projects, however it reduces funding targeted for school information technology

improvements and the replacement of aging/outdated school buses (as shown in Exhibit A).

Based on preliminary assessments, the reallocation is anticipated to impact future plans for school audio systems and video camera systems with Measure US funds as follows:

- **School Audio Enhancements:** Under the original Measure US spending target of \$521,000,000, 547 school sites were anticipated to be upgraded with updated school audio systems, including integrated and enhanced school internet protocol (IP) - public address speakers, IP-based master clocks, audio enhancement systems, such as classroom speakers for instruction, and mass notification systems. After the proposed reallocation, audio systems at 396 school sites are expected to be upgraded with the \$416,500,000 updated spending target. The outstanding need for upgraded school audio systems will remain at 323 school sites until additional funding is identified.
- **Campus Safety Systems Upgrades (Phase 2B):** Projects to modernize school technology safety systems consisting of video and intrusion alarm systems are underway at 321 school sites utilizing bond (30 sites) and 2023 COPs (291 sites) proceeds. These video camera and intrusion alarm systems (separate from secure entry projects) serve as a deterrent to potential offenders and assist with property protection. Under the original Measure US spending target of \$70,500,000, video and intrusion alarm system installations at an additional 231 sites were anticipated to be undertaken. With the reallocation, no new funding will be targeted and the outstanding need for campus technology safety systems upgrades will remain at 398 school sites until additional funding is identified.

If the \$75,000,000 targeted to replace aging and outdated school buses is redirected to defease eligible 2023 COPs, the Transportation Services Division will continue to aggressively pursue grant opportunities for electric school buses, for which there are many opportunities. Currently, there are 108 electric school buses on hand, 143 pending delivery, and recent grant awards for an additional 224. Approximately 900 aging buses remain to be replaced. Due to grant restrictions, the Measure US funding targeted for school buses could not have been used as a local match for a grant.

Attachments:

Exhibit A: Updated School Upgrade Program

Exhibit B: Scope, Schedule, and Budget for Three School Facilities Projects/Programs Funded
with Certificates of Participation (COPs 2023 Series A)

Exhibit C: BOC Resolution

Exhibit D: BOC Presentation

Submitted:

02/26/25

File #: Rep-247-24/25, Version: 1
In Control: Business & Finance Division

Agenda Date: 3/11/2025

RESPECTFULLY SUBMITTED,


ALBERTO M. CARVALHO
Superintendent


APPROVED & PRESENTED BY:


PEDRO SALCIDO
Deputy Superintendent
Office of the Deputy Superintendent

REVIEWED BY:


DEVORA NAVERA REED
General Counsel

APPROVED & PRESENTED BY:


CHRISTOPHER MOUNT-BENITES
Chief Financial Officer
Business & Finance Division

✓ Approved as to form.

REVIEWED BY:


NOLBERTO DELGADILLO
Deputy Chief Financial Officer

APPROVED & PRESENTED BY:


SOHEIL KATAL
Chief Information Officer
Information Technology Division

✓ Approved as to budget impact statement.

APPROVED & PRESENTED BY:


KRISZTINA TOKES
Chief Facilities Executive
Facilities Services Division

APPROVED & PRESENTED BY:


DANIEL KANG
Director of Transportation
Transportation Services Division

UPDATED SCHOOL UPGRADE PROGRAM

*Upgrading, Modernizing, and Replacing Aging and Deteriorating School Facilities, Updating Technology and
Addressing School Facilities Inequities*

CATEGORIES OF NEED GOALS DRIVING PROJECT DEVELOPMENT	Spending Target for Projects *	Remaining Available*	COPs Funding Added	ELO-P Funding Added	Measure US Reallocation For COPs	Less: Project Budgets	New Available Spending Target
FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN							
Major Modernizations, Upgrades, and Reconfigurations to School Campuses	\$11,617,591,963	\$4,220,825,579	\$25,000,000	\$50,000,000		(\$92,827,000)	\$4,202,998,579
Critical Replacements and Upgrades of School Building/Site Systems and Components	\$3,435,832,154	\$1,452,971,015					\$1,452,971,015
IT School Network Infrastructure Upgrades Executed by FSD	\$166,579,875	\$0					\$0
School Cafeteria Upgrades	\$645,457,501	\$492,561,590					\$492,561,590
School Upgrades and Reconfigurations to Support Wellness, Health, Athletics, Learning, and Efficiency	\$856,208,582	\$376,916,384					\$376,916,384
ADA Transition Plan Implementation	\$1,105,125,189	\$290,638,700					\$290,638,700
Charter School Facilities Upgrades and Expansions	\$839,360,745	\$572,377,176					\$572,377,176
Early Childhood Education Facilities Upgrades and Expansions	\$333,848,195	\$165,424,850					\$165,424,850
Adult and Career Education Facilities Upgrades	\$284,734,819	\$159,918,105					\$159,918,105
Board Member Priority Projects	\$89,188,612	\$62,351,027					\$62,351,027
Region Priority Projects	\$72,767,735	\$53,975,811					\$53,975,811
INFORMATION TECHNOLOGY DIVISION STRATEGIC EXECUTION PLAN							
Technology Infrastructure and System Upgrades	\$2,020,259,490	\$885,885,820	\$146,000,000		(\$104,500,000)	(\$146,000,000)	\$781,385,820
Upgrade and Equip Schools with 21st Century Technology	\$381,396,933	\$70,036,000					\$70,036,000
IT Campus Safety Upgrades	\$169,114,181	\$169,114,181			(\$70,500,000)		\$98,614,181
TRANSPORTATION SERVICES STRATEGIC EXECUTION PLAN							
Replace Aging and Polluting School Buses	\$141,875,000	\$75,000,000	\$80,880,057		(\$75,000,000)	(\$80,880,057)	\$0
CHIEF FINANCIAL OFFICER							
Defeasance of Certificates of Participation	\$0	\$0			\$250,000,000		\$250,000,000
OFFICE OF THE INSPECTOR GENERAL							
Conduct Inspector General Independent Audits of Board	\$110,000,000	\$69,839,769					\$69,839,769
TOTAL	\$22,269,340,974	\$9,117,836,007	\$251,880,057	\$50,000,000	\$0	(\$319,707,057)	\$9,100,009,007

*Includes all actions that modified the amount available for direct projects since the inception of the SUP in January 2014. Includes Measure US.

** As of 12/31/24 for Facilities managed programs

LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report

Exhibit B: Scope, Schedule, and Budget for Three School Facilities Projects/Programs
 Funded with Certificates of Participation (COPs 2023 Series A)

1. Sun Valley Electric Buses and Generator Purchases Project

Over the next 14 years, the District is required to pay nearly \$97.4 million in debt service for COPs issued for the purchase of 180 electric school buses (bond eligible scope). The debt service cost is currently obligated to be paid by the General Fund. The proposed project includes the defeasance of \$80,276,360 of debt service for COPs issued for the bond eligible scope of this project.

The underlying project will replace all 180 school buses based at the Sun Valley Transportation Center with zero-emissions electric school buses (ESBs). The ESBs will be equipped with the latest safety features, including Wi-Fi and a Global Positioning System (GPS), and will have a capacity for 42 or 78 passengers (depending on the model) and an operating range of approximately 125 miles with a full charge. Studies have shown that electric buses are more fuel efficient and significantly reduce the cost of repairs and maintenance. This can result in overall savings of up to \$1.8 million per year.

While not part of the bond funded scope of the project, including the defeasance, the overall project includes the purchase of 25 propane-powered generators to support ESB charging until the construction and installation of permanent charging infrastructure is completed (anticipated approximately two years after the delivery of the ESBs). A generator, situated on a trailer, can fully charge up to eight buses at one time in approximately six to eight hours. The chargers will be ordered and purchased, as needed, to coincide with the projected delivery of the ESBs. These generators will also be part of the energy contingency plan, in the event there is a widespread power outage. The District is required to pay approximately \$9.4 million in debt service over the next 14 years for the generators. This will be paid by the General Fund.

Budget:

The funding strategy consists of COPs proceeds and Measure US bond proceeds as follows:

- \$88,700,000: total project budget (including generators) funded by COPs
- \$80,880,057: total project budget for electric school buses only
 - COPs proceeds in the equivalent amount to be allocated to the School Upgrade Program for the replacement of aging and outdated school buses to support project implementation.
 - \$80,276,360: Measure US proceeds to be reallocated for defeasance of eligible project scope: replacement of aging/outdated school buses (\$75,000,000) and IT infrastructure and system upgrades: comprehensive enhancements to school audio systems (\$5,276,360)

Project Schedule: Purchases began in Q2-2023 and are anticipated to be completed in Q4-2025.

LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report

Exhibit B: Scope, Schedule, and Budget for Three School Facilities Projects/Programs
 Funded with Certificates of Participation (COPs 2023 Series A)

2. Green Schoolyard Upgrade Projects

Over the next 14 years, the District is required to pay nearly \$30.1 million in debt service for COPs issued to fund a portion of 15 green schoolyard upgrade projects. The debt service cost is currently obligated to be paid by the General Fund. The proposed project includes the defeasance of \$24,813,398 of debt service for COPs issued for this project.

The underlying projects will provide upgrades to schoolyards to align with the goal of providing 30% of a school sites' schoolyard with green/natural spaces. The scope may include replacing significant areas of paved surfaces with permeable surfaces that incorporate native/drought tolerant planting, the addition of natural grass play fields, the installation of trees and other shade elements to achieve 20% shade in the schoolyard, irrigation, decomposed granite and pavers, outdoor classroom elements, as well as accessibility improvements, as required, to ensure equal access to all students.

In December 2023, sites were identified using the Green Schoolyards Index, which ranks sites based on the following datasets for each site: updated schoolyard measurements, CalEnviroScreen 4.0 score, and Extreme Heat Temperature Tool. The first eight sites on the list that do not have an approved or planned project that would provide substantial greening improvements were selected. Additionally, in an effort to provide geographic equality, at least two high-ranked sites were selected in each Board District. Subsequently, one of the designated campuses in Board District 1, Marvin Elementary School, was identified as having an active paving replacement project which would address greening improvements. As a result, in November 2024 (Board Report No. 106-24/25), the Board approved the replacement of the project at Marvin Elementary School with a project at Budlong Elementary School, the next Board District 1 school on the priority list without a greening project.

Board District	Region	Site Name	Green Schoolyards Index Rank	Budget	Construction Start	Construction Completion
1	South	Manchester ES	84	\$6,493,000	Q3-2026	Q4-2027
1	West	Budlong ES	92	\$6,308,000	Q3-2026	Q4-2027
2	East	Bridge ES	4	\$2,758,000	Q4-2026	Q1-2028
2	East	Dena ES	7	\$4,008,000	Q3-2026	Q4-2027
3	North	Canoga Park ES	16	\$6,863,000	Q3-2026	Q4-2027
3	North	Sylvan Park ES	30	\$6,941,000	Q4-2026	Q1-2028
4	North	Vanalden ES	31	\$10,866,000	Q4-2026	Q1-2028
4	North	Encino ES	113	\$6,185,000	Q4-2026	Q1-2028
5	East	San Pedro ES	5	\$5,117,000	Q3-2026	Q4-2027
5	East	Heliotrope ES	8	\$5,259,000	Q4-2026	Q1-2028
6	North	Strathern ES	10	\$6,743,000	Q4-2026	Q1-2028
6	North	Roscoe ES	15	\$7,678,000	Q4-2026	Q1-2028

LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report

Exhibit B: Scope, Schedule, and Budget for Three School Facilities Projects/Programs
 Funded with Certificates of Participation (COPs 2023 Series A)

Board District	Region	Site Name	Green Schoolyards Index Rank	Budget	Construction Start	Construction Completion
6	North	Arminta ES	2	\$5,805,000	Q3-2026	Q4-2027
7	South	Gardena ES	33	\$6,072,000	Q3-2026	Q4-2027
7	South	Ritter ES	34	\$5,731,000	Q4-2026	Q1-2028

Budget:

The original combined budget for the green schoolyard upgrade projects was estimated at \$100,000,000 in December 2023. An initial funding allocation of \$75,000,000 was provided, which was expected to provide sufficient funding to complete pre-construction activities at all 15 sites and construction at a minimum of 11 sites. The funding strategy consisted of \$25,000,000 of 2023 COPs proceeds, an allocation of \$50,000,000 of Restricted General Fund-Expanded Learning Opportunities Program (ELO-P) funds, and a future allocation of \$25,000,000 to complete all the projects.

In aligning these 15 projects with the School Upgrade Program framework and Measure US priorities and implementation strategies, the combined total project budget is being updated to \$92,827,000 to reflect current information known, and assumptions about the project scope, site conditions, and market conditions. The project budgets will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise and will be adjusted accordingly to enable the successful completion of the projects.

Additionally, \$17,827,000 of bond program funds targeted in the School Upgrade Program for major modernizations, upgrades, and reconfigurations to school campuses is being allocated to fund construction activities for all 15 projects. Facilities staff, in collaboration with the Division of Instruction and the Office of the Chief Financial Officer, will continue to assess opportunities to leverage ELO-P entitlements on an annual basis to support these 15 Green Schoolyard Upgrade Projects. If ultimately there is an insufficient amount of ELO-P funds available, additional bond program funds will be allocated to complete these 15 projects.

The funding strategy consists of COPs proceeds, ELO-P funds, and bond program funds, as follows:

- \$92,827,000: total project budget
 - \$25,000,000: COPs proceeds to be allocated to the School Upgrade Program for major modernizations, upgrades, and reconfigurations to support implementation of the projects.
 - \$24,813,000: Measure US proceeds to be reallocated for defeasance of COPs from funds targeted for IT infrastructure and system upgrades: comprehensive enhancements to school audio systems
 - \$50,000,000: ELO-P allocation
 - \$17,827,000: bond program funding targeted in the School Upgrade Program for major modernizations, upgrades, and reconfigurations to school campuses

LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report

Exhibit B: Scope, Schedule, and Budget for Three School Facilities Projects/Programs
 Funded with Certificates of Participation (COPs 2023 Series A)

3. Campus Information Technology (IT) Safety Systems Improvements Program (Phase 1: 291 sites)

Over the next 14 years, the District is required to pay approximately \$175.7 million in debt service for COPs issued for improvements to campus safety systems at 291 sites. The debt service cost is currently obligated to be paid by the General Fund. The proposed project includes the defeasance of \$144,910,242 of debt service for COPs issued for this program.

The underlying project includes the design and installation of new video camera and intrusion alarm systems at 291 sites ([site list](#)). Each project will include approximately 20 camera locations at smaller schools and 30 camera locations at larger schools, with each consisting of three to four cameras, or a total of 60 to 120 cameras per school site. The “large and small” school designation will be determined by student enrollment, number of buildings, and campus layout. The new systems will include remote monitoring capabilities through LASPD’s Operations Center.

Each project will include approximately 20 camera locations at smaller schools and 30 camera locations at larger schools, with each consisting of three to four cameras, or a total of 60 to 120 cameras per school site. The “large and small” school designation will be determined by student enrollment, number of buildings, and campus layout. The new systems will include remote monitoring capabilities through LASPD’s Operations Center.

Budget:

The funding strategy consists of COPs proceeds and Measure US proceeds as follows:

- \$146,000,000: total project budget
 - \$146,000,000: COPs proceeds to be allocated to the School Upgrade Program for IT Safety Upgrades: video camera systems to improve safety of campus infrastructure, to support implementation of the program.
 - \$144,910,242: Measure US proceeds to be reallocated for defeasance of COPs from funds targeted for IT Safety Upgrades: video camera systems to improve safety of campus infrastructure

Project Schedule: The project began in Q1-2024, with construction anticipated to substantially complete at all 291 sites by Q1-2027.

SCHOOL CONSTRUCTION BOND CITIZENS' OVERSIGHT COMMITTEE

D. Michael Hamner, FAIA, Chair
American Institute of Architects
Robert Campbell, Vice-Chair
L.A. Co. Auditor-Controller's Office
Dr. Samantha Rowles, Secretary
LAUSD Student Parent
Patrick MacFarlane, Executive Committee
Early Education Coalition
Scott Pansky, Executive Committee
L.A. Area Chamber of Commerce

Joseph P. Buchman – Legal Counsel
Burke, Williams & Sorensen, LLP
Lori Raineri and Keith Weaver – Oversight Consultants
Government Financial Services Joint Powers Authority

Neelura Bell
CA Charter School Association
Sandra Betts
CA Tax Reform Assn.
Chad Boggio
L.A. Co. Federation of Labor AFL-CIO
Aleigh Lewis
L.A. City Controller's Office
Jennifer McDowell
L.A. City Mayor's Office
Brian Mello
Assoc. General Contractors of CA
Santa Ramirez
Tenth District PTSA

William O. Ross IV
31st District PTSA
Dr. Bevin Ashenmiller (Alternate)
Tenth District PTSA
Ashley Kaiser (Alternate)
Assoc. General Contractors of CA
Connie Yee (Alternate)
L.A. Co. Auditor-Controller's Office
Vacant
Senior Citizens' Organization
Vacant
LAUSD Student Parent

Timothy Popejoy
Bond Oversight Administrator
Perla Zitle
Bond Oversight Coordinator

RESOLUTION 2025-08

BOARD REPORT NO. 247-24/25

**RECOMMENDING BOARD APPROVAL REGARDING PROJECTS TO BE REFINANCED
WITH EXPENDITURES OF GENERAL OBLIGATION BOND PROCEEDS AND TO AMEND
THE STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN**

WHEREAS, on August 31, 2023, the Los Angeles Unified School District ("District") executed and delivered its \$384,260,000 Certificates of Participation, 2023 Series A (Sustainability Bonds) (the "2023 COPs") for the purposes of funding the projects listed in Board Report No. 247-24/25, a copy of which is attached hereto in the form it was presented to the BOC and is incorporated herein by this reference; and

WHEREAS, at an election held on November 5, 2024, the voters of the District approved the District's Measure US bond proposition ("Measure US"), approving the issuance by the District of not to exceed \$9.0 billion in general obligation bonds, and included the prepayment of the 2023 COPs allocated to bond-approved projects as an allowable use of Measure US bond proceeds; and

WHEREAS, District staff has determined that the refunding of a portion of the 2023 COPs (the "Project") with Measure US GO bond proceeds is consistent with the District's commitment to address unmet school facilities needs and provide students with a safe and healthy learning environment; and

WHEREAS, District staff has concluded that the proposed amendments to the Strategic Execution Plans ("SEP") will facilitate the District's ability to successfully complete the SEPs; and

WHEREAS, the Board of Education's approval of the Project will authorize District staff to proceed with the expenditure of Bond Program funds to undertake the Project in accordance with the provisions set forth in the District's Measure US; and

WHEREAS, the District Office of General Counsel has reviewed the Project and determined that it may proceed to the School Construction Bond Citizens' Oversight Committee ("BOC") for its consideration for recommendation to the Board of Education.

RESOLUTION 2025-08**RECOMMENDING BOARD APPROVAL REGARDING PROJECTS TO BE REFINANCED WITH EXPENDITURES OF GENERAL OBLIGATION BOND PROCEEDS AND TO AMEND THE STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN**

WHEREAS, Los Angeles Unified Staff has concluded that the proposed Information Technology Services, Facilities Services Division and Transportation Services Division SEP amendments will facilitate Los Angeles Unified's ability to successfully implement the SEPs.

NOW, THEREFORE, BE IT RESOLVED THAT:

1. The BOC recommends the Board of Education approve three school facilities projects/programs – Campus Safety Systems Improvements Program (Phase 1 – 291 sties), Sun Valley electric school buses (180 buses), and Green Schoolyard Upgrade projects (15 projects) – be refinanced with General Obligation Bond Proceeds of up to \$250,000,000 for partial defeasance of the 2023 COPs for the proposed three projects/programs, and amend the SEP to incorporate therein, as described in Board Report No. 247-24/25, a copy of which is attached hereto in the form it was presented to the BOC and is incorporated herein by reference.
2. This resolution shall be transmitted to the Los Angeles Unified School District Board of Education and posted on the BOC's website.
3. The District is requested to track the above recommendation and to report on the adoption, rejection, or pending status of the recommendations as provided in section 6.2 of the Charter and Memorandum of Understanding between the BOC and the District.

ADOPTED on February 27, 2025, by the following vote:

AYES: 5

ABSTENTIONS: 2

NAYS: 4

ABSENCES: 2

Robert Campbell
Vice-Chair

Dr. Samantha Rowles
Secretary



LAUSD UNIFIED

**Align Funding Strategies for Three School Facilities Projects/Programs
Funded by Certificates of Participation with the School Upgrade Program
Framework and Measure US Priorities and Implementation Strategies**

**Bond Oversight Committee Meeting
February 27, 2025**

Overview



- Align three school facilities projects/programs funded with the 2023 Certificates of Participation (COPs) with School Upgrade Program framework and Measure US priorities and implementation strategies

- Reallocate up to \$250M of Measure US funds to defuse a portion of 2023 COPs
- Allocate \$251.88M of 2023 COPs proceeds into School Upgrade Program to implement three projects/programs
- Approve Strategic Execution Plan Amendments to incorporate three projects/programs, and update funding strategy for one project/program to fund construction at all sites

Background - Timeline



- June 2023: Board authorized execution of Certificates of Participation (COPs) for a not-to-exceed amount of \$500M
- August 2023: COPs generating \$423.5M sold
- December 2023: Board approves use of \$423.5M of COPs to fund all or a portion of 9 programs/projects
- August 2024: Board authorizes placement of \$9B local bond measure on the November 2024 ballot
- November 2024: Voters approve \$9B Measure US local school bond

9 Projects/Programs - COPS Allocation



307

Project/Program Description	COPS Allocation	Future Anticipated Allocation*	Total Anticipated Project Budget*
Sun Valley Transportation Center Electrification Project	\$72,162,739	\$7,957,901	\$80,120,640
Electric Buses & Generator Purchases (Sun Valley)	\$88,700,000	\$0	\$88,700,000
Enrollment Modernization	\$2,000,000	\$0	\$2,000,000
Student Information Systems Upgrades	\$1,000,000	\$0	\$1,000,000
Student Support Applications Modernization	\$11,400,000	\$3,000,000	\$14,400,000
Campus Safety System Improvements	\$146,000,000	\$210,000,000	\$356,000,000
Student Data Analytics, Reporting and Dashboards	\$4,763,040	\$844,800	\$5,607,840
Cybersecurity Improvement Program	\$72,517,106	\$109,242,394	\$181,759,500
Green Schools for All Program	\$25,000,000	\$25,000,000	\$139,500,000**
Grand Total	\$423,542,885	\$356,045,095	\$777,387,980

* as of December 2023

** includes ELO-P allocation



174

2023 COPs Debt Service



308

- Term: 2025-2038
- 2033: Date longest term debts can be paid off (maturities called)
- Estimated debt service over term: \$504M
- Debt service included in 2023-24 budget: \$11.3M
- Estimated annual General Fund debt service for subsequent years: \$36M
- Next principal payment: October 1, 2025

18

Measure US Bond Language



REFINANCING OF CERTIFICATES OF PARTICIPATION (Retiring Existing Debt)

Acquisition of all or a portion of any school site or facility, or an interest therein, or make lease payments with respect to any school site or facility, encumbered in order to finance capital projects pursuant to the portion of the District's Los Angeles Unified School District Certificates of Participation, 2023 Series A (Sustainability Bonds), executed and delivered on August 31, 2023, attributable to projects which are authorized to be financed under this measure (i.e., bond eligible projects).

Measure US Priorities



310

- Enhance school safety
- Modernize school facilities
- Upgrade school sites
- Enhance accessibility
- Address facility inequities
- Update school and learning technology
- Support the health and well-being of students: enhance and expand outdoor spaces and food services
- Promote efficiency



20

COPs Capital Projects and Measure US 311



- Purchase Electric School Buses (180)
 - Total project budget: \$80.88M (COPs proceeds)
 - Total defeasement: \$80.3M (Measure US reallocation)
- Campus IT Safety System Improvements (Phase 1: 291 sites)
 - Total project budget: \$146M (COPs proceeds)
 - Total defeasement: \$144.9M (Measure US reallocation)
- Green Schools for All Program (15 sites)
 - Total project budget: \$92.82M
 - + COPs proceeds: \$25M
 - + Expanded Learning Opportunities Program: \$50M
 - + Bond Program funds: \$17.82M (major modernizations SUP category of need)
 - Total defeasement: \$24.8M

Measure US Reallocations



Category of Need/Measure US Implementation Strategy	Total Measure US Available	Proposed Reallocation	Revised Available
Comprehensive Enhancements to School Audio Systems	\$521.0	(\$104.5)	\$416.5
Video Camera Systems to Improve Safety of Campus Infrastructure	\$70.5	(\$70.5)	\$0.0
Replace Aging and Outdated School Buses	\$75.0	(\$75.0)	\$0.0

Strategy maintains funding for school greening and building resiliency projects in light of recent fire, wind and rain events

COPs Defeasance



313

- General fund impacts for 3 projects/programs
 - Total savings: \$303M
 - Annual debt service savings: \$21.6M/year
- The original COPs proceeds (cash) will continue to be spent on the projects originally approved in 2023
- Bond eligible projects and funding will be incorporated into the Strategic Execution Plans
- Why Now?
 - Worsening of economic and budget conditions
 - Projects/programs align with Bond Program priorities and implementation strategies
 - Waiting until 2023 would equate to a savings of approximately \$152M compared to \$303M

23

Three School Facilities Projects/Programs

24

Transportation Services: Sun Valley Electric School Buses Project



315

- Purchase of 180 Electric School Buses
- 150 Type D – 78 passenger school buses
- 30 Type C – 42 passenger school buses

Purchase commenced in Q2 2023

Deliveries started in Q4 2024

- Receiving 10 – 12 per week
- Delivery expected to be complete by Q2 2025

25

Information Technology Services: Campus Safety Systems – Phase 1



The Campus Safety Systems Project is crucial for addressing the growing security concerns and vulnerabilities in Los Angeles Unified. Safe schools are fundamental to creating a positive and effective learning environment. However, many of the District's schools currently face significant challenges due to outdated, malfunctioning, and often non-operational or non-existent physical security and video systems. These outdated or non-existent systems leave schools increasingly exposed to security risks, particularly during non-school hours, such as holidays or weekends, when campuses are unoccupied.



Outdated Safety Cameras




Enhanced Camera System

Information Technology Services: Campus Safety Systems – Phase 1

317



Overview

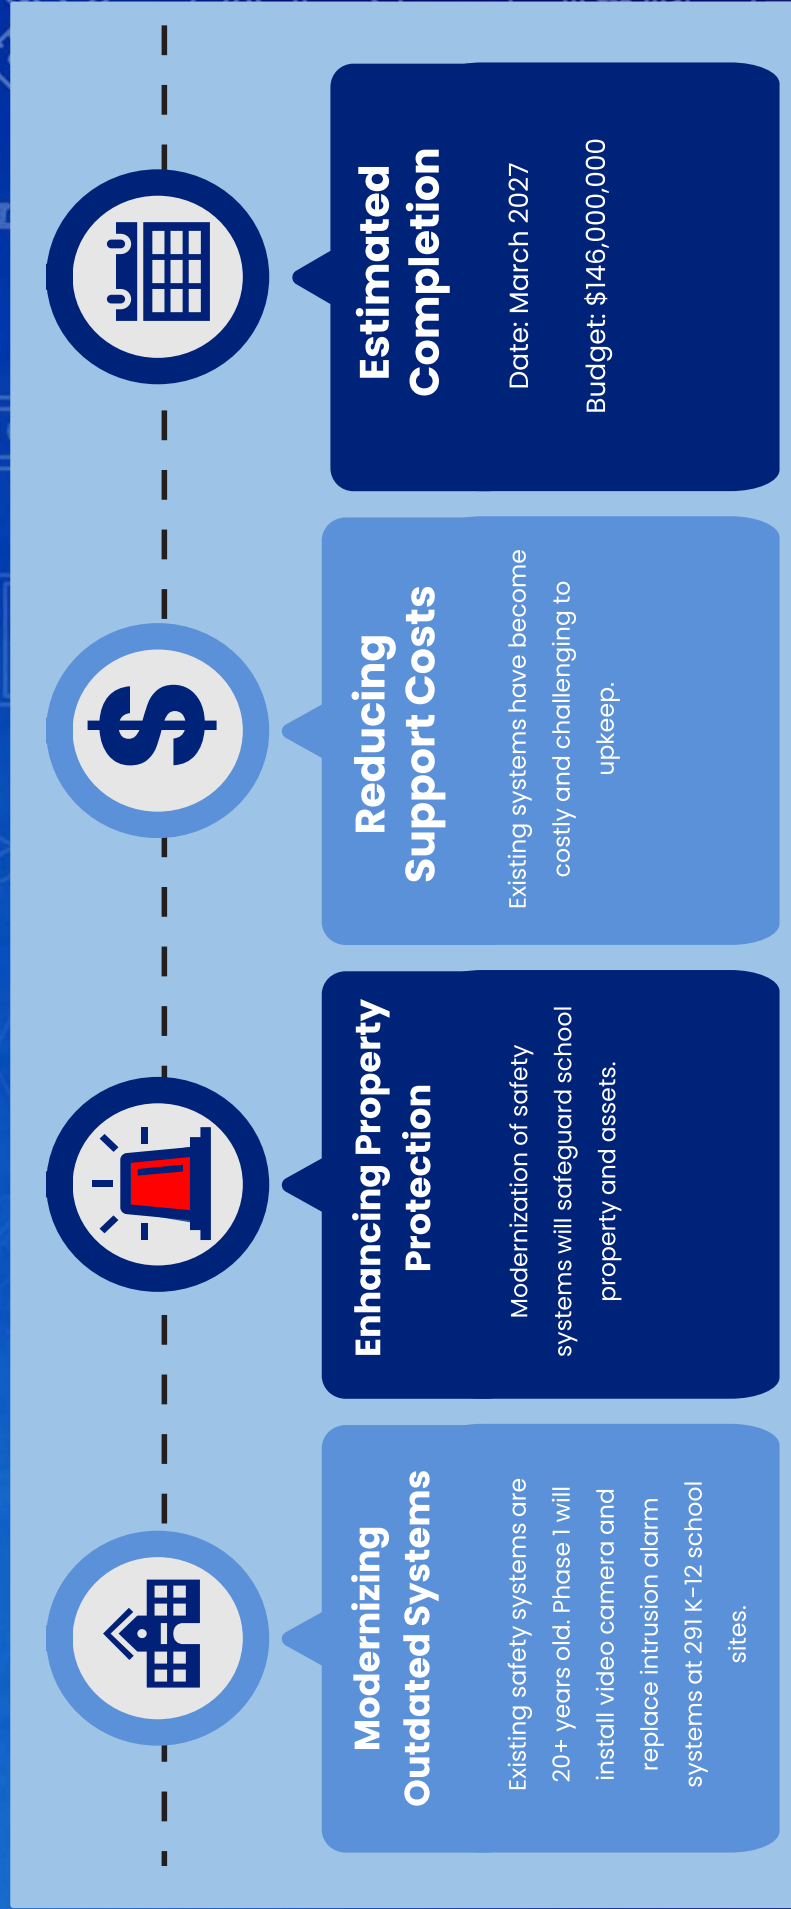

27

Information Technology Services: Campus Safety Systems – Phase I

318

Progress

Project Description: Design and install new video camera and intrusion alarm systems at 291 sites



	Q4 23	Q1 24	Q2 24	Q3 24	Q4 24	Q1 25	Q2 25	Q3 25	Q4 25	Q1 26	Q2 26	Q3 26	Q4 26	Q1 27
Video Camera/Intrusion Survey and Design	4	64	187	240	288									
Video Camera Installation	0	0	0	7	25									
Intrusion Alarm Installation	0	0	0	0	1									
Completed in Quarter	0	0	0	0	0									
Total Schools Substantially Completed	0	0	0	0	0									
Total Schools Target	0	0	0	0	0	10	40	70	100	138	176	214	252	291

Note: all figures in the above table are cumulative/running totals, except for figures in the "Completed in Quarter" row.

Facilities Services Division: Green Schoolyard Upgrade Projects

319



Project Overview: Upgrade campuses by converting schoolyard from paved surfaces to have 30% green/natural spaces

Project Scope

- Surface Conversion - Replacing paved areas with permeable, natural surfaces
- Green Elements - Native/drought-tolerant plants, natural grass play fields, strategic tree placement (20% shade coverage goal)
- Infrastructure Improvements - Landscaping and irrigation systems, decomposed granite and pavers, outdoor classroom spaces, resurfacing and restriping of remaining asphalt
- Accessibility Enhancements - Upgrades designed for equal access

29

Prioritizing and Identifying Projects



320

Green Schoolyards Index

Developed to prioritize schools based on their need for green/natural spaces

Qualifying Schools

205 Elementary Schools with a schoolyard with less than 10% Green/Natural space

Selection Criteria

- Top 8 ranked schools without existing greening projects
- Geographic equity: minimum of two high-ranked sites per Board District

30

15 Green Schoolyard Upgrade Projects



321

Board District	Region	Site Name	Green Schoolyards Index Rank	Construction Start	Construction Completion	Budget
1	South	Manchester ES	84	Q3-2026	Q4-2027	\$6,493,000
1	West	Budlong ES	92	Q3-2026	Q4-2027	\$6,308,000
2	East	Bridge ES	4	Q4-2026	Q1-2028	\$2,758,000
2	East	Dena ES	7	Q3-2026	Q4-2027	\$4,008,000
3	North	Canoga Park ES	16	Q3-2026	Q4-2027	\$6,863,000
3	North	Sylvan Park ES	30	Q4-2026	Q1-2028	\$6,941,000
4	North	Vanalden ES	31	Q4-2026	Q1-2028	\$10,866,000
4	North	Encino ES	113	Q4-2026	Q1-2028	\$6,185,000
5	East	San Pedro ES	5	Q3-2026	Q4-2027	\$5,117,000
5	East	Heliotrope ES	8	Q4-2026	Q1-2028	\$5,259,000
6	North	Strathern ES	10	Q4-2026	Q1-2028	\$6,743,000
6	North	Roscoe ES	15	Q4-2026	Q1-2028	\$7,678,000
6	North	Arminta ES	2	Q3-2026	Q4-2027	\$5,805,000
7	South	Gardena ES	33	Q3-2026	Q4-2027	\$6,072,000
7	South	Ritter ES	34	Q4-2026	Q1-2028	\$5,731,000
					Total	\$92,827,000

31

18

382

Manchester ES Green Schoolyard Upgrade Project 322

Board District 1, Region South



Project Scope

Site Improvements

- Replace approximately **51,700** square feet of paving in the main playground with green/natural surfaces. Currently, there is approximately **8%** green/natural spaces in the schoolyard.
- Greening improvements may include native/drought tolerant planting, natural grass play fields, trees and other shade elements, outdoor learning elements, landscaping with irrigation, decomposed granite and pavers, and planting areas in alignment with the District's Green Schoolyards for All Plan (April 2024).
- Asphalt resurfacing and restriping as necessary
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget


• Site & Environmental Plans	\$6,493,000
• Construction	2.5%
• Management	12.1%
• Other/Reserve	70.7%
	8.3%
	6.4%

Anticipated Construction Schedule

- Construction Start Q3-2026
- Construction Complete Q4-2027



Enrollment (2024-25):	513	Development Zone
-----------------------	-----	------------------





Project Scope

Site Improvements

- Replace approximately **41,800** square feet of paving in the main playground with green/natural surfaces. Currently, there is approximately **4%** green/natural spaces in the schoolyard.
- Greening improvements may include native/drought tolerant planting, natural grass play fields, trees and other shade elements, outdoor learning elements, landscaping with irrigation, decomposed granite and pavers, and planting areas in alignment with the District's Green Schoolyards for All Plan (April 2024).
- Asphalt resurfacing and restriping as necessary
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget

• Site & Environmental	\$6,308,000
• Plans	2.3%
• Construction	12.0%
• Management	71.0%
• Other/Reserve	8.3%
	6.4%

Anticipated Construction Schedule

- Construction Start
- Construction Complete

Enrollment
(2024-25):

624

33
20

LEGEND
Development
Zone

Bridge ES– Green Schoolyard Upgrade Project

Board District 2, Region East



324

Project Scope

Site Improvements

- Replace approximately **22,400** square feet of paving in the main playground with green/natural surfaces. Currently, there is approximately **1%** green/natural spaces in the schoolyard.
- Greening improvements may include native/drought tolerant planting, natural grass play fields, trees and other shade elements, outdoor learning elements, landscaping with irrigation, decomposed granite and pavers, and planting areas in alignment with the District's Green Schoolyards for All Plan (April 2024).
- Asphalt resurfacing and restriping as necessary
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget

• Site & Environmental	\$2,758,000
• Plans	4.2%
• Construction	11.4%
• Management	70.2%
• Other/Reserve	8.1%
	6.1%

Anticipated Construction Schedule

- Construction Start Q4-2026
- Construction Complete Q1-2028




Enrollment
(2024-25):

178

LEGEND



Development
Zone



385

Dena ES – Green Schoolyard Upgrade Project

Board District 2, Region East



Project Scope

Site Improvements


- Replace approximately **37,500** square feet of paving in the main playground with green/natural surfaces. Currently, there is approximately **2%** green/natural spaces in the schoolyard.
- Greening improvements may include native/drought tolerant planting, natural grass play fields, trees and other shade elements, outdoor learning elements, landscaping with irrigation, decomposed granite and pavers, and planting areas in alignment with the District's Green Schoolyards for All Plan (April 2024).
- Asphalt resurfacing and restriping as necessary
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget

• Site & Environmental Plans	\$4,008,000
• Construction	3.2%
• Management	11.8%
• Other/Reserve	70.7%
	8.1%
	6.2%

Anticipated Construction Schedule

- Construction Start Q3-2026
- Construction Complete Q4-2027

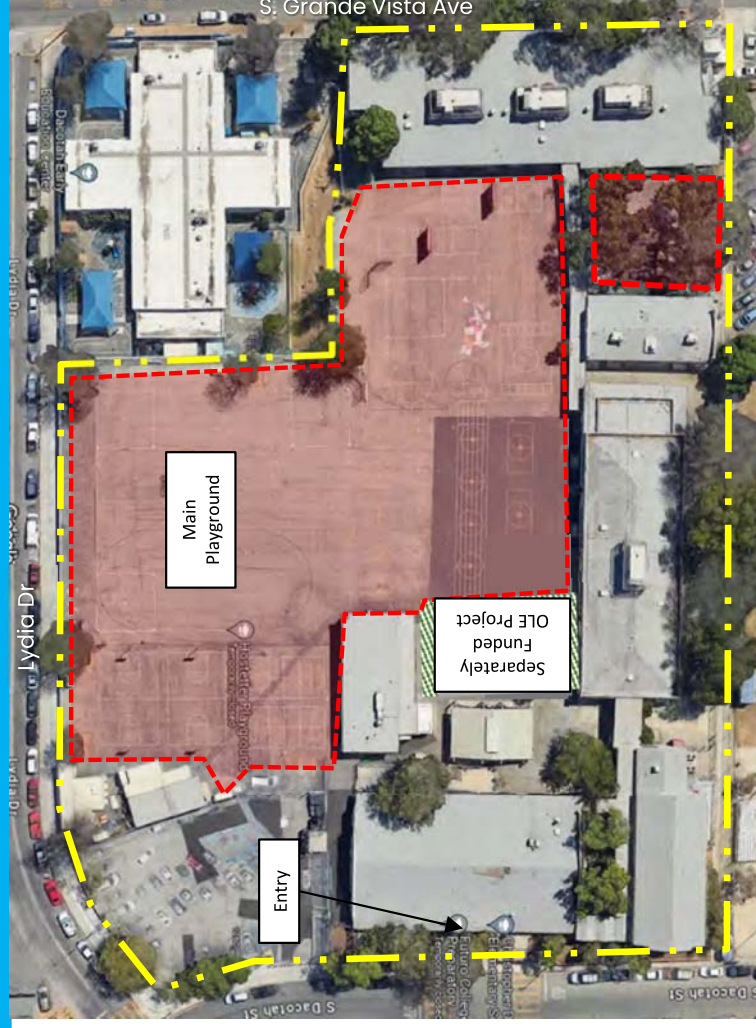

Enrollment (2024-25):	316
-----------------------	-----



Canoga Park ES – Green Schoolyard Upgrade Proj 326t

Board District 3, Region North



Project Scope

Site Improvements


- Replace approximately **49,600** square feet of paving in the main playground with green/natural surfaces. Currently, there is approximately **3%** green/natural spaces in the schoolyard.
- Greening improvements may include native/drought tolerant planting, natural grass play fields, trees and other shade elements, outdoor learning elements, landscaping with irrigation, decomposed granite and pavers, and planting areas in alignment with the District's Green Schoolyards for All Plan (April 2024).
- Asphalt resurfacing and restriping as necessary
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget

- Site & Environmental Plans \$6,863,000
- Construction 2.1%
- Management 12.1%
- Other/Reserve 71.0%
- 8.4%
- 6.4%

Anticipated Construction Schedule

- Construction Start Q3-2026
- Construction Complete Q4-2027

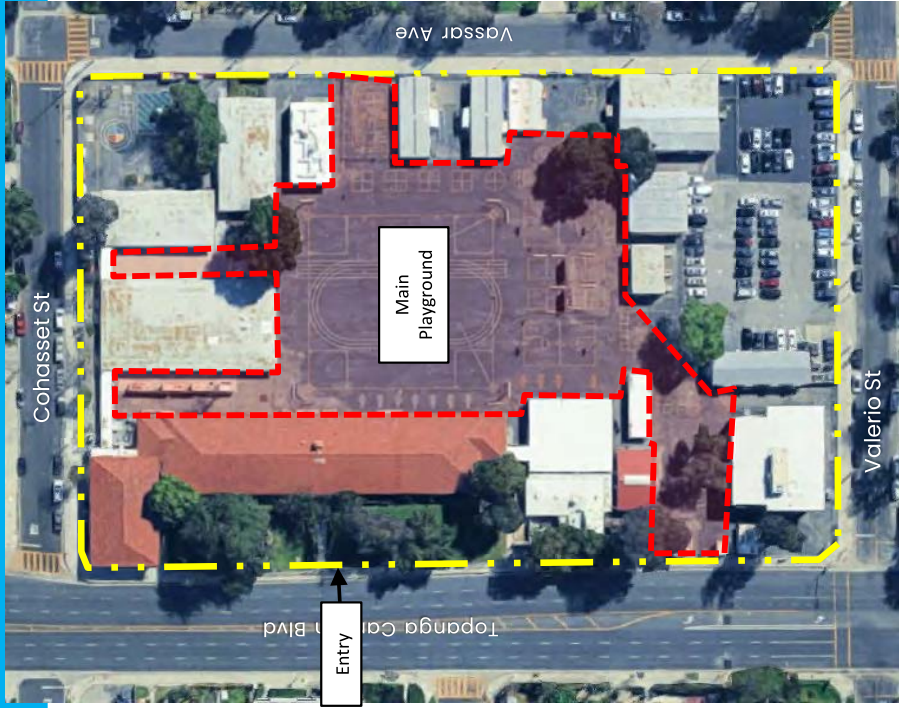

Enrollment (2024-25):	462
-----------------------	-----

LEGEND
 Development Zone

Sylvan Park ES – Green Schoolyard Upgrade Project

Board District 3, Region North



Project Scope

Site Improvements

- Replace approximately **51,800** square feet of paving in the main playground with green/natural surfaces. Currently, there is approximately **6%** green/natural spaces in the schoolyard.
- Greening improvements may include native/drought tolerant planting, natural grass play fields, trees and other shade elements, outdoor learning elements, landscaping with irrigation, decomposed granite and pavers, and planting areas in alignment with the District's Green Schoolyards for All Plan (April 2024).
- Asphalt resurfacing and restriping as necessary
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget

- | | |
|------------------------|-------------|
| • Site & Environmental | \$6,941,000 |
| • Plans | 2.3% |
| • Construction | 12.2% |
| • Management | 70.8% |
| • Other/Reserve | 8.3% |
| | 6.4% |


Anticipated Construction Schedule

- | | |
|-------------------------|---------|
| • Construction Start | Q4-2026 |
| • Construction Complete | Q1-2028 |



Enrollment
(2024-25):

645



Vanalden ES- Green Schoolyard Upgrade Project 328

Board District 4, Region North



Project Scope

Site Improvements


- Replace approximately **81,900** square feet of paving in the main playground with green/natural surfaces. Currently, there is approximately **7%** green/natural spaces in the schoolyard.
- Greening improvements may include native/drought tolerant planting, natural grass play fields, trees and other shade elements, outdoor learning elements, landscaping with irrigation, decomposed granite and pavers, and planting areas in alignment with the District's Green Schoolyards for All Plan (April 2024).
- Asphalt resurfacing and restriping as necessary
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget

- Site & Environmental
 - Plans
 - Construction
 - Management
 - Other/Reserve
- | |
|--------------|
| \$10,866,000 |
| 1.7% |
| 12.3% |
| 71.2% |
| 8.4% |
| 6.4% |

Anticipated Construction Schedule

- Construction Start
 - Construction Complete
- | |
|---------|
| Q4-2026 |
| Q1-2028 |

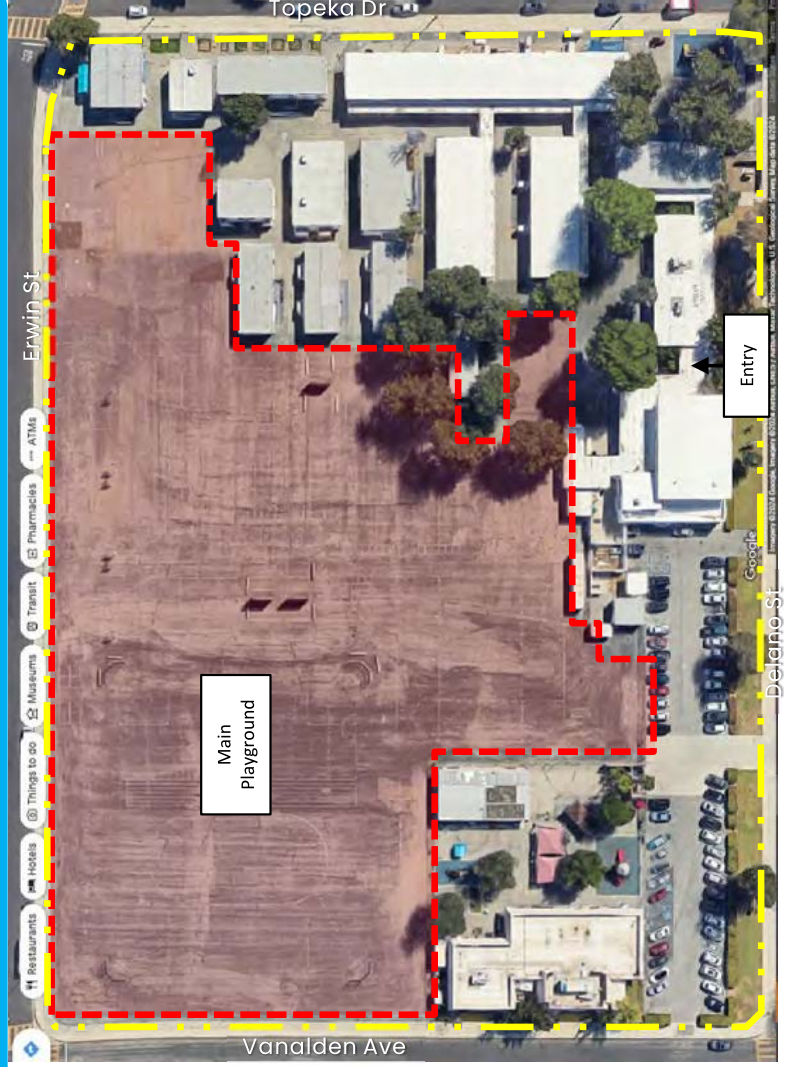

LEGEND

Development Zone

Enrollment (2024-25):	366
-----------------------	-----

N

38

25

Encino Charter ES – Green Schoolyard Upgrade Project

Board District 4, Region North



Project Scope

Site Improvements

- Replace approximately **39,000** square feet of paving in the main playground with green/natural surfaces. Currently, there is approximately **9%** green/natural spaces in the schoolyard.
- Greening improvements may include native/drought tolerant planting, natural grass play fields, trees and other shade elements, outdoor learning elements, landscaping with irrigation, decomposed granite and pavers, and planting areas in alignment with the District's Green Schoolyards for All Plan (April 2024).
- Asphalt resurfacing and restriping as necessary
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget

- Site & Environmental Plans 2.1%
- Construction Management 12.0%
- Other/Reserve 71.2%
- 8.3%
- 6.4%

Anticipated Construction Schedule

- Construction Start
 - Construction Complete
- Q4-2026

Q1-2028



26

39

San Pedro ES – Green Schoolyard Upgrade Project330

Board District 5, Region East



Project Scope

Site Improvements


- Replace approximately **33,000** square feet of paving in the main playground with green/natural surfaces. Currently, there is approximately **7%** green/natural spaces in the schoolyard.
- Greening improvements may include native/drought tolerant planting, natural grass play fields, trees and other shade elements, outdoor learning elements, landscaping with irrigation with the granite and pavers, and planting areas in alignment with the District's Green Schoolyards for All Plan (April 2024).
- Asphalt resurfacing and restriping as necessary
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget

- Site & Environmental
 - Plans
 - Construction
 - Management
 - Other/Reserve
- | | |
|--|-------------|
| | \$5,117,000 |
| | 2.5% |
| | 12.0% |
| | 70.9% |
| | 8.3% |
| | 6.3% |

Anticipated Construction Schedule

- Construction Start
 - Construction Complete
- | | |
|--|---------|
| | Q3-2026 |
| | Q4-2027 |

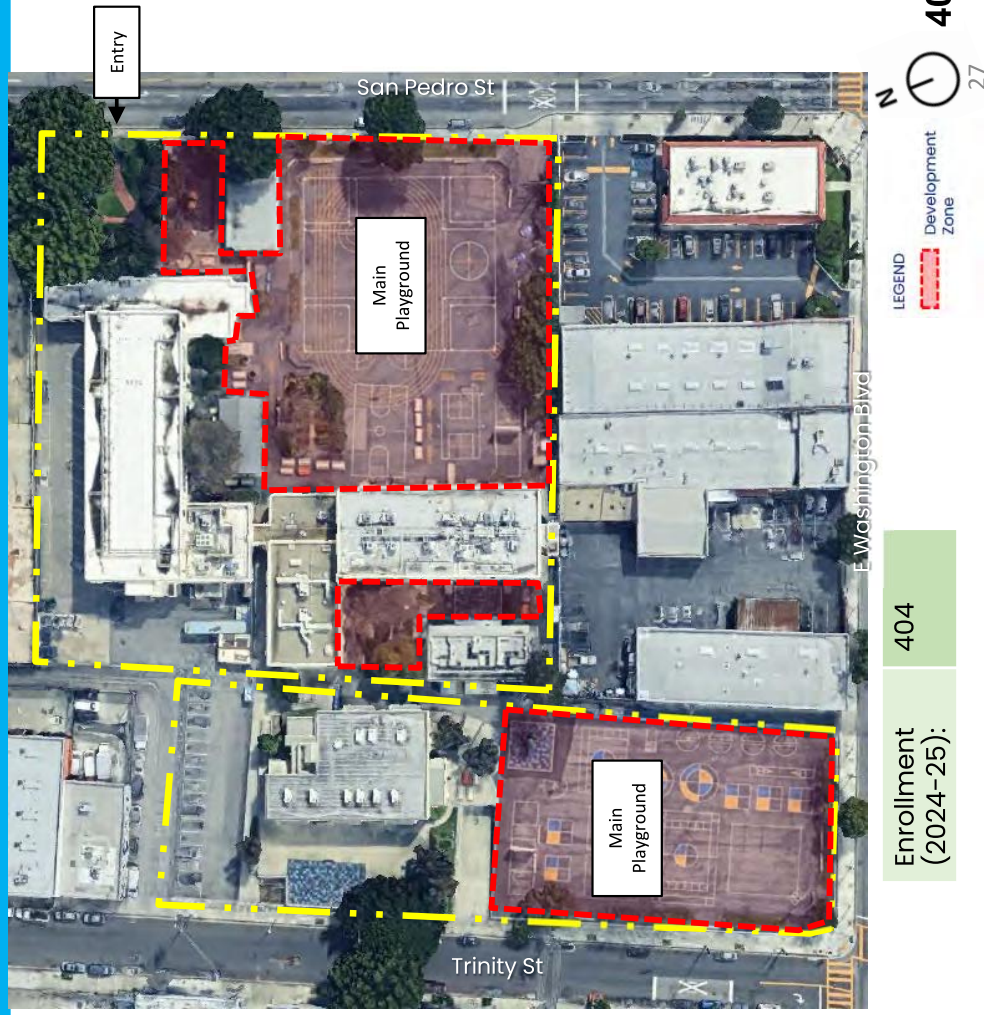

Enrollment
(2024-25):

404

LEGEND
Development
Zone

40
27

Heliotrope ES- Green Schoolyard Upgrade Project

Board District 5, Region East



Project Scope

Site Improvements


- Replace approximately **32,400** square feet of paving in the main playground with green/natural surfaces. Currently, there is approximately **2%** green/natural spaces in the schoolyard.
- Greening improvements may include native/drought tolerant planting, natural grass play fields, trees and other shade elements, outdoor learning elements, landscaping with irrigation, decomposed granite and pavers, and planting areas in alignment with the District's Green Schoolyards for All Plan (April 2024).
- Asphalt resurfacing and restriping as necessary
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget

• Site & Environmental	\$5,259,000
• Plans	2.3%
• Construction	12.0%
• Management	71.1%
• Other/Reserve	8.3%
	6.3%

Anticipated Construction Schedule

- Construction Start Q4-2026
- Construction Complete Q1-2028

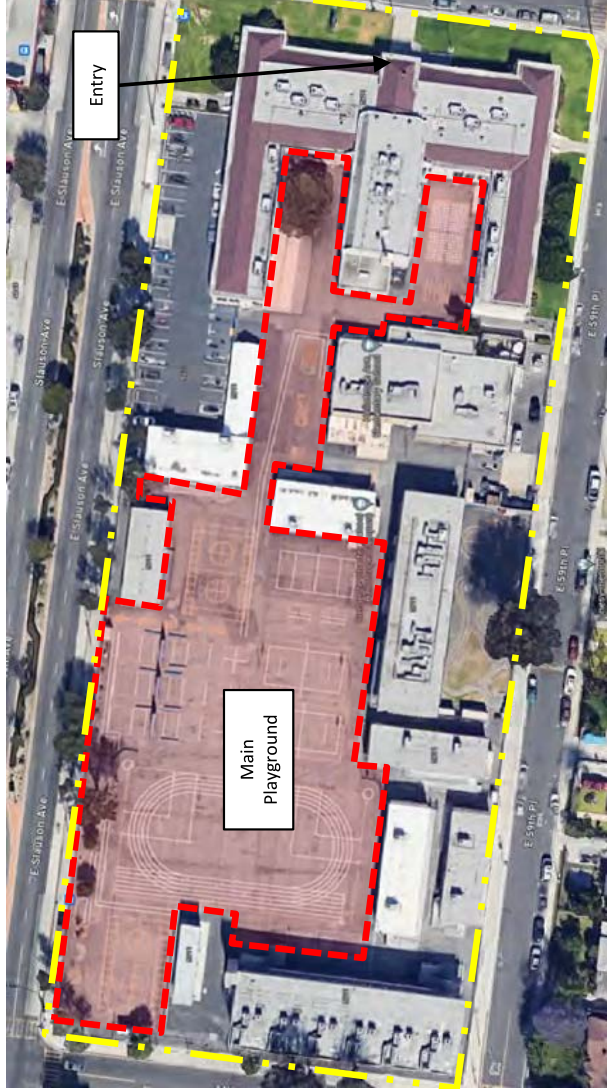

Enrollment (2024-25):	463
--------------------------	-----



28 41

392

Strathern ES– Green Schoolyard Upgrade Project 332

Board District 6, Region North



Project Scope

Site Improvements


- Replace approximately **57,900** square feet of paving in the main playground with green/natural surfaces. Currently, there is approximately **5%** green/natural spaces in the schoolyard.
- Greening improvements may include native/drought tolerant planting, natural grass play fields, trees and other shade elements, outdoor learning elements, landscaping with irrigation, decomposed granite and pavers, and planting areas in alignment with the District’s Green Schoolyards for All Plan (April 2024).
- Asphalt resurfacing and restriping as necessary
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget

• Site & Environmental Plans	\$6,743,000
• Construction	2.4%
• Management	12.1%
• Other/Reserve	70.8%
	8.3%
	6.4%

Anticipated Construction Schedule

- Construction Start Q4-2026
- Construction Complete Q1-2028

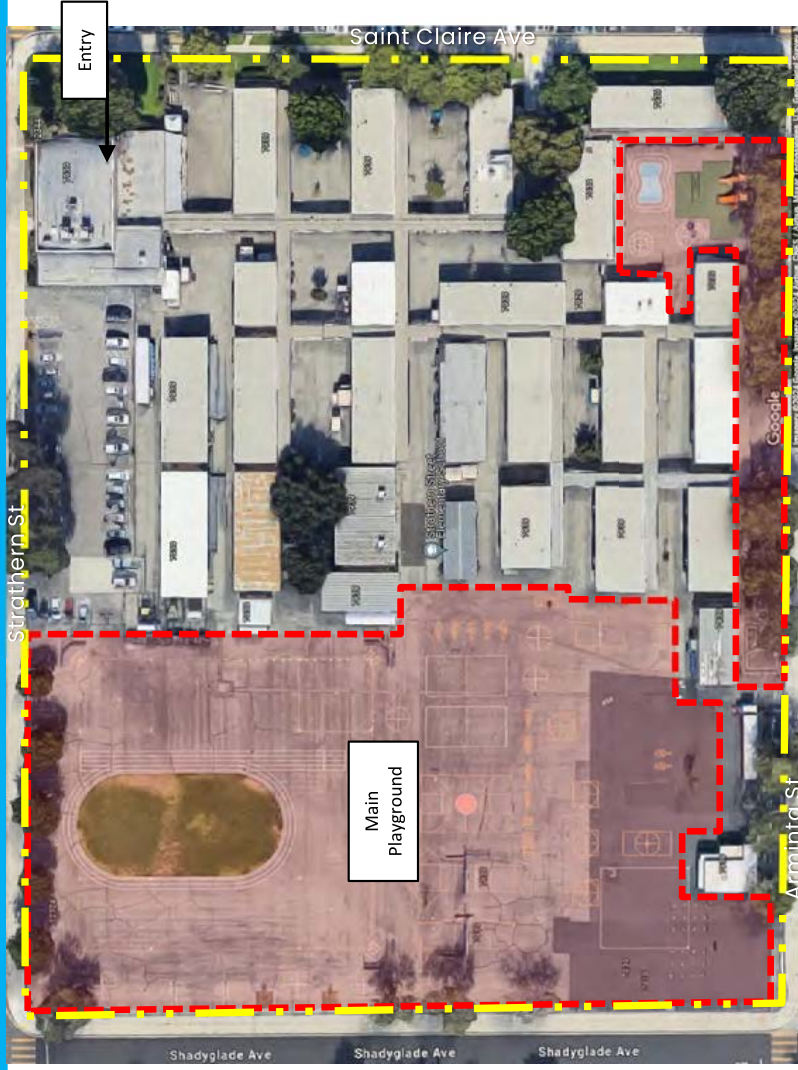

LEGEND
Development Zone

Enrollment (2024–25):	446
-----------------------	-----

N 1 42 29

Roscoe ES- Green Schoolyard Upgrade Project

Board District 6, Region North



Project Scope

Site Improvements

- Replace approximately **51,000** square feet of paving in the main playground with green/natural surfaces. Currently, there is approximately **10%** green/natural spaces in the schoolyard.
- Greening improvements may include native/drought tolerant planting, natural grass play fields, trees and other shade elements, outdoor learning elements, landscaping with irrigation, decomposed granite and pavers, and planting areas in alignment with the District's Green Schoolyards for All Plan (April 2024).
- Asphalt resurfacing and restriping as necessary
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget

• Site & Environmental	\$7,678,000
• Plans	2.1%
• Construction	12.2%
• Management	70.9%
• Other/Reserve	8.4%
	6.4%

Anticipated Construction Schedule

- Construction Start Q4-2026
- Construction Complete Q1-2028



Arminta ES – Green Schoolyard Upgrade Project

Board District 6, Region North



Project Scope

Site Improvements

- Replace approximately **46,200** square feet of paving in the main playground with green/natural surfaces. Currently, there is approximately **3%** green/natural spaces in the schoolyard.
- Greening improvements may include native/drought tolerant planting, natural grass play fields, trees and other shade elements, outdoor learning elements, landscaping with irrigation, decomposed granite and pavers, and planting areas in alignment with the District's Green Schoolyards for All Plan (April 2024).
- Asphalt resurfacing and restriping as necessary
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget


• Site & Environmental	\$5,805,000
• Plans	2.5%
• Construction	12.0%
• Management	70.9%
• Other/Reserve	8.3%
	6.3%

Anticipated Construction Schedule

- Construction Start Q3-2026
- Construction Complete Q4-2027

Enrollment
(2024-25):

315

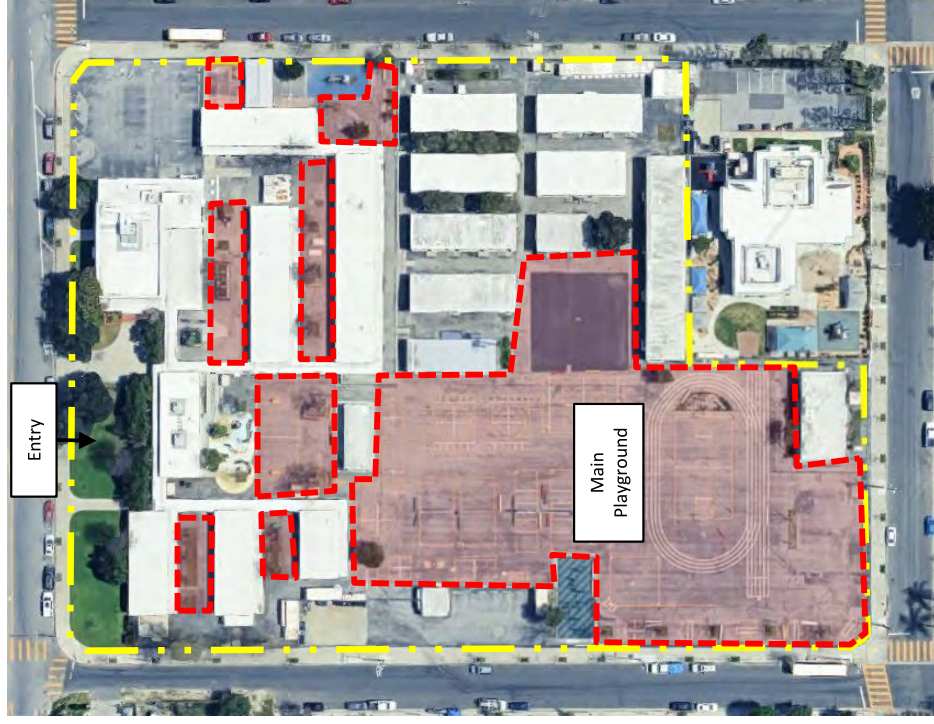

LEGEND



Development
Zone 31

N

(44)

395

Gardena ES – Green Schoolyard Upgrade Project 335

Board District 7, Region South



Project Scope

Site Improvements

- Replace approximately **43,200** square feet of paving in the main playground with green/natural surfaces. Currently, there is approximately **5%** green/natural spaces in the schoolyard.
- Greening improvements may include native/drought tolerant planting, natural grass play fields, trees and other shade elements, outdoor learning elements, landscaping with irrigation, decomposed granite and pavers, and planting areas in alignment with the District's Green Schoolyards for All Plan (April 2024).
- Asphalt resurfacing and restriping as necessary
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget


• Site & Environmental	\$6,072,000
• Plans	2.1%
• Construction	12.1%
• Management	71.1%
• Other/Reserve	8.3%
	6.4%

Anticipated Construction Schedule

- Construction Start Q3-2026
- Construction Complete Q4-2027



Enrollment (2024-25):	398
LEGEND	Development Zone



Ritter ES– Green Schoolyard Upgrade Project

Board District 7, Region South



Project Scope

Site Improvements


- Replace approximately **35,500** square feet of paving in the main playground with green/natural surfaces. Currently, there is approximately **4%** green/natural spaces in the schoolyard.
- Greening improvements may include native/drought tolerant planting, natural grass play fields, trees and other shade elements, outdoor learning elements, landscaping with irrigation, decomposed granite and pavers, and planting areas in alignment with the District's Green Schoolyards for All Plan (April 2024).
- Asphalt resurfacing and restriping as necessary
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget

- Site & Environmental
 - Plans
 - Construction
 - Management
 - Other/Reserve
- | |
|-------------|
| \$5,731,000 |
| 2.3% |
| 12.0% |
| 71.1% |
| 8.3% |
| 6.3% |

Anticipated Construction Schedule

- Construction Start
 - Construction Complete
- | |
|---------|
| Q4-2026 |
| Q1-2028 |

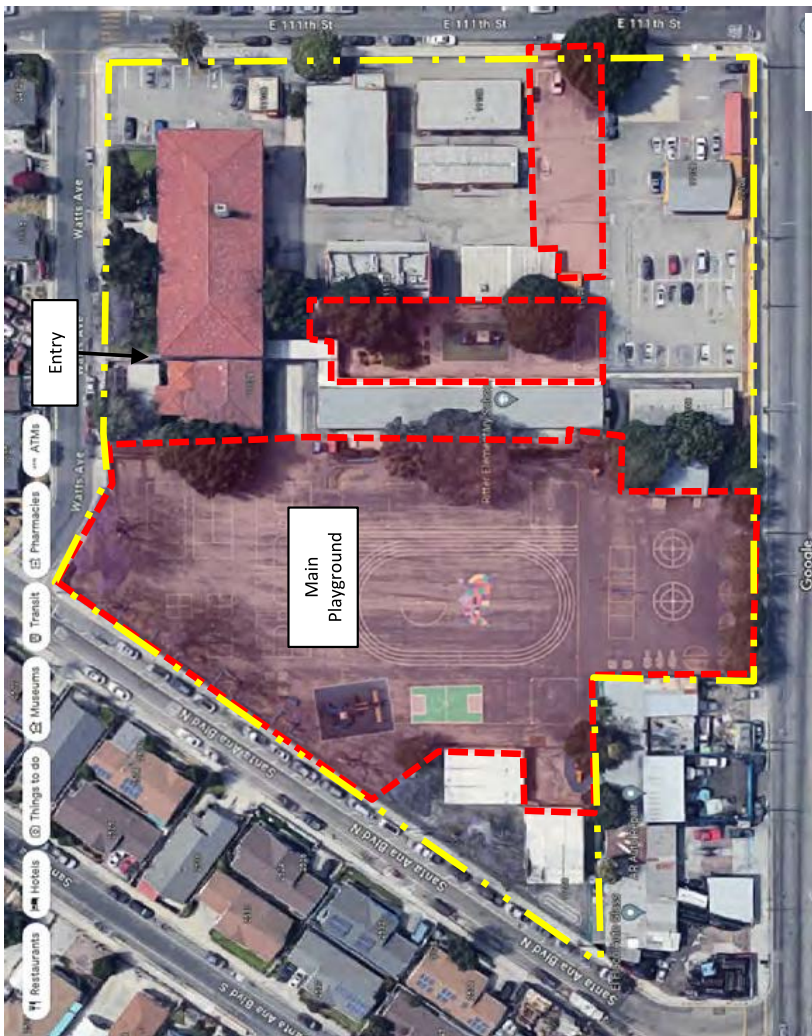

Enrollment (2024-25):

302

LEGEND

Development Zone

336 LA

READY FOR THE WORLD

33

46

397

Thank you



Questions?



347



Board of Education Report

File #: Rep-158-23/24, Version: 1

Approval of Facilities Contracts Actions

April 9, 2024

Procurement Services Division - Facilities Contracts

Action Proposed:

Ratify the Procurement Services Division (PSD) contract actions taken by Facilities Contracts under delegated authority as listed in Attachment “A” including: award of advertised construction contracts; award of job order contracts; approval of change orders; completion of contracts; award of informal contracts; award of architectural and engineering contracts; award of professional/technical services amendment; award of professional services contract; extra services/amendments for architectural and engineering contracts and approve the proposed contracts listed in Attachment B including construction schedule reviews and/or time impact analysis contracts, and Local Hazard Mitigation Plan services contract.

Background:

Facilities Contracts staff prepares monthly reports for contract actions necessary for the execution of projects approved by the Board and contained in the FSD Strategic Execution Plan (SEP), and for the maintenance and operation of District facilities in accordance with District policies and Board-delegated authority. As described in the November 12, 2013, Board Report #048-13/14 Informative, detailed information is provided on the Facilities Services website.

Expected Outcomes:

Approval of these items will allow services provided by these contracts to proceed in support of FSD projects, District policies and goals, and the Board-approved FSD-SEP.

Board Options and Consequences:

The Board can approve all actions presented or postpone selected actions pending receipt of additional information. Non-ratification of actions awarded under delegated authority in Attachment “A” will result in the immediate discontinuance of services. While non-ratification may be legally defensible, it will likely result in costly litigation over discontinued payments or if the District attempts to reclaim payments made to a vendor. District costs will likely increase as fewer contractors compete for future procurements.

Policy Implications:

This action does not change District policy and conforms to California Education Code section 17604 that permits the Board of Education to delegate authority for Facilities Contracts (Board Report #444-17/18), which the Board exercised on May 08, 2018.

Budget Impact:

The contract actions presented are within the budget authority previously approved by the Board. Unless indicated otherwise, all contract actions are Bond funded.

File #: Rep-158-23/24, Version: 1

Student Impact:

The contract actions will help ensure that the students are provided with safe and healthy environments, and up to-date facilities that promote learning.

Equity Impact:

Not Applicable.

Issues and Analysis:

There are no policy implications on these agreements.

Attachments:

Attachment A - Ratification of Facilities Contracts Actions Awarded Under Delegated Authority

Attachment B - Approval of Facilities Contracts Actions Not Under Delegated Authority

Linked Materials

Previously adopted Board report(s) referenced:

- In the background [Board Report No. 048-13/14 <https://drive.google.com/file/d/1q-FUsW7AXKe8h0A4KY-J3OVby30HueD6/view>](https://drive.google.com/file/d/1q-FUsW7AXKe8h0A4KY-J3OVby30HueD6/view), dated November 12, 2013, Informative
- In the policy implications [Board Report No. 444-17/18 <https://drive.google.com/file/d/16sRw7yPe-tScbr2wG8AMTWB9QSeiQazM/view>](https://drive.google.com/file/d/16sRw7yPe-tScbr2wG8AMTWB9QSeiQazM/view), dated May 8, 2018.

Informatives:

Not Applicable.

Submitted:

03/12/24


File #: Rep-158-23/24, Version: 1

RESPECTFULLY SUBMITTED,



ALBERTO M. CARVALHO
Superintendent

APPROVED BY:



PEDRO SALCIDO
Deputy Superintendent,
Business Services & Operations


REVIEWED BY:



DEVORA NAVERA REED
General Counsel

☒ Approved as to form.

APPROVED:



SUNG YON LEE
Deputy Chief Business Officer
Business Services and Operations


REVIEWED BY:



NOLBERTO DELGADILLO
Deputy Chief Business Officer, Finance

☒ Approved as to budget impact statement

APPROVED & PRESENTED BY:



CHRISTOPHER MOUNT-BENITES
Chief Procurement Officer
Procurement Services Division

REVIEWED BY:



KRISZTINA TOKES
Chief Facilities Executive

☒ Approved as to facilities impact

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

AWARD OF ADVERTISED CONSTRUCTION CONTRACTS

Item A

<u>CONTRACTOR</u>	<u>IDENTIFICATION NO.</u>	<u>DESCRIPTION</u>	<u>SOURCE OF FUNDS</u>	<u>AMOUNT</u>
Pars Arvin Construction, Inc. (SBE)	2410046 / 4400012840	<u>Carthay Elementary of Environmental Studies Magnet Accessibility Enhancement Project</u> Board Member: <u>Dr. George J. McKenna III</u>	<i>Bond Funds (100%)</i>	\$6,183,000

Ratification of formally competed best value contract selected from nine (9) bids received to construct and deliver an accessibility enhancement project at Carthay Elementary of Environmental Studies Magnet as authorized on December 7, 2021 ([Board Report No. 144-21/22](#)).

The project upgrades the following facilities to comply with the Americans with Disabilities Act (ADA) and improve program accessibility: doors/jambs, door hardware, thresholds, accessible paths of travel, signs, restrooms, drinking fountains, assistive listening devices, intercoms, concrete ramps, metal ramps, pieces of accessible furniture, railings, playground components, one new elevator with covered bridge, and one new stage lift. Pillar 4 of the Strategic Plan is supported by this action.

The contractor has worked with the District since 2003.

Contract Term: 03/04/24 through completion.

Contract Value: \$6,183,000

Requester:

Greg Garcia, Director, Facilities Project Execution
Facilities Services Division

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

AWARD OF ADVERTISED CONSTRUCTION CONTRACTS

Item B

<u>CONTRACTOR</u>	<u>IDENTIFICATION NO.</u>	<u>DESCRIPTION</u>	<u>SOURCE OF FUNDS</u>	<u>AMOUNT</u>
PaveWest, Inc.	2410050 / 4400012865	<u>Calvert Charter for Enriched Studies</u> Asphalt Replacement and Solar Reflective Coating Board Member: <u>Nick Melvoin</u>	<i>Restricted Maintenance Funds (100%)</i>	\$844,000

Ratification of formally competed contract selected from four (4) bids received to replace deteriorated asphalt and provide solar reflective coating at Calvert Charter for Enriched Studies.

The project replaces approximately 50,000 square feet of deteriorated asphalt paving on the playground and provides solar reflective coating of approximately 139,000 square feet. Pillar 4 of the Strategic Plan is supported by this action.

The contractor has worked with the District since 2021.

Contract Term: 03/11/24 through completion.

Contract Value: \$844,000

Requester:

India Griffin, Director, Facilities Maintenance & Operations
Facilities Services Division

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

AWARD OF ADVERTISED CONSTRUCTION CONTRACTS

Item C

<u>CONTRACTOR</u>	<u>IDENTIFICATION NO.</u>	<u>DESCRIPTION</u>	<u>SOURCE OF FUNDS</u>	<u>AMOUNT</u>
Geronimo Concrete, Inc. (SBE)	2410052 / 4400012800	<u>Curtiss MS</u> ADA Barrier Removal Board Member: <u>Tanya Ortiz Franklin</u>	<i>Bond Funds (100%)</i>	\$1,110,526

Ratification of formally competed contract selected from nine (9) bids received to construct and deliver an accessibility enhancement project at Curtiss Middle School improvements as authorized on August 30, 2022 ([Board Report No. 007-22/23](#)).

The project upgrades the following facilities to comply with the Americans with Disabilities Act (ADA) and improve program accessibility: 2 restrooms, 2 concrete ramps, and other miscellaneous upgrades to the main entrance and multipurpose room. Pillar 4 of the Strategic Plan is supported by this action.

The contractor has worked with the District since 2005.

Contract Term: 02/16/24 through completion.

Contract Value: \$1,110,526

Requester:

Greg Garcia, Director, Facilities Project Execution
Facilities Services Division

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

AWARD OF ADVERTISED CONSTRUCTION CONTRACTS

Item D

Ratification of the first eleven (11) formally competed contracts funded by the Expanded Learning Opportunities Program (ELOP) consisting of thirty-four (34) projects to provide green schoolyard improvements beginning Q1-2024 through Q4-2027 as authorized on December 12, 2023 ([Board Report No. 024-23/24](#)).

The projects consist of new planting, trees, turf, and/or decomposed granite within existing or new planting areas at existing school sites. At some school sites, the scope will also include asphalt removal. Pillar 4 of the Strategic Plan is supported by this action.

<u>CONTRACTOR</u>	<u>IDENTIFICATION NO.</u>	<u>DESCRIPTION</u>	<u>AMOUNT</u>
Ian Thomas Group (SBE)	2410059 / 4400012600	<u>Wilton Place ES</u> Board Member: <u>Dr. George J. McKenna III</u>	\$689,000
Ian Thomas Group (SBE)	2410060 / 4400012842	<u>109th Street ES</u> Board Member: <u>Tanya Ortiz Franklin</u>	\$689,000
Ian Thomas Group (SBE)	2410061 / 4400012843	<u>118th Street ES</u> Board Member: <u>Tanya Ortiz Franklin</u>	\$580,000
R Brothers, Inc. (SBE)	2410062 / 4400012846	<u>Belvedere ES</u> Board Member: <u>Dr. Rocío Rivas</u>	\$523,290
R Brothers, Inc. (SBE)	2410063 / 4400012847	<u>Hamasaki Medical & Science Magnet ES</u> Board Member: <u>Dr. Rocío Rivas</u>	\$401,026
R Brothers, Inc. (SBE)	2410064 / 4400012848	<u>Marianna Avenue ES</u> Board Member: <u>Dr. Rocío Rivas</u>	\$567,684
R Brothers, Inc. (SBE)	2410065 / 4400012860	<u>Coldwater Canyon ES</u> Board Member: <u>Kelly Gonez</u>	\$393,000
R Brothers, Inc. (SBE)	2410066 / 4400012861	<u>Griffith-Joyner ES</u> Board Member: <u>Tanya Ortiz Franklin</u>	\$527,811

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

<u>CONTRACTOR</u>	<u>IDENTIFICATION NO.</u>	<u>DESCRIPTION</u>	<u>AMOUNT</u>
R Brothers, Inc. (SBE)	2410067 / 4400012862	<u>Russell ES</u> Board Member: <u>Tanya Ortiz Franklin</u>	\$645,838
R Brothers, Inc. (SBE)	2410068 / 4400012864	<u>Stoner ES</u> Board Member: <u>Nick Melvoin</u>	\$502,351
R Brothers, Inc. (SBE)	2410069 / 4400012837	<u>Capistrano Avenue ES</u> Board Member: <u>Scott M. Schmerelson</u>	\$303,000

Ian Thomas Group has worked with the District since 2009. R Brothers has worked with the District since 2012.

Contract Term: Various

Contract Value: \$5,822,000 (100% ELOP – FSD Funds)

Requester:

India Griffin, Director, Facilities Maintenance & Operations
Facilities Services Division

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

AWARD OF ADVERTISED CONSTRUCTION CONTRACTS

Item E

Ratification of five (5) bundled formally competed contracts to construct and deliver walk-in freezer and cooler modernizations, as authorized on March 8, 2016 ([Board Report No. 284-15/16](#)) and November 13, 2018 ([Board Report No. 092-18/19](#)).

The projects consist of providing new panels, ceilings, floors, doors and new energy-efficient refrigeration and lighting systems. Pillar 4 of the Strategic Plan is supported by this action. The contractor has worked with the District since 2023.

<u>CONTRACTOR</u>	<u>IDENTIFICATION NO.</u>	<u>DESCRIPTION</u>	<u>AMOUNT</u>
Market Cooling & Construction, Inc.	2410072 / 4400012890	<u>32nd Street/USC Magnet School</u> Board Member: <u>Dr. George J. McKenna III</u>	\$240,688
Market Cooling & Construction, Inc.	2410073 / 4400012891	<u>109th Street ES</u> Board Member: <u>Tanya Ortiz Franklin</u>	\$255,393
Market Cooling & Construction, Inc.	2410074 / 4400012892	<u>Miramonte ES</u> Board Member: <u>Tanya Ortiz Franklin</u>	\$242,376
Market Cooling & Construction, Inc.	2410075 / 4400012893	<u>Dominguez ES</u> Board Member: <u>Tanya Ortiz Franklin</u>	\$224,307
Market Cooling & Construction, Inc.	2410076 / 4400012894	<u>Rowan Avenue ES</u> Board Member: <u>Dr. Rocío Rivas</u>	\$275,788

Contract Term: Various

Contract Value: \$1,238,552 (100% Bond Funds)

Requester:

India Griffin, Director, Facilities Maintenance & Operations
Facilities Services Division

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

**JOB ORDER CONTRACTS AWARDS –
Electrical and Low Voltage Contracting Services**
Item F

Ratification of eleven (11) formally competed Job Order Contract awards procured via RFQ R-24017 to provide electrical contracting services Districtwide.

These services provide operational effectiveness and modernize infrastructure. Pillar 4 of the Strategic Plan is supported by this action.

<u>CONTRACTOR</u>	<u>IDENTIFICATION NO.</u>	<u>DESCRIPTION</u>	<u>AMOUNT</u>
Birdi Systems, Inc. (SBE)	2430006 / 4400012685	Category A: CCTV & Intrusion Alarm Systems Installations	\$500,000
Advanced Cable Solutions, Inc. (SBE)	2430007 / 4400012677	Category A: CCTV & Intrusion Alarm Systems Installations	\$500,000
Alternate Power and Construction, Inc. (SBE)	2430008 / 4400012670	Category A: CCTV & Intrusion Alarm Systems Installations	\$500,000
Reyes Electrical Contractor, Inc., dba Reyes Engineering Corp. (SBE)	2430009 / 4400012651	Category A: CCTV & Intrusion Alarm Systems Installations	\$500,000
Telenet VoIP, Inc. (SBE)	2430011 / 4400012672	Category A: CCTV & Intrusion Alarm Systems Installations	\$500,000
Johnson Controls, Inc.	2430012 / 4400012681	Category A: CCTV & Intrusion Alarm Systems Installations	\$500,000
Advanced Cable Solutions, Inc. (SBE)	2430013 / 4400012678	Category B: Public Address (PA) and Telephone Installations	\$500,000
Alternate Power and Construction, Inc. (SBE)	2430014 / 4400012671	Category B: Public Address (PA) and Telephone Installations	\$500,000
Reyes Electrical Contractor, Inc., dba Reyes Engineering Corp. (SBE)	2430015 / 4400012652	Category B: Public Address (PA) and Telephone Installations	\$500,000

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

<u>CONTRACTOR</u>	<u>IDENTIFICATION NO.</u>	<u>DESCRIPTION</u>	<u>AMOUNT</u>
Telenet VoIP, Inc. (SBE)	2430017 / 4400012673	Category B: Public Address (PA) and Telephone Installations	\$500,000
Johnson Controls, Inc.	2430018 / 4400012682	Category B: Public Address (PA) and Telephone Installations	\$500,000

Contract Term: Various

Aggregate Contract Value: \$5,500,000 (100% Bond Funded)

Requester:

Soheil Katal, Chief Information Officer
Information Technology Services

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

Item G

B. APPROVAL OF CHANGE ORDERS

February 2024 = \$11,847,391

		<u>QUANTITY</u>	<u>AMOUNT</u>
	i. New Construction contract change orders that do not individually exceed 10 percent for February 2024 (Average Transaction: \$90,679; Median Transaction: \$9,707)	41	\$3,717,857
	ii. New Construction contract credit change orders for February 2024:	1	<\$11,399>
	iii. Existing Facilities contract change orders that do not individually exceed 15 percent for February 2024 (Average Transaction: \$21,323; Median Transaction: \$6,517):	414	\$8,827,536
	iv. Existing Facilities contract credit change orders for February 2024:	20	<\$686,603>
	v. Existing Facilities contract change orders that individually exceed 15 percent (but do not exceed 25 percent) for February 2024, requiring 75 percent approval by the Board:	0	\$0

C.	COMPLETION OF CONTRACTS – February 2024	19	\$14,343,476
-----------	--	----	--------------

D.	AWARD OF INFORMAL CONTRACTS (Not Exceeding \$114,500)		
	A & B Letters for February 2024 (Average Transaction: \$53,473; Median Transaction: \$45,712)	22	\$1,176,396

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

AWARD OF ARCHITECTURAL AND ENGINEERING CONTRACTS

Item H

CONTRACTOR	IDENTIFICATION NO.	DESCRIPTION	SOURCE OF FUNDS	AMOUNT
tBP/Architecture, Inc. (SBE)	2420005/ 4400011902	<u>Reseda Charter High School</u> Synthetic Track and Natural Turf Football/Soccer Field Upgrade Project Board Member: <u>Nick Melvoin</u>	<i>Bond</i> <i>Funds</i> <i>(100%)</i>	\$496,978

Ratification of design contract to provide architectural and engineering services for the synthetic track and natural turf football/soccer field upgrade project as authorized on June 20, 2023 ([Board Report No. 127-22/23](#)). The contract was procured via RFQ R-19012.

tBP/Architecture, Inc. will provide architectural and engineering services for site analysis/preliminary schematic design, design development, construction document, DSA backcheck, bidding/proposal and award, and construction and closeout for the synthetic track and natural turf football/soccer field upgrade project.

The project includes but is not limited to design and construction of a new synthetic running track, natural grass football/soccer field, and other associated upgrades, including landscape, hardscape, and infrastructure. Demolition and removal of the existing decomposed granite track and natural grass football/soccer field. Improvements to ensure compliance with local, state, and federal requirements including from the ADA, DSA, California Environmental Quality Act (CEQA), and Department of Toxic Substances Control (DTSC).

These services provide operational effectiveness and modernize infrastructure. Pillar 4 of the Strategic Plan is supported by this action.

Contract Term: 02/07/2024 through closeout.

Contract Value: \$496,978

Requester:
Aaron Bridgewater, Director, Facilities Asset Management
Facilities Services Division

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

AWARD OF ARCHITECTURAL AND ENGINEERING CONTRACTS

Item I

<u>CONTRACTOR</u>	<u>IDENTIFICATION NO.</u>	<u>DESCRIPTION</u>	<u>SOURCE OF FUNDS</u>	<u>AMOUNT</u>
tBP/Architecture, Inc. (SBE)	2420021/ 4400012296	<u>Halldale ES</u> Accessibility Enhancement Project Board Member: <u>Tanya Ortiz Franklin</u>	<i>Bond Funds (100%)</i>	\$459,119

Ratification of design contract to provide architectural and engineering services for an accessibility enhancement project at Halldale Elementary School as authorized on December 12, 2023 ([Board Report No. 128-23/24](#)). The contract was procured via RFQ R-19012.

tBP/Architecture, Inc. will provide architectural and engineering services for site investigation/preliminary planning, construction document, bid/proposal and award, construction, and closeout for the accessibility enhancement project.

The project includes, but is not limited to, various upgrades to 10 buildings as required, including: correction, installation, or replacement of, one permanent wheelchair lift, 10 restroom upgrades, four concrete ramps, one arcade, three assembly seating area upgrades, six metal ramps, eight drinking fountain upgrades, 12 path of travel upgrades, one parking lot upgrade, one changing room with toilet, other accessibility upgrades such as door hardware, playground components/matting, railings, and any other required improvements or mitigations to ensure programmatic access and compliance with local, state and/or federal facilities requirements.

These services provide operational effectiveness and modernize infrastructure. Pillar 4 of the Strategic Plan is supported by this action.

Contract Term: 01/25/2024 through closeout.

Contract Value: \$459,119

Requester:

Aaron Bridgewater, Director, Facilities Asset Management
Facilities Services Division

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

AWARD OF ARCHITECTURAL AND ENGINEERING CONTRACTS

Item J

<u>CONTRACTOR</u>	<u>IDENTIFICATION NO.</u>	<u>DESCRIPTION</u>	<u>SOURCE OF FUNDS</u>	<u>AMOUNT</u>
Gruen Associates (SBE)	2420022/ 4400012297	<u>Utah Span School</u> Accessibility Enhancement Project Board Member: <u>Dr. Rocío Rivas</u>	<i>Bond Funds (100%)</i>	\$602,709

Ratification of design contract to provide architectural and engineering services for an accessibility enhancement project at Utah Span School as authorized on December 12, 2023 ([Board Report No. 128-23/24](#)). The contract was procured via RFQ R-19012.

Gruen Associates will provide architectural and engineering services for site investigation/preliminary planning, construction document, bid/proposal and award, construction, and closeout for the accessibility enhancement project.

The project includes, but is not limited to, various upgrades to seven buildings as required, including: correction, installation, or replacement of one new elevator, one permanent wheelchair lift, 11 restroom upgrades, one concrete ramp, six drinking fountain upgrades, one parking lot upgrade, 16 path of travel upgrades, three assembly seating area upgrades, other accessibility upgrades such as door hardware, playground components/matting, railings, and any other required improvements or mitigations to ensure programmatic access and compliance with local, state and/or federal facilities requirements.

These services provide operational effectiveness and modernize infrastructure. Pillar 4 of the Strategic Plan is supported by this action.

Contract Term: 01/31/2024 through closeout.

Contract Value: \$602,709

Requester:

Aaron Bridgewater, Director, Facilities Asset Management
Facilities Services Division

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

AWARD OF ARCHITECTURAL AND ENGINEERING CONTRACTS

Item K

<u>CONTRACTOR</u>	<u>IDENTIFICATION NO.</u>	<u>DESCRIPTION</u>	<u>SOURCE OF FUNDS</u>	<u>AMOUNT</u>
PBK Architects, Inc.	2420029/ 4400012303	<u>Cleveland Charter HS</u> Field Upgrades with Synthetic Turf Project Board Member: <u>Scott M. Schmerelson</u>	<i>Bond Funds (100%)</i>	\$447,600

Ratification of design contract to provide architectural and engineering services for the field upgrades with synthetic turf project at Cleveland Charter High School as authorized on June 20, 2023 ([Board Report No. 127-22/23](#)). The contract was procured via RFQ R-19012.

PBK Architects, Inc. will provide architectural and engineering services for site analysis/preliminary and final schematic design, design development, construction document, DSA backcheck, bidding/proposal and award, construction and closeout for athletic facilities upgrade project.

The project includes but is not limited to the design and construction of a new synthetic turf football/soccer field and other associated upgrades, including landscape, hardscape, and infrastructure. Demolition and removal of the existing natural grass football/soccer field. Relocation of the existing kiosk. Improvements to ensure compliance with local, state, and federal requirements including from the Americans with Disabilities Act (ADA), Division of the State Architect (DSA), California Environmental Quality Act (CEQA) and Department of Toxic Substances Control (DTSC).

These services provide operational effectiveness and modernize infrastructure. Pillar 4 of the Strategic Plan is supported by this action.

Contract Term: 01/22/2024 through closeout.

Contract Value: \$447,600

Requester:

Aaron Bridgewater, Director, Facilities Asset Management
Facilities Services Division

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

AWARD OF ARCHITECTURAL AND ENGINEERING CONTRACTS

Item L

CONTRACTOR	IDENTIFICATION NO.	DESCRIPTION	SOURCE OF FUNDS	AMOUNT
Mun Leu Architect, Inc., dba MLArchitecture (SBE)	2420030/ 4400012447	Strathern Street ES Accessibility Enhancement Project Board Member: Kelly Gonez	Bond Funds (100%)	\$322,817

Ratification of design contract to provide architectural and engineering services for the accessibility enhancement project at Strathern Street Elementary School as authorized on December 12, 2023 ([Board Report No. 128-23/24](#)). The contract was procured via RFQ R-19012.

Mun Leu Architect, Inc., will provide architectural and engineering services for site investigation/preliminary planning, construction document, bid/proposal and award, and construction and closeout phases for the accessibility enhancement project.

The project includes, but is not limited to, various upgrades to 13 buildings as required, including: correction, installation, or replacement of nine restroom upgrades, four assembly seating area upgrades, one changing room, four drinking fountain upgrades, 20 path of travel upgrades, other accessibility upgrades such as door hardware, playground components/matting, railings, and any other required improvements or mitigations to ensure programmatic access and compliance with local, state and/or federal facilities requirements.

These services provide operational effectiveness and modernize infrastructure. Pillar 4 of the Strategic Plan is supported by this action.

Contract Term: 01/25/2024 through closeout.

Contract Value: \$322,817

Requester:
Aaron Bridgewater, Director, Facilities Asset Management
Facilities Services Division

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

AWARD OF ARCHITECTURAL AND ENGINEERING CONTRACTS

Item M

<u>CONTRACTOR</u>	<u>IDENTIFICATION NO.</u>	<u>DESCRIPTION</u>	<u>SOURCE OF FUNDS</u>	<u>AMOUNT</u>
HMC Group dba HMC Architects	2420032/ 4400012660	<u>Foshay Learning Center</u> Seismic Modernization Project: Exterior Wall Tile Assessment and Replacement Board Member: <u>Dr. George J. McKenna III</u>	<i>Bond Funds (100%)</i>	\$68,687

Ratification of design contract to provide architectural and engineering services for the assessment and repair of exterior wall tile associated with a seismic modernization project at Foshay Learning Center as authorized on June 18, 2013 ([Board Report No. 317-12/13](#)). The contractor was procured via RFQ R-13019.

HMC Architects will provide architectural and engineering services for site investigation/preliminary planning, construction document, bid/proposal and award, construction administration and closeout for exterior wall tile repair and assessment.

Due to a tile installation issue that was later identified, an assessment by a forensic architect was undertaken that determined all tiles needed to be removed due to an installation error. The architect will draft the new design plan to have all the tiles replaced. An insurance claim has been opened against this incident.

These services provide operational effectiveness and modernize infrastructure. Pillar 4 of the Strategic Plan is supported by this action.

Contract Term: 02/01/2024 through closeout.

Contract Value: \$68,687

Requester:

Aaron Bridgewater, Director, Facilities Asset Management
Facilities Services Division

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

**ASSIGNMENT AND ASSUMPTION OF RIGHTS AND DELEGATION OF DUTIES –
REGULATION NO. 4 TESTING AND CERTIFICATION (LIFE/SAFETY SYSTEM
TESTING) SERVICES TASK ORDER AGREEMENT**

Item N

<u>CONTRACTOR</u>	<u>IDENTIFICATION NO.</u>	<u>AMOUNT</u>
ADT COMMERCIAL LLC (Tax ID Number: <u>45-4517261</u>) – ADT COMMERCIAL LLC (Tax ID Number: <u>90-0008456</u>)	2280011- 4400010111	\$0

Ratification of Assignment and Assumption of Agreement from ADT Commercial LLC (Assignor) to ADT Commercial LLC (Assignee) to provide Regulation No. 4 Testing and Certification Services in support of the Fire Life System Test Group (FLSTG) of the Facilities Services Division’s Maintenance & Operations Branch.

ADT Commercial LLC was acquired by a private equity firm but will not change its name; and ADT Commercial LLC has had a change in their taxpayer identification number to 90-0008456 and updated its vendor number to 1000026902.

These services provide operational effectiveness and modernize infrastructure. Pillar 4 of the Strategic Plan is supported by this action.

Requester:

India Griffin, Director, Facilities Maintenance & Operations
Facilities Services Division

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

AWARD OF PROFESSIONAL SERVICES CONTRACT

\$245,000

Item O

<u>CONTRACTOR</u>	<u>IDENTIFICATION NO.</u>
Chicago Title Company	2490052/4400012845

Ratification of a formally competed contract selected via RFP R-24037 to provide real estate title and escrow services for on-going site evaluations and acquisition services. Pillar 4 of the Strategic Plan is supported by this action.

Contract Term: 03/01/24 through 02/28/27, plus two (2) one-year renewal options.

NOT-TO-EXCEED AGGREGATE AMOUNT

\$245,000 (80% Bond Funds, 10% General Funds, 10% Restricted Maintenance Funds)

Requester:

Aaron Bridgewater, Director, Facilities Asset Management
Facilities Services Division

ATTACHMENT A

RATIFICATION OF CONTRACTS AWARDED UNDER DELEGATED AUTHORITY

**EXTRA SERVICES / AMENDMENTS FOR ARCHITECTURAL AND
ENGINEERING CONTRACTS****\$47,694****Item P**

CONTRACT NOS.	1820026/4400006211; 1820031/4400006280; 2120145/4400009611; 2220022/4400010168
---------------	---

Extra services are for design work that is not covered under the original Agreement. January Extra Services are listed at the following link: [BOE 158 Extra Services](#)

These services provide operational effectiveness and modernize infrastructure. Pillar 4 of the Strategic Plan is supported by this action.

ATTACHMENT B
APPROVAL OF CONTRACTS NOT UNDER DELEGATED AUTHORITY

ADOPTED BY BOARD
420
APRIL 9, 2024

A. APPROVAL OF CONSTRUCTION SCHEDULE REVIEWS SERVICES CONTRACTS

\$5,000,000

Item Q

<u>CONTRACTOR</u>	<u>IDENTIFICATION NO.</u>
FS3, Inc., dba fs3 Hodges (SBE)	2490024 /4400012791
Greenridge CPM (a joint venture)	2490025 /4400012792
OCMI, Inc. (SBE)	2490026 /4400012793
Red Brick Consulting, Inc. (Micro-SBE)	2490027 /4400012794

Authorization to award four (4) formally competed contracts to provide Construction Schedule Reviews and/or Time Impact Analysis procured via RFP R-24023. Pillar 4 of the Strategic Plan is supported by this action.

Contract Term: 05/01/24 through 04/30/29, including two (2) one-year renewal options.

NOT-TO-EXCEED AGGREGATE AMOUNT

\$5,000,000 (100% Bond Funds)

Requester:

Greg Garcia, Director Project Execution,
Facilities Services Division

ATTACHMENT B
APPROVAL OF CONTRACTS NOT UNDER DELEGATED AUTHORITY

ADOPTED BY BOARD
421
APRIL 9, 2024

B. APPROVAL OF LOCAL HAZARD MITIGATION PLAN CONTRACT

\$150,000

Item R

<u>CONTRACTOR</u>	<u>IDENTIFICATION NO.</u>
Foster Morrison Consulting Ltd.	2490023 /4400012763

Authorization to award a formally competed contract to update the District's Local Hazard Mitigation Plan (LMHP) selected via RFP R-24036. The LHMP provides a framework to lessen the impact of natural disasters by encouraging whole-community involvement, assessing risk, and using a range of resources, local governments can reduce risk to people, economies, and natural environments. Additionally, the updated plan will ensure the District would be eligible for Federal Emergency Management Agency (FEMA) Pre-Disaster Mitigation and Hazard Mitigation Grant programs. Pillar 4 of the Strategic Plan is supported by this action.

Contract Term: 05/01/24 through 04/30/27.

NOT-TO-EXCEED AGGREGATE AMOUNT

\$150,000 (100% FEMA Funds)

Requester:

Carlos A. Torres, Director
Office of Environmental Health and Safety



Board of Education Report

File #: Rep-064-24/25, Version: 1

Approve the Definition of 12 Classroom Upgrade Projects and Amend the Facilities Services Division Strategic Execution Plan to Incorporate Therein

October 22, 2024

Facilities Services Division

Action Proposed:

Approve the definition of 12 Classroom Upgrade Projects (Projects), as described in Exhibit A, and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein. The combined budget for the proposed Projects is \$106,372,000.

Authorize the Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the proposed Projects including budget modifications and the purchase of equipment and materials.

Background:

On August 24, 2021, the Board of Education (Board) adopted an update to the School Upgrade Program (SUP) to integrate Measure RR funding and priorities into its operational framework. The updated SUP framework and the Measure RR Implementation Plan (Implementation Plan) help guide the identification of sites and development of project proposals. The Implementation Plan included, among other priorities, the development of projects to provide upgrades focused on the interior of existing classroom spaces.

The school sites identified for the proposed Projects were deemed to have the highest need for classroom upgrades based on their overall Facilities Condition Index (FCI) score for interior classroom spaces. FCI scores indicate the remaining service life of the physical components within classroom spaces and as compared to other schools. Additionally, the priority for implementation of the proposed Projects focused on middle school programs with the goal of attracting and retaining students transitioning from elementary to secondary education across the District's four geographic Regions.

The proposed Projects will provide upgrades to classrooms utilized for instruction, special education, and school set-asides within permanent and relocatable buildings. Each classroom within a school site has unique conditions and will be surveyed to understand deficiencies needing to be addressed. Based on the individual needs of each classroom, the scope may include upgrades to technology, electrical upgrades to support new classroom technology, white boards, tack boards, window blinds, paint, and security locks. The proposed Projects also include providing new classroom furniture, replacing damaged ceiling tiles, and other upgrades required to comply with local, state, and federal requirements.

Bond Oversight Committee Recommendations:

This item was considered by the School Construction Bond Citizens' Oversight Committee (BOC) at its meeting on October 10, 2024, as referenced in Exhibit B. The presentation that was provided is included as Exhibit C. Staff has concluded that this proposed Facilities SEP amendment is in alignment with BOC recommendations and will facilitate Los Angeles Unified School District's ability to successfully complete the

Facilities SEP.

Expected Outcomes:

Approval of the 12 proposed Projects and amendment to the Facilities SEP to incorporate therein. The approval will enable staff to proceed with the design and construction of the proposed Projects.

The upgraded classrooms, once completed, will provide facilities that support education programs and student achievement. The proposed Projects will also decrease demands for repair and maintenance, alleviate the burden on custodial staff, and benefit the local economy by creating tax revenue and new jobs.

Board Options and Consequences:

Adoption of the proposed action will authorize staff to proceed with the expenditure of Bond Program funds and begin the environmental reviews and clearances, design, procurement, construction, and other activities necessary to implement the proposed Projects.

If the proposal is not approved, the proposed Projects will not commence, and the schools will not benefit from the upgrades being proposed.

Policy Implications:

The proposal does not impact Los Angeles Unified policy. It furthers implementation of the update to the SUP to integrate Measure RR funding and priorities into its operational framework. Furthermore, the proposal is consistent with the District's long-term goal to address unmet school facilities needs and significantly improve the conditions of aging and deteriorating school facilities as described in the District's local bond measures K, R, Y, Q, and RR. The proposed action advances Los Angeles Unified's 2022-2026 Strategic Plan Pillar 4 Operational Effectiveness Modernizing Infrastructure by upgrading classrooms at schools.

Budget Impact:

The combined Project budget for the 12 proposed Projects is \$106,372,000. The proposed Projects will be funded by Bond Program funds targeted in the School Upgrade Program for major modernizations, upgrades, and reconfigurations to school campuses.

The \$11,423,000 budget for the proposed Project at Robert Louis Stevenson College & Career Prep includes \$1,819,000 for classrooms presently occupied by a co-located charter school pursuant to Education Code section 47614 (Proposition 39). Bond Program funds targeted for Charter School Facilities Upgrades and Expansions will be transferred to funds earmarked in the SUP for major modernizations, upgrades, and reconfigurations to school campuses, and all aspects of the proposed upgrades will be owned entirely by District.

The Project budgets were prepared based on the current information known, and assumptions about the proposed Project scope, site conditions, and market conditions. The Project budgets will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise and will be adjusted accordingly to enable the successful completion of the proposed Projects.

Student Impact:

The proposed Projects, once completed, will help ensure approximately 11,500 current and future students attending these 12 schools are provided with safe, welcoming, and state-of-the-art learning environments that support student-centered, experiential, and engaged learning. The proposed Projects will also allow schools to attract and retain future students, which builds school pride and enhances opportunities to create a positive

File #: Rep-064-24/25, Version: 1

school culture.

Equity Impact:

School sites represent all four Regions (North, East, South, and West) and were prioritized based on their Facilities Condition Index scores.

Issues and Analysis:

Staff will implement all opportunities to minimize construction impacts on school operations and existing education programs. As necessary, the temporary use of unused classrooms, off-hour construction and other opportunities will be utilized to reduce impacts to the existing education programs at each school.

The Office of Environmental Health and Safety (OEHS) will evaluate the proposed Projects in accordance with the California Environmental Quality Act (CEQA).

Attachments:

Exhibit A: Scope, Budget, and Schedule for 12 Classroom Upgrade Projects

Exhibit B: BOC Resolution


Exhibit C: BOC Presentation

Informatives:

None

Submitted:

09/20/24

RESPECTFULLY SUBMITTED,**APPROVED BY:**
ALBERTO M. CARVALHO
Superintendent
PEDRO SALCIDO
Deputy Superintendent, Business Services and Operations**REVIEWED BY:****APPROVED BY:**
DEVORA NAVERA REED
General Counsel
KRISZTINA TOKES
Chief Facilities Executive
Facilities Services Division☒ Approved as to form.**REVIEWED BY:****PRESENTED BY:**
NORBERTO DELGADILLO
Deputy Chief Financial Officer
ISSAM DAHDUL
Director of Facilities Planning & Development
Facilities Services Division☒ Approved as to budget impact statement.

1. Dodson Middle School – Classroom Upgrade Project

Region South, Board District 7 (Tanya Ortiz Franklin)

The proposed project includes upgrades to the interiors of approximately 60 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the Americans with Disabilities Act (ADA), Division of the State Architect (DSA), California Environmental Quality Act (CEQA), Department of Toxic Substances Control (DTSC), or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$9,570,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

2. Drew Middle School - Classroom Upgrade Project

Region South, Board District 7 (Tanya Ortiz Franklin)

The proposed project includes upgrades to the interiors of approximately 56 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$9,106,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

3. El Sereno Middle School – Classroom Upgrade Project

Region East, Board District 2 (Dr. Rocio Rivas)

The proposed project includes upgrades to the interiors of approximately 55 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$8,847,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

4. Mann UCLA Community School – Classroom Upgrade Project

Region South, Board District 1 (Dr. George McKenna)

The proposed project includes upgrades to the interiors of approximately 41 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$6,660,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

5. Mount Gleason Middle School – Classroom Upgrade Project

Region North, Board District 6 (Kelly Gonez)

The proposed project includes upgrades to the interiors of approximately 50 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$8,125,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

6. Nimitz Middle School - Classroom Upgrade Project

Region East, Board District 5 (Jackie Goldberg)

The proposed project includes upgrades to the interiors of approximately 63 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$9,960,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

7. Pio Pico Middle School – Classroom Upgrade Project

Region West, Board District 1 (Dr. George McKenna)

The proposed project includes upgrades to the interiors of approximately 28 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$4,587,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

8. Reed Middle School – Classroom Upgrade Project

Region North, Board District 3 (Scott Schmerelson)

The proposed project includes upgrades to the interiors of approximately 58 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$9,441,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

9. Revere Charter Middle School – Classroom Upgrade Project

Region West, Board District 4 (Nick Melvoin)

The proposed project includes upgrades to the interiors of approximately 69 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$10,586,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

10. Robert Louis Stevenson College & Career Prep – Classroom Upgrade Project

Region East, Board District 2 (Dr. Rocio Rivas)

The proposed project includes upgrades to the interiors of approximately 72 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$11,423,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

11. Sepulveda Middle School – Classroom Upgrade Project

Region North, Board District 6 (Kelly Gonez)

The proposed project includes upgrades to the interiors of approximately 72 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$11,229,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

12. Twain Middle School – Classroom Upgrade Project

Region West, Board District 4 (Nick Melvoin)

The proposed project includes upgrades to the interiors of approximately 42 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$6,838,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

SCHOOL CONSTRUCTION BOND CITIZENS' OVERSIGHT COMMITTEE

D. Michael Hamner, FAIA, Chair
American Institute of Architects
Robert Campbell, Vice-Chair
L.A. Co. Auditor-Controller's Office
Dr. Samantha Rowles, Secretary
LAUSD Student Parent
Patrick MacFarlane, Executive Committee
Early Education Coalition
Scott Pansky, Executive Committee
L.A. Area Chamber of Commerce

Joseph P. Buchman – Legal Counsel
Burke, Williams & Sorensen, LLP
Lori Raineri and Keith Weaver – Oversight Consultants
Government Financial Services Joint Powers Authority

Neelura Bell
CA Charter School Association
Sandra Betts
CA Tax Reform Assn.
Chad Boggio
L.A. Co. Federation of Labor AFL-CIO
Aleigh Lewis
L.A. City Controller's Office
Jennifer McDowell
L.A. City Mayor's Office
Brian Mello
Assoc. General Contractors of CA

Santa Ramirez
Tenth District PTSA
William O. Ross IV
31st District PTSA
Ashley Kaiser (Alternate)
Assoc. General Contractors of CA
Connie Yee (Alternate)
L.A. Co. Auditor-Controller's Office
Vacant
Senior Citizens' Organization
Vacant
LAUSD Student Parent

Timothy Popejoy
Bond Oversight Administrator
Perla Zitle
Bond Oversight Coordinator

RESOLUTION 2024-30**BOARD REPORT 064-24/25**

**RECOMMENDING BOARD APPROVAL TO DEFINE AND APPROVE 12
CLASSROOM UPGRADE PROJECTS AND AMEND THE FACILITIES SERVICES
DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN**

WHEREAS, Los Angeles Unified School District (Los Angeles Unified) Staff proposes that the Board of Education (Board) define and approve 12 Classroom Upgrade Projects (Projects), as described in Exhibit A to Board Report No. 064-24/25, and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein; and

WHEREAS, Los Angeles Unified Staff also requests that the Board authorize the Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the proposed Projects including budget modifications and the purchase of equipment and materials; and

WHEREAS, The proposed Projects will provide upgrades to classrooms utilized for instruction, special education, and school set-asides within permanent and relocatable buildings. Each classroom within a school site has unique conditions and will be surveyed to understand deficiencies needing to be addressed. Based on the individual needs of each classroom, the scope may include upgrades to technology, electrical upgrades to support new classroom technology, white boards, tack boards, window blinds, paint, and security locks. The proposed Projects also include providing new classroom furniture, replacing damaged ceiling tiles, and other upgrades required to comply with local, state, and federal requirements; and

WHEREAS, The combined Project budget for the proposed Projects is \$106,372,000. The proposed Projects will be funded with Bond Program funds targeted in the School Upgrade Program for major modernizations, upgrades, and reconfigurations to school campuses; and

RECOMMENDING BOARD APPROVAL TO DEFINE AND APPROVE 12 CLASSROOM UPGRADE PROJECTS AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN

WHEREAS, The \$11,423,000 budget for the proposed Project at Robert Louis Stevenson College & Career Prep includes \$1,819,000 for classrooms presently occupied by a co-located charter school pursuant to Education Code section 47614 (Proposition 39). Bond Program funds targeted for Charter School Facilities Upgrades and Expansions will be transferred to funds earmarked in the SUP for major modernizations, upgrades, and reconfigurations to school campuses, and all aspects of the proposed upgrades will be owned entirely by Los Angeles Unified ; and

WHEREAS, The Los Angeles Unified Office of General Counsel has reviewed the proposed Projects and determined that they may proceed to the School Construction Bond Citizens' Oversight Committee (BOC) for its consideration for recommendation to the Board of Education; and

WHEREAS, Los Angeles Unified Staff has concluded that this proposed Facilities SEP amendment will facilitate Los Angeles Unified's ability to successfully implement the Facilities SEP.

NOW, THEREFORE, BE IT RESOLVED THAT:

1. The BOC recommends that the Board define and approve 12 Classroom Upgrade Projects as described in Board Report No. 064-24/25, a copy of which is attached hereto in the form it was presented to the BOC and is incorporated herein by reference and amend the Facilities SEP accordingly.
2. This resolution shall be transmitted to the Los Angeles Unified Board and posted on the BOC's website.
3. Los Angeles Unified is directed to track the above recommendation and to report on the adoption, rejection, or pending status of the recommendations as provided in section 6.2 of the Charter and Memorandum of Understanding between the BOC and Los Angeles Unified.

ADOPTED on October 10, 2024, by the following vote:

AYES: 11

ABSTENTIONS: 1

NAYS: 0

ABSENCES: 1

/Michael Hamner/

D. Michael Hamner
Chair

/Samantha Rowles/

Dr. Samantha Rowles
Secretary



Classroom Upgrade Projects



*Bond Oversight Committee Meeting
October 10, 2024*

Background



- August 2021 – Facilities School Upgrade Program was approved, which included \$350 Million for Classroom Upgrade Projects
 - 2,000 classrooms at approximately 50 schools
- Projects will upgrade classroom interiors throughout a school, without moving walls or replacing ceilings, lighting, or windows

Priority Middle Schools–Top 48



*Equally Distributed per Region + Ranked by Classroom FCI**

Group	Rank by Highest Classroom FCI*	Region East	Region North	Region South	Region West	Board Approval of Project Definition
1	1	LA ACADEMY MS	PACOIMA MS	GOMPERS MS	PALMS MS	Q4 2023
2	2	ADAMS MS	ARMSTRONG MS	AUDUBON MS**	BANCROFT MS	Q2 2024
	3	BURBANK ATC MAG MS	HALE CHART ACAD MS	FLEMING MS	WEBSTER MS**	Q2 2024
3	4	EL SERENO MS	SEPULVEDA MS	DODSON MS	TWAIN MS	Q4 2024
	5	STEVENSON C&CP**	MOUNT GLEASON MS	DREW MS	REVERE CHARTER MS	Q4 2024
	6	NIMITZ MS	REED MS	MANN UCLA COMM SCH	PIO PICO MS	Q4 2024
4	7	CARVER MS	SAN FERNANDO MS	MUIR MS	KING MAG MS	Q1 2025
	8	GAGE MS	PORTOLA CHARTER MS	MARKHAM MS	EMERSON COMM CHART MS	Q1 2025
	9	VIRGIL MS**	SUTTER MS**	BETHUNE MS	BERENDO MS	Q1 2025
5	10	SOUTH GATE MS	PORTER MS	WILMINGTON MAG MS	COCHRAN MS	Q3 2025
	11	NIGHTINGALE MS	MULHOLLAND MS	EDISON MS	WRIGHT STEAM MAG MS**	Q3 2025
	12	GRIFFITH STEAM MAG MS	LAWRENCE MS	CARNEGIE MS	LE CONTE MS**	Q3 2025

**Classroom FCI includes classrooms used for instruction, special education, and school set asides*

***Co-located charter present at campus site*

~2,000 classrooms proposed for upgrade

~46,000 middle school students positively impacted

Scoping Tenets



Project will include upgrades to classrooms:

- In permanent and relocatable buildings
- Used for instruction, special education, and school set-asides
- Co-located charter school classrooms
- Does not include upgrades to District set-asides, classrooms out-of-service, and unallocated

Scoping Tenets



Work may include:

- New classroom technology equipment
- Sound enhancements
- New classroom furniture
- Replacement of window blinds
- Interior painting
- Replacement of damaged ceiling tiles
- Limited electrical upgrades to support new classroom technology
- Accessibility improvements
(as necessary per DSA requirements)

Construction Execution Strategy

Work to occur in 2 Phases

- **Phase 1 (Year 1-2) – Non-DSA Scope**
 - Upgrade Blinds, Classroom Door Locks, and Damaged Ceiling Tiles
 - Provide New Classroom Furniture and Interior Painting
- **Phase 2 (Year 2-3) – DSA review required**
 - Classroom Technology Equipment
 - Provide Electrical Support for Technology and Required Accessibility Improvements

Construction Execution Strategy **LAUSD** UNIFIED


Work to be scheduled for nights, weekends, and school breaks

- No Interim Housing to be added to school sites
- Maximize existing swing space, if available



Project Location Map

447



Dodson Middle School Classroom Upgrade Project


Board District 7 (Tanya Ortiz Franklin)
Region South

Project:
Upgrade of approximately 60 classrooms used for instruction, special education, and support spaces.

Scope:
Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:	\$9,570,000
• Site & Environmental	0.3%
• Plans	8%
• Construction	83%
• Management	5%
• Other/Reserve	4%

Project Schedule:	
• Construction Start	Q4-2025
• Construction Complete	Q1-2027

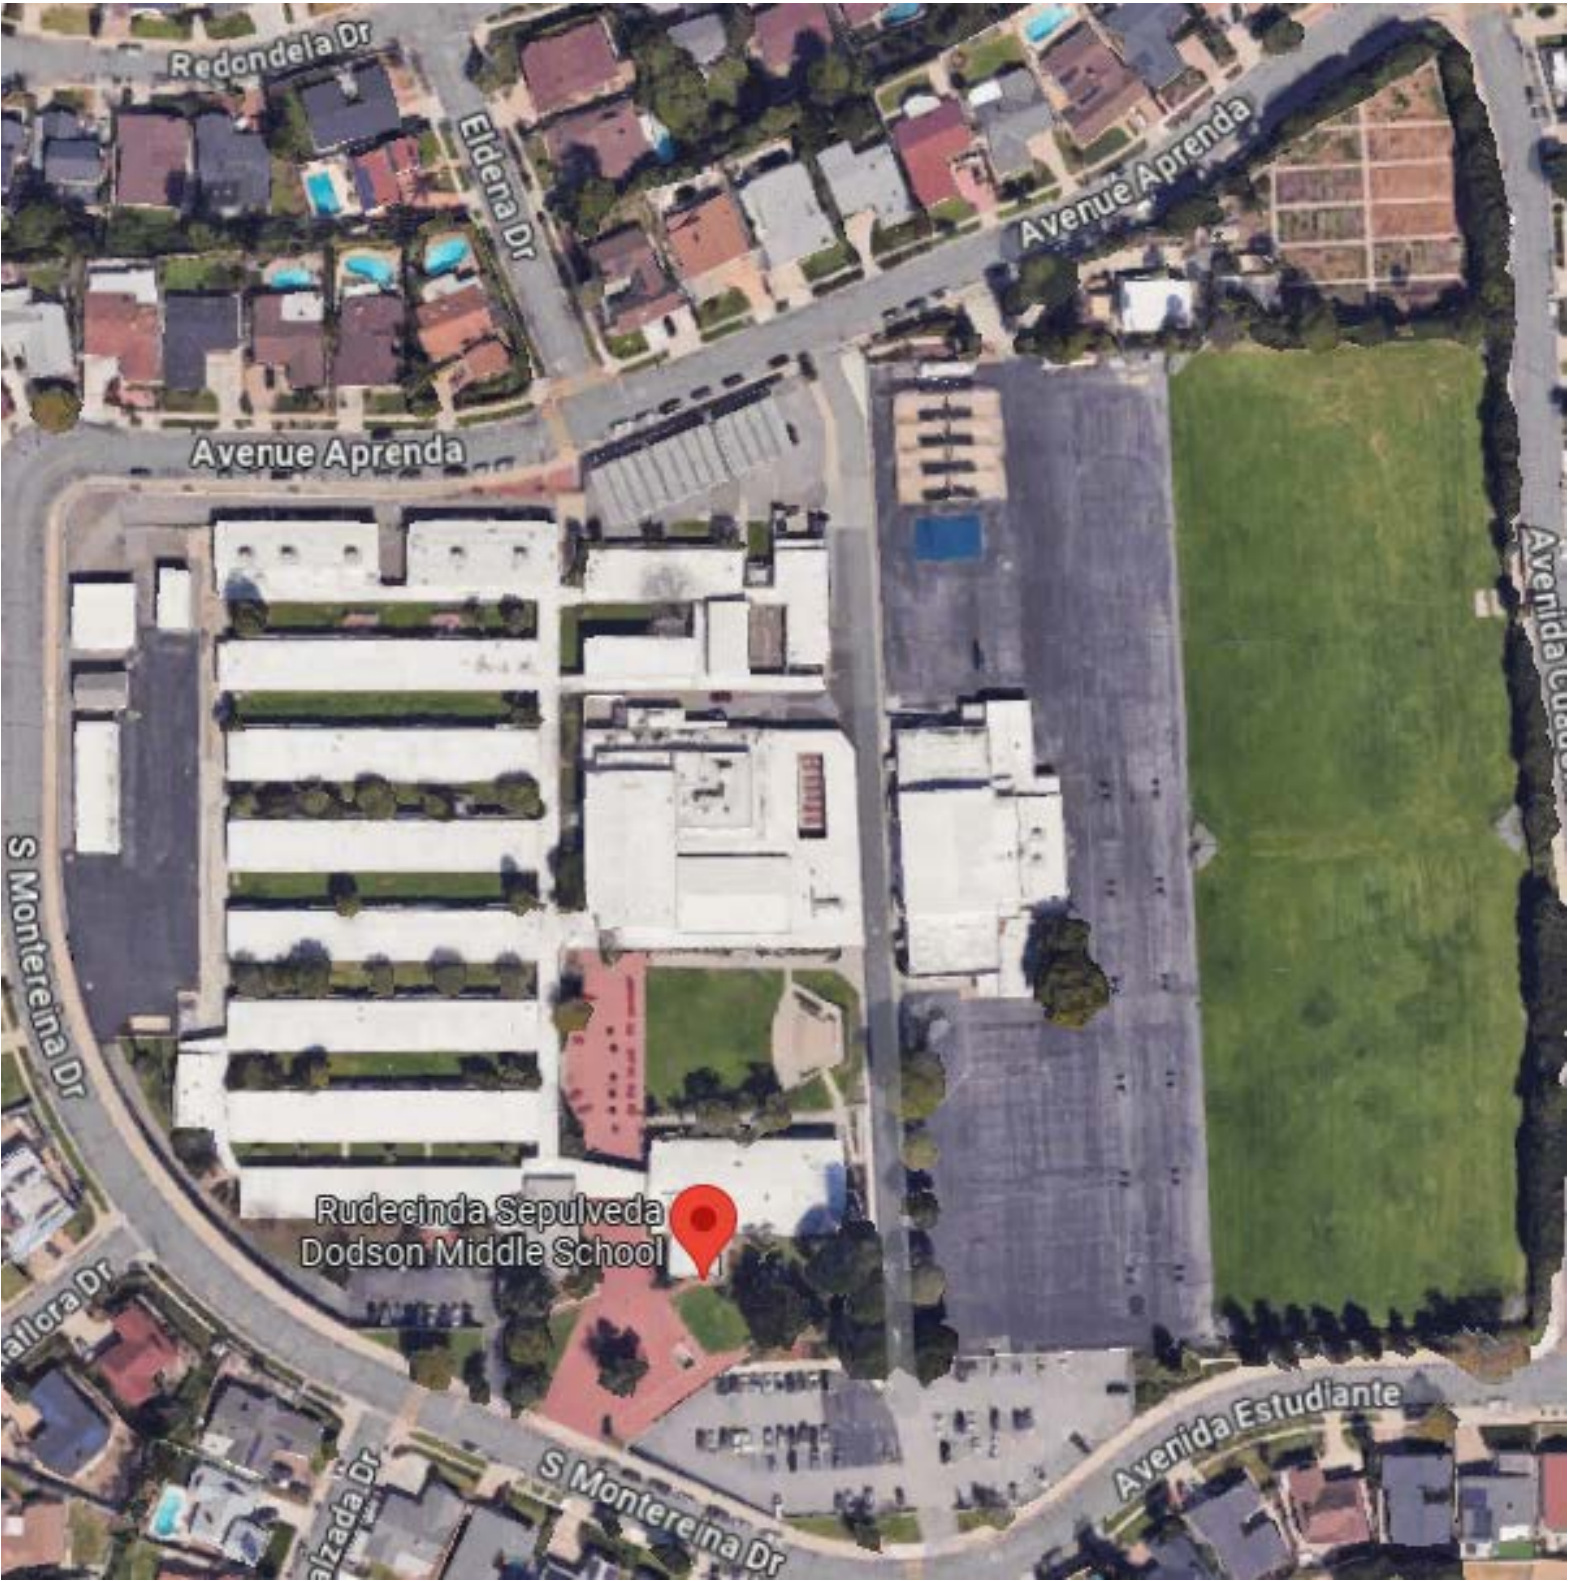

Drew Middle School Classroom Upgrade Project

Board District 7 (Tanya Ortiz Franklin)
Region South

Project:

Upgrade of approximately 56 classrooms used for instruction, special education, and support spaces.

Scope:

Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:	\$9,106,000
• Site & Environmental	0.4%
• Plans	8%
• Construction	83%
• Management	5%
• Other/Reserve	4%

Project Schedule:

• Construction Start	Q4-2025
• Construction Complete	Q1-2027



El Sereno Middle School Classroom Upgrade Project

Board District 2 (Dr. Rocio Rivas)
Region East

Project:

Upgrade of approximately 55 classrooms used for instruction, special education, and support spaces.

Scope:

Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:

	\$8,847,000
• Site & Environmental	0.4%
• Plans	8%
• Construction	83%
• Management	5%
• Other/Reserve	4%

Project Schedule:

• Construction Start	Q4-2025
• Construction Complete	Q1-2027



Mann UCLA Community School Classroom Upgrade Project

Board District 1 (Dr. George McKenna)
Region South

Project:

Upgrade of approximately 41 classrooms used for instruction, special education, and support spaces.

Scope:

Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:

	\$6,660,000
• Site & Environmental	0.5%
• Plans	8%
• Construction	83%
• Management	5%
• Other/Reserve	4%

Project Schedule:

• Construction Start	Q4-2025
• Construction Complete	Q1-2027



Mount Gleason Middle School Classroom Upgrade Project

Board District 6 (Kelly Gonez)
Region North

Project:

Upgrade of approximately 50 classrooms used for instruction, special education, and support spaces.

Scope:


Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:

	\$8,125,000
• Site & Environmental	0.4%
• Plans	8%
• Construction	83%
• Management	5%
• Other/Reserve	4%

Project Schedule:

• Construction Start	Q4-2025
• Construction Complete	Q1-2027

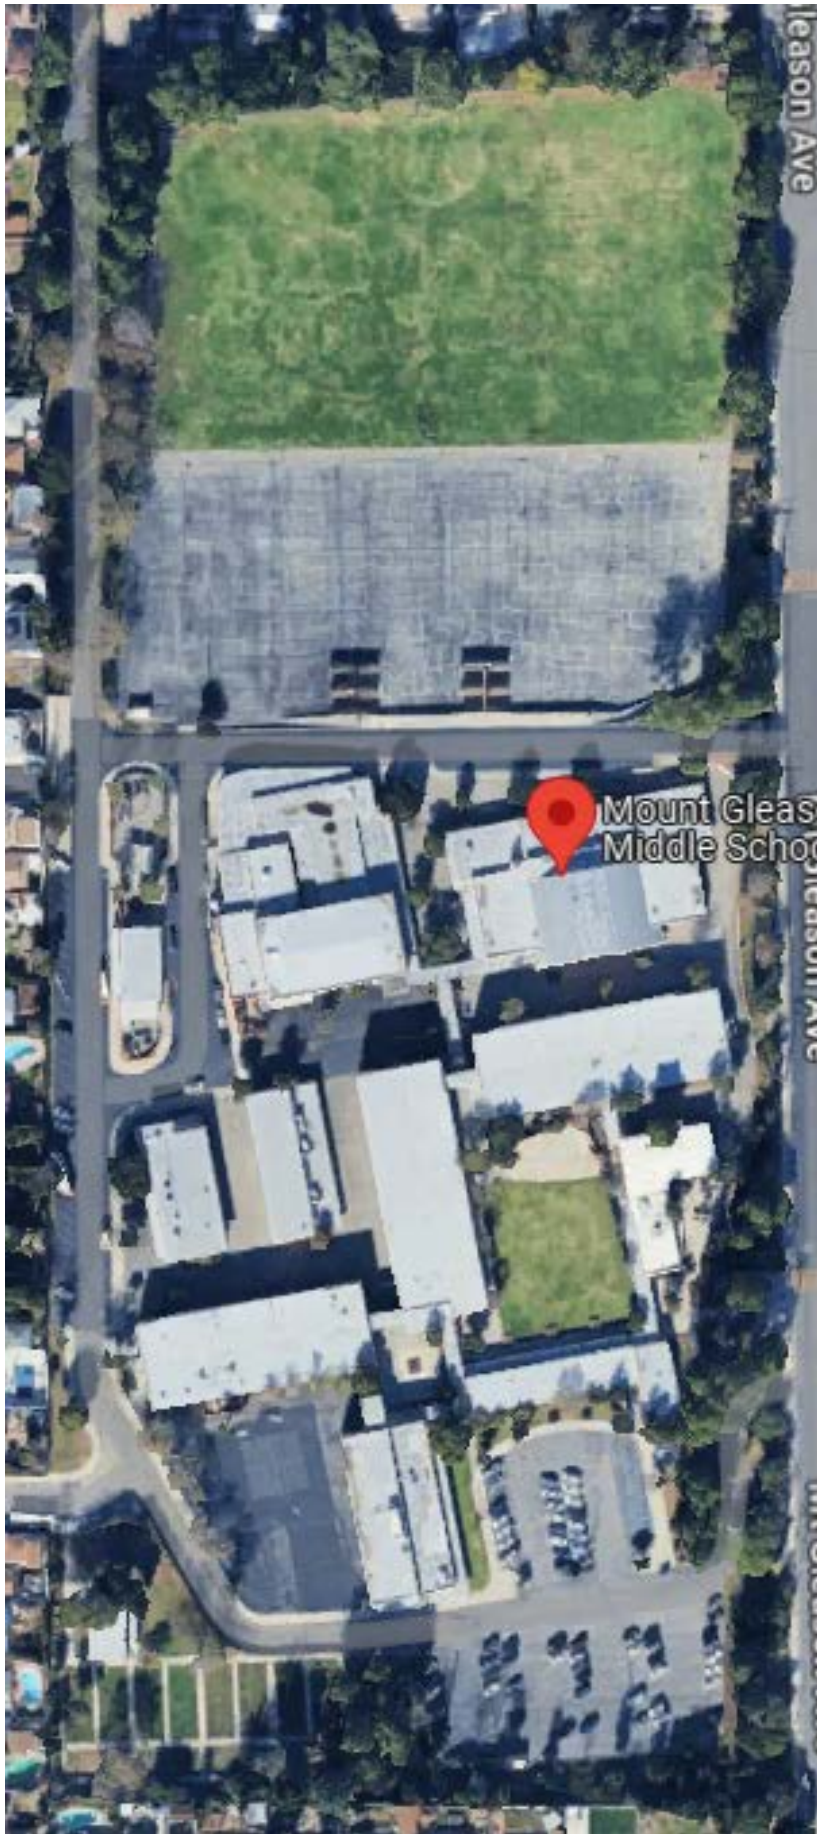

Nimitz Middle School Classroom Upgrade Project

Board District 5 (Jackie Goldberg)
Region East

Project:

Upgrade of approximately 63 classrooms used for instruction, special education, and support spaces.

Scope:

Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:

	\$9,960,000
• Site & Environmental	0.3%
• Plans	8%
• Construction	83%
• Management	5%
• Other/Reserve	4%

Project Schedule:

• Construction Start	Q4-2025
• Construction Complete	Q1-2027



Pio Pico Middle School Classroom Upgrade Project

Board District 1 (Dr. George McKenna)
Region West

Project:

Upgrade of approximately 28 classrooms used for instruction, special education, and support spaces.

Scope:

Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:

• Site & Environmental	\$4,587,000
• Plans	0.7%
• Construction	8%
• Management	82%
• Other/Reserve	5%
	4%

Project Schedule:

• Construction Start	Q4-2025
• Construction Complete	Q1-2027



Reed Middle School Classroom Upgrade Project

Board District 3 (Scott Schmerelson)
Region North

Project:

Upgrade of approximately 58 classrooms used for instruction, special education, and support spaces.

Scope:

Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:

	\$9,441,000
• Site & Environmental	0.3%
• Plans	8%
• Construction	83%
• Management	5%
• Other/Reserve	4%

Project Schedule:

• Construction Start	Q4-2025
• Construction Complete	Q1-2027



Revere Charter Middle School Classroom Upgrade Project

Board District 4 (Nick Melvoin)
Region West

Project:

Upgrade of approximately 69 classrooms used for instruction, special education, and support spaces.

Scope:

Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:

\$10,586,000	
• Site & Environmental	0.3%
• Plans	8%
• Construction	83%
• Management	5%
• Other/Reserve	4%

Project Schedule:

• Construction Start	Q4-2025
• Construction Complete	Q1-2027



Robert Louis Stevenson College & Career Prep Classroom Upgrade Project

Board District 2 (Dr. Rocio Rivas)
Region East

Project:
Upgrade of approximately 72 classrooms used for instruction, special education, and support spaces.

Scope:
Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:	\$11,423,000
• Site & Environmental	0.3%
• Plans	8%
• Construction	83%
• Management	5%
• Other/Reserve	4%

Project Schedule:	
• Construction Start	Q4-2025
• Construction Complete	Q1-2027

*Upgrades to classrooms occupied by co-located charter school will be funded with \$1,819,000 from Bond Program funds earmarked for Charter School Facilities Upgrades and Expansions.



Sepulveda Middle School Classroom Upgrade Project

Board District 6 (Kelly Gonez)
Region North

Project:

Upgrade of approximately 72 classrooms used for instruction, special education, and support spaces.

Scope:


Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:

	\$11,229,000
• Site & Environmental	0.3%
• Plans	8%
• Construction	83%
• Management	5%
• Other/Reserve	4%

Project Schedule:

• Construction Start	Q4-2025
• Construction Complete	Q1-2027

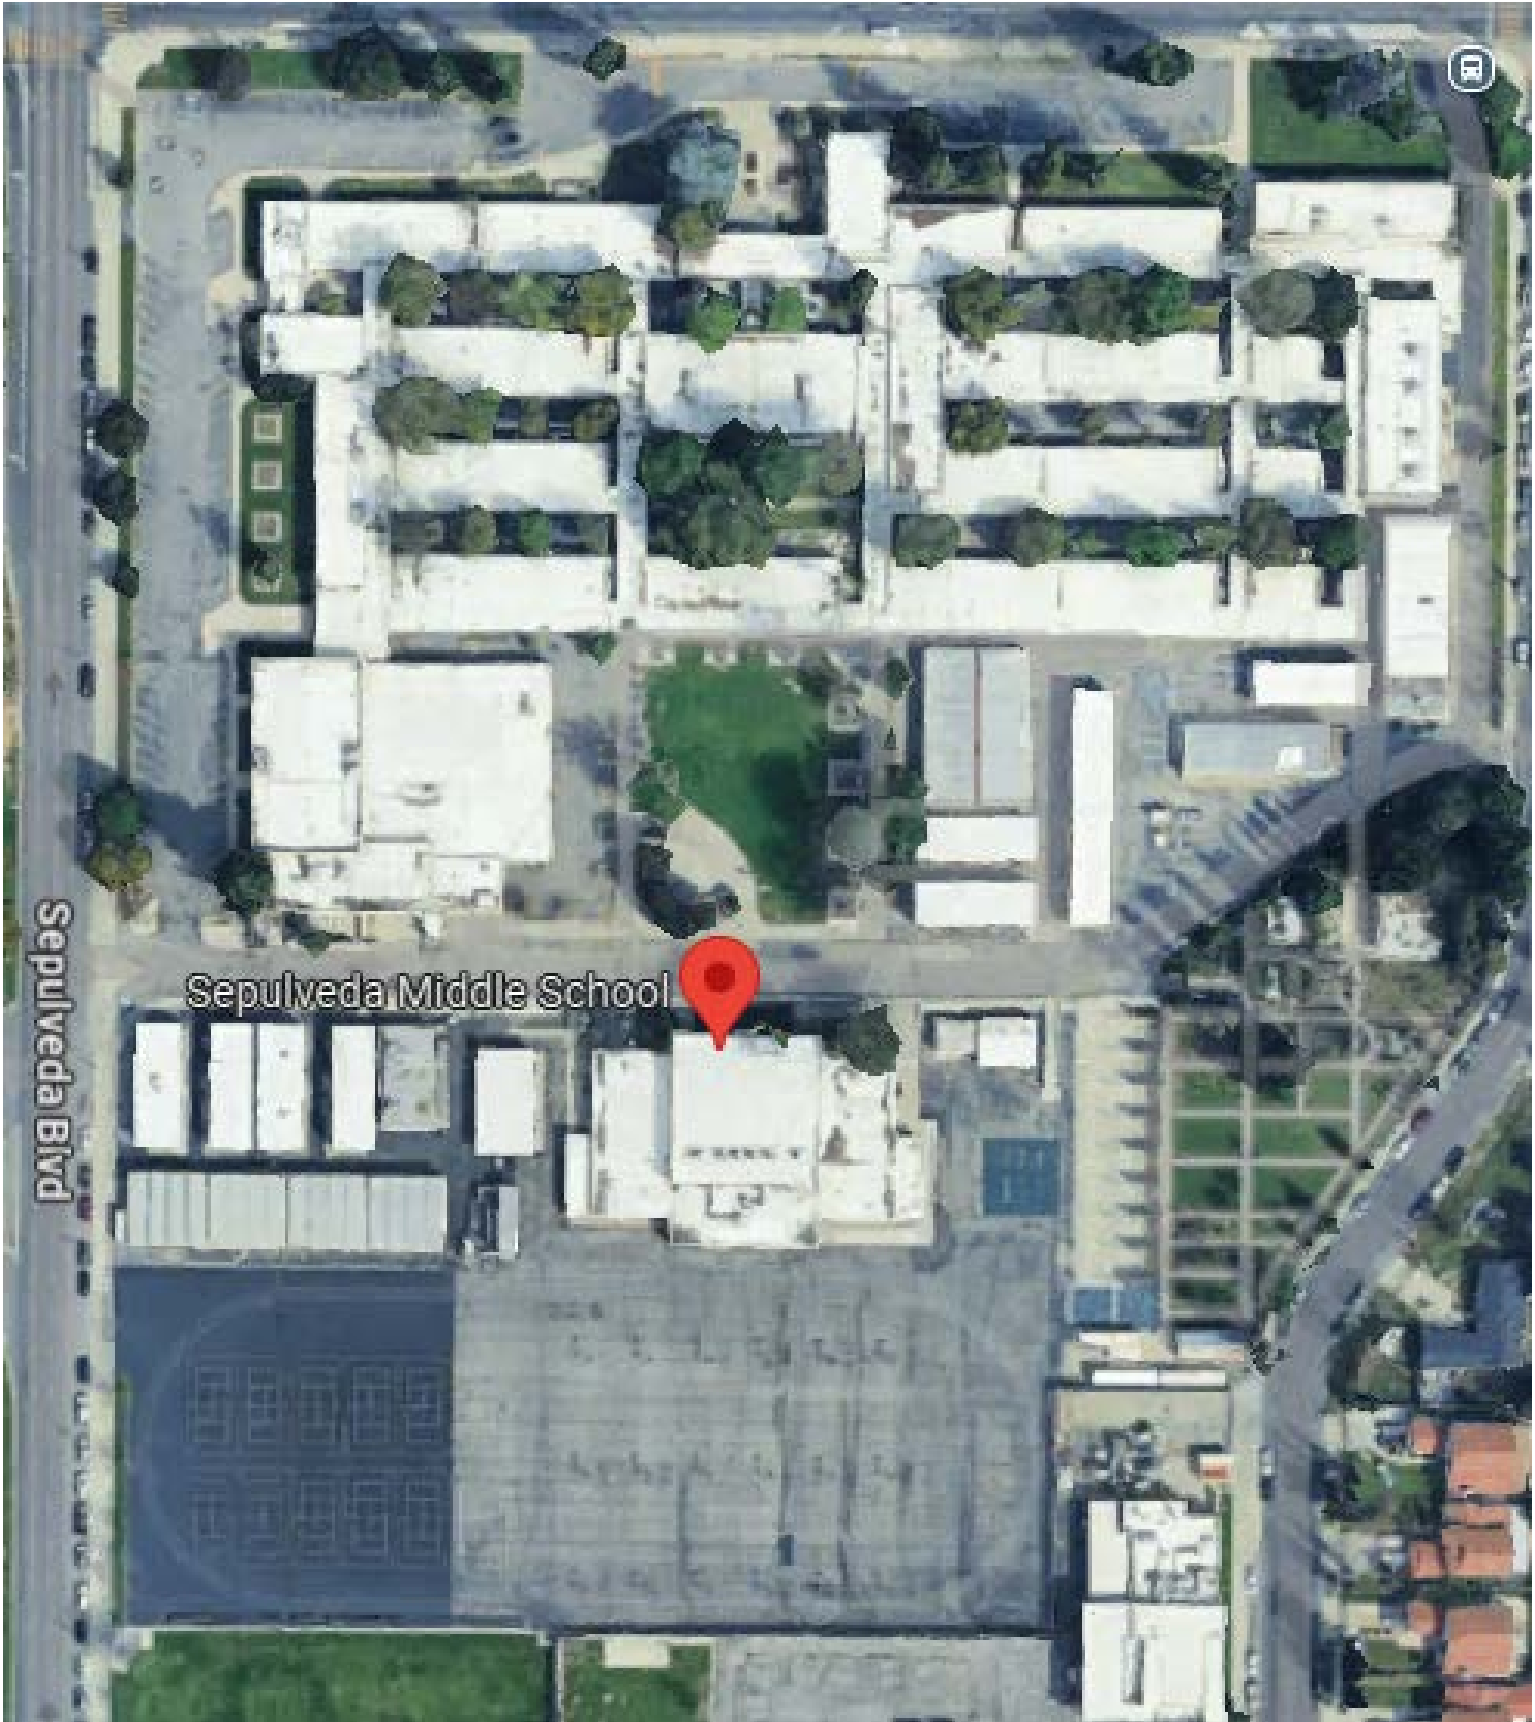

Twain Middle School Classroom Upgrade Project

Board District 4 (Nick Melvoin)
Region West

Project:

Upgrade of approximately 42 classrooms used for instruction, special education, and support spaces.

Scope:

Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:

	\$6,838,000
• Site & Environmental	0.5%
• Plans	8%
• Construction	83%
• Management	5%
• Other/Reserve	4%

Project Schedule:

• Construction Start	Q4-2025
• Construction Complete	Q1-2027



Questions?



Board of Education Report

File #: Rep-024-23/24, Version: 2

Capital Plan Projects

December 12, 2023

Office of the Chief Business Officer

Action Proposed:

Approve the use of \$423.5 million of Certificates of Participation (COP) to fund all or a portion of nine Capital Plan projects and/or programs, to be undertaken at one or more sites, the scope schedule and budget of which is outlined in Attachment A, and authorize the Superintendent and/or his designee(s) to execute all instruments necessary, as legally permissible, to implement the initial Capital Plan projects and/or programs, including budget modifications.

Some of the listed projects may require additional funding to fully complete, however this proposal is to authorize COP expenditures in the amount equal to what was generated by the August 2023 issuance, which was authorized by the Board of Education (Board) in June 2023. The funding strategy for some projects may include the use of various General Fund sources.

Background:

On June 13, 2023, the Board authorized a resolution approving the execution and delivery of COPs in the not-to-exceed amount of \$500 million (Board Report No. 300-22/23). In August 2023, the Office of the Chief Business Officer (CBO) sold COPs generating \$423.5 million to fund critical unmet needs of our school support facilities, as well as high-priority school facility needs for which sufficient bond funding is not currently available.

Under the leadership of the Chief Business Officer, a five-year capital plan covering fiscal years 2023-24 through 2027-2028 is being developed. Projects and/or programs were proposed as priority projects from various divisions, and only individual projects over \$1 million for which sufficient bond funds are not currently available and/or eligible were considered. All projects were reviewed by a steering committee comprised of various District senior executives using criteria including health and safety, regulatory compliance, alignment to the Strategic Plan, and economic impact. This work resulted in the identification of 12 priority projects and/or programs with an approximate budget of \$1.3 billion, approximately \$1.1 billion of which was identified for COPs proceeds. Requests to authorize future sales of COPs are anticipated to be proposed to the Board in subsequent years. The projects and/or programs being proposed for funding are a result of this work. All 12 identified projects and/or programs are listed below:

1. Enrollment Modernization Project
2. Student Information Systems Upgrades Project
3. Student Support Applications Modernization*
4. Student Data Analytics, Reporting and Dashboards Project*
5. Sun Valley Electric Buses and Generator Purchases Project
6. Sun Valley Transportation Center Electrification Project*
7. Green Schools for All Program*

8. Campus Security Systems Improvements*
9. Cybersecurity Improvements*
10. Gardena Area Transportation Center and Electric Bus Charging**
11. Gardena Area Electric Bus and Generator Purchases**
12. Procurement Services Support Center Upgrades: Electrification and Industrial Fans**

*Based on current scope and budget estimates, anticipated to require additional funding to fully complete/implement.

**No funding is being requested as part of this action; however, their current total estimated budget is part of the \$1.3 billion Capital Plan estimate.

The project budgets were prepared based on current information, and assumptions about the project scope, site conditions, and market conditions. The project budgets will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise and will be adjusted accordingly to enable the successful completion of the proposed projects.

Expected Outcomes:

The Board will approve nine Capital Plan projects and/or programs, allowing the District to move forward with needed capital improvements.

Board Options and Consequences:

Upon Board approval, staff will be authorized to proceed with the expenditure of COP funds and all other activities necessary to implement the proposed projects. If the proposed action is not approved, the District will not move forward with the projects.

Policy Implications:

This does not impact existing policy.

Budget Impact:

The 2023-24 Budget included the annual debt service for the 2023 COPs and non-capital costs for the projects. In Fiscal Year 2024, the annual debt service cost is estimated at \$11.3 million, and from FY 2025-FY 2038 the estimated annual cost is \$33.4 million. The debt service will be paid out of the District's General Fund. Furthermore, some projects will require additional funding to fully complete and/or implement. Sources of funds may vary. These additional costs are estimated to be approximately \$800 million, with the majority of funds, approximately \$650 million, expected to be funded by future COP issuances, and approximately \$89.5 million from Restricted General Fund-Expanded Learning Opportunity Program (ELOP).

A portion of the scope of five projects was temporarily front funded with operational budget with the intent to reimburse with COP proceeds once approved for specific projects. With the Board's approval of the Capital Plan projects, any prior expenditures will be transferred to the proposed projects. The projects that received some front funding are:

- Sun Valley Electric Buses and Generator Purchases Project: due to the high demand for electric school buses and to account for additional time needed to fulfill an order of 180 buses.
- Sun Valley Transportation Center Electrification Project: to help meet the District's electrification goals.
- Campus Safety Systems Improvement Projects at 291 Sites (Phase 1): due to a need to address student

safety as quickly as possible at priority school sites.

- Cybersecurity Improvement Program: due to an urgent need to begin implementing cybersecurity enhancements throughout the District.

If future COPs issuances and/or other funding sources are authorized for Capital Plan projects, all funding sources will be integrated into the Capital Plan sources of funds to support funding flexibility and efficiency and the effective implementation of the Capital Plan.

Student Impact:

Projects will improve the educational opportunities for students. The cybersecurity project will reduce risks associated with students' personal information and coursework. Similarly, the campus security project will provide a safer physical environment for students. Electrification of the school bus fleet will reduce the long-term operating costs and improve air quality.

Equity Impact:

Component	Score	Score Rationale
Recognition	2	Some of the projects are influenced by equity.
Resource Prioritization	4	Implementation of many of the projects will be conducted such that underserved populations will be a priority.
Results	3	Many of the projects, including electrification of the fleet, are expected to benefit those most impacted by historic health inequities.
TOTAL	9	

Issues and Analysis:

Projects may be undertaken at multiple District sites and/or may include various phases. Exhibit A outlines the scope of work proposed to be undertaken within the initial COPs issuance of \$423.5 million. Three of the nine projects are anticipated to be completed in their entirety, and six projects include an additional phase(s) of scope requiring further funding or a future allocation of funds to complete the initial phase as scoped.

Staff expects to return to the Board at a later date for authorization to sell additional COPs to fund projects at other District sites, additional project phases, and/or new Capital Plan projects.

Attachments:




Attachment A - Capital Plan Projects - scope, schedule, and budget

Informatives:

None.

Submitted:

12/8/2023

RESPECTFULLY SUBMITTED,
ALBERTO M. CARVALHO
Superintendent**APPROVED BY:**
PEDRO SALCIDO
Deputy Superintendent, Business Services and Operations**REVIEWED BY:**
DEVORA NAVERA REED
General Counsel**APPROVED & PRESENTED BY:**
DAVID D. HART
Chief Business Officer

☒ Approved as to form.

REVIEWED BY:
NOLBERTO DELGADILLO
Deputy Chief Business Officer, Finance

☒ Approved as to budget impact statement.

**LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report**

Attachment A: Capital Plan Projects: Scope, Schedule, and Budget

1. Enrollment Modernization Project

Project Scope: Includes creation of an efficient process for families to apply, register and enroll their children in District schools by eliminating many of the forms parents currently must submit, transitioning from a manual, paper-based process to an automated one. This initiative will be accomplished via multiple projects in coordination with various business owners and stakeholders. One of the projects under this initiative is:

- o Configure online enrollment system to be mobile friendly.
- o Implement changes identified in Board Resolution (Res-044-18/19) "Everyone Counts", which requests that additional ethnicities be added to District applications to further disaggregate data for Asian, Pacific Islander, and other ethnic groups.
- o Enhancements to applications including, but not limited to, enrollment applications, MiSiS, SAP, Focus reports, data warehouse (IODS).
- o Develop new reports and dashboards for internal use as needed.
- o Develop new reports for external Federal and State reporting as needed.

Total Project Budget and COPs Allocation: \$2,000,000

Project Schedule: Implementation is anticipated to begin in Q1-2024 and be completed in Q4-2024.

2. Student Information Systems Upgrades Project

Project Scope: Includes updates to the District's student information system, including integration with the Bell Schedule, Household Hub (a system of record for parent information), and Early Education Student Information System. The scope may include, but is not limited to:

- o *Household Hub Integration:* Integrate the household hub with all District applications that use parent information. This includes the Parent Portal, Early Ed Student Information System (EESIS), Unified Enrollment, Cafeteria Management Services (CMS), etc.

This project will also support non-application needs such as reducing mailings (e.g., a single magnet flier can be sent to a household with multiple District students), providing wrap-around services for families (e.g., chronic absenteeism, mental health, etc.), and data analysis.

Furthermore, the project will address creation of a common path for updating parent information and sharing the household hub information. Options for cleaning existing parent information and sharing the cleansed data across the applications will also be explored.

- o *My Integrated Student Information System (MiSiS) with Bell Schedule:* Optimize the management of student schedules, school calendars, and improve overall school operations. By establishing a seamless connection between MiSiS and the Bell Schedule system, schools can enhance efficiency, accuracy, and communication related to student attendance, class timetables, and daily routines.
- o *Early Education Student Information System Migration to MiSiS:* Integrate preschool student information and early information into MiSiS. This will eliminate achievement gaps before the third grade and provide instructional support by allowing educators to identify issues and provide educational interventions.

Total Project Budget and COPs Allocation: \$1,000,000

Project Schedule: Implementation is anticipated to begin in Q1-2024 and be completed in Q4-2024.

3. Student Support Applications Modernization Project

Project Scope: Technology refresh and additional functionality for the District's Student support applications, including, but not limited to the Academic Monitoring System, LAUSD Parent Portal/Mobile App upgrade, Special Education Data Management, Student Medical Services Management System, and Universal ID for students. The scope may include, but is not limited to:

- *Academic Monitoring System (AMS):* Provide ability to disaggregate student data such as Low-Income, Emergent Bilingual, Foster Youth, African American, and Students with Disabilities, and allow for real-time assessment and an instant collection of results.
- *LAUSD Parent Portal/Mobile App:* Provide additional functionality to enhance family engagement and communication around student progress and achievement. Leverage data analytics and artificial intelligence to analyze the student's progress and engage families and students with personalized recommendations and support.
- *Special Education Data Management:* Implement a web-based software system to be utilized Districtwide for the management and tracking of online Individualized Education Programs (IEPs), Individualized Family Services Plan (IFSP), Individual Service Plan (ISP), Section 504 Plans, Transition Services, RSP (Resource Program) Substitute, Due Process, Informal Dispute Resolution, State CALPADS reporting, District Validation Review, Extended School Year, Special Education Student Transportation, IEP Translation, and tracking of related services provided to students during the course of their education.
- *Student Medical Services Management System:* Implement a web-based system to be utilized Districtwide for the management and tracking of student treatment plan, protocols, medication management, immunization compliance, nursing services, health office visits, audiological evaluation, chronic conditions, health alerts, vision/audio/dental/speech/sports physical screenings, and vital monitoring.
- *Universal ID for Students:* Provide a singular ID for students to access services such as transportation, food services, library, after school programs, and school events. This will streamline many of the processes that will greatly benefit students.

Initial Budget and COPs Allocation:	\$11,400,000
<u>Future Anticipated Allocation(s):</u>	<u>\$ 3,000,000</u>
Total Anticipated Project Budget:	\$14,400,000

Project Schedule: Implementation is anticipated to begin in Q1-2024 and be completed in Q4-2025.

4. Student Data, Analytics, Reporting and Dashboards Project

Project Scope: Modernization of the District’s student data, analytics, reporting, and dashboards systems. With a continued increase in the number of tools students use to learn, there has been a significant increase in the volume of data available to help measure and inform student growth and achievement. This project puts in place / modernizes tools to understand this data. The scope may include, but is not limited to, implementation of a Cloud-based, fully managed solution for student analytics. New features / functionalities include:

- o Learning analytics
- o Guide resources
- o Supports for administrators, schools, staff, students, and parents
- o Data drill-down by region, school, and student group level, and support the learning management needs
- o Integration of curriculum, learning, student performance, student progress and related information
- o Suitable metrics and measurements
- o Notifications for exceptions
- o Incorporation of suitable views in the current workbench and views provided to schools, including those for principals, teachers and counselors, and also aggregated views for Regions and offices, to effectively monitor and manage student progress, including English Learners, students with disabilities, students experiencing homelessness, foster youth and other focus groups

Initial Budget and COPs Allocation:	\$ 4,763,040
<u>Future Anticipated Allocation(s):</u>	<u>\$ 844,800</u>
Total Anticipated Project Budget:	\$ 5,607,840

Project Schedule: Implementation is anticipated to begin in Q1-2024 and be completed in Q3-2025.

5. Sun Valley Electric Buses and Generator Purchases Project

Project Scope: Located at 11247 Sherman Way, in the community of Sun Valley, the Sun Valley Transportation Center is one of three LAUSD transportation centers located in the San Fernando Valley serving students in the surrounding communities. The buses currently residing there are equipped with internal combustion engines powered with CNG and propane fuels. The Sun Valley Transportation Center will be the first bus yard to have all its school buses transition to electric-powered.

The project will replace all 180 school buses based at Sun Valley Transportation Center with zero-emissions electric school buses (ESBs). The ESBs will be equipped with the latest safety features, including Wi-Fi and a Global Positioning System (GPS), and will have a capacity for 42 or 75 passengers (depending on the model) and an operating range of approximately 125 miles with a full charge. Studies have shown that electric buses are more fuel efficient and significantly reduce the cost of repairs and maintenance. This can result in overall savings of up to \$1.8 million per year. The new buses are anticipated to be delivered in 2025.

As part of the project, 25 propane-powered generators will be purchased to support ESB charging until the construction and installation of permanent charging infrastructure is completed (anticipated approximately two years after the delivery of the ESBs). The generator, situated on a trailer, can fully charge up to eight buses at one time in approximately six to eight hours. The chargers can be ordered and purchased, as needed, to coincide with the projected delivery of the ESBs in 2025. These chargers will also be part of the energy contingency plan, in the event there is a widespread power outage.

This project is critical to ensuring that the new ESBs will be delivered in time to replace CNG school buses with tanks expiring in April 2025. These buses must be removed from service per State and Federal regulations upon expiration. Sufficient lead time is needed for manufacturers to build the buses and for the California Highway Patrol (CHP) to inspect the buses which may take three months after the delivery of the buses.

Total Project Budget and COPs Allocation: \$88,700,000

Project Schedule: Purchases began in Q2-2023 and are anticipated to be completed in Q4-2025.

6. Sun Valley Transportation Center Electrification Project

Project Scope: The Sun Valley Transportation Center Electrification project consists of:

- o *Charging Stations:* The installation of approximately 200 electric vehicle (EV) charging stations for school buses.
- o *Solar and Battery Storage:* Provide a new solar array canopy with battery storage.
- o *Bus Wash Building Replacement:* Replace the existing bus wash with a new prefabricated bus wash building.
- o *Paving:* Provide new asphalt overlay throughout the site with new parking striping. Provide new asphalt paving in the areas of trenching for underground conduit.
- o *Perimeter Barrier Wall:* Provide a new concrete perimeter barrier wall around the site with new security gates at the vehicle entry locations.
- o *Site Lighting & Security:* Provide new site lighting poles and provide new lighting under the solar canopy. Provide new security cameras.
- o *Landscape:* Provide a new landscape buffer on Sun Valley Magnet School property, adjacent to the new pre-cast concrete wall for noise reduction and improved aesthetics.
- o *Temporary Bus Parking:* Provide temporary offsite bus parking, as needed, during construction.

Initial Budget and COPs Allocation:	\$72,162,739
<u>Future Anticipated Funding Allocation(s):</u>	<u>\$ 7,957,901</u>
Total Anticipated Project Budget:	\$80,120,640

Project Schedule: Construction is anticipated to begin in Q4-2025 and to be completed in Q4-2026.

7. Green Schools for All Program

A multi-pronged approach, which includes various project types and funding sources, will be utilized to help meet the goal of providing 30% safe and sustainable green schoolyards at all schools, to the extent feasible based on the physical constraints of individual campuses, by 2035. In total \$139,500,000 of non-bond funds are anticipated to be invested to further this work. This action allocates \$25,000,000 of COPs, and authorizes the execution of all instruments necessary, as legally permissible, to implement the projects, including those funded with General Fund-ELOP, and to make budget modifications. As detailed below, it is anticipated that an additional funding allocation of \$25,000,000 will be requested to complete this work. Additionally, \$89,500,000 of Restricted General Fund- Expanded Learning Opportunity Program (ELOP) has been allocated for these projects.

Green Schoolyard Upgrade Projects

Project Scope/Background: The proposed projects will provide improvements to schoolyards to align with the goal of providing 30% of a school sites' schoolyard with green/natural spaces. The scope may include replacing significant areas of paved surfaces with permeable surfaces that incorporate native/drought tolerant planting, the addition of natural grass play fields, the installation of trees and other shade elements to achieve 20% shade in the schoolyard, irrigation, decomposed granite and pavers, outdoor classroom elements, as well as accessibility improvements, as required, to ensure equal access to all students. After approval of this action, individual project budgets, scopes and schedules will be developed.

Approximately \$100,000,000 of non-bond funding is anticipated to be invested in the development of 15 Green Schoolyard Upgrade projects. This action will authorize \$25,000,000 of COP funding, which will be combined with an allocation of \$50,000,000 of Restricted General Fund-ELOP, to provide an initial \$75,000,000 of Green Schoolyard Upgrade projects. This is expected to provide sufficient funding to complete pre-construction activities at all 15 sites listed below, and to complete construction at a minimum of 11 sites. It is anticipated that an additional allocation of approximately \$25,000,000 will be needed to complete all of these projects.

Board District	Region	Site Name	Green Schoolyards Index Rank
1	West	Marvin ES	81
1	South	Manchester ES	84
2	East	Bridge ES	4
2	East	Dena ES	7
3	North	Canoga Park ES	16
3	North	Sylvan Park ES	30
4	North	Vanalden ES	31
4	North	Encino ES	113
5	East	San Pedro ES	5

Board District	Region	Site Name	Green Schoolyards Index Rank
5	East	Heliotrope ES	8
6	North	Strathern ES	10
6	North	Roscoe ES	15
6	North	Arminta ES	2
7	South	Gardena ES	33
7	South	Ritter ES	34

Sites were identified using the Green Schoolyards Index, which ranks sites based on the following datasets for each site: updated schoolyard measurement, existing green/natural components, CalEnviroScreen 4.0 score, and Extreme Heat Temperature Tool. The first eight sites on the list that do not have an approved or planned project that would provide substantial greening improvements* were selected. Additionally, in an effort to provide geographic equality, at least two high-ranked sites were selected in each Board District.

*(*Project types which will provide substantial greening improvements: comprehensive modernization, major modernization, classroom replacement, Pavement and Campus Exterior Upgrade (PACEUP) projects, Green Schoolyard Improvement Projects (Non-Division of the State Architect (DSA)/Americans with Disabilities Act (ADA), and third-party funded projects).*

Green Schoolyards Improvement Projects (Non-DSA)

Project Scope/Background: In addition to Green Schoolyard Upgrade Projects, Green Schoolyard Improvement Projects will be undertaken at 34 sites with \$39,500,000 of Restricted General Fund-ELOP. These projects were identified in Summer 2023, in order to utilize, to the extent possible, funding that expires on June 30, 2024. This was prior to the development of the Green Schoolyards Index, and work has already begun. The scope of the projects consists of new plantings, trees, turf, and/or decomposed granite within existing or new planting areas, and thus will not require Division of the State Architect (DSA) approval. Based on the scoping assumptions, all projects are anticipated to significantly increase the green space, getting each school as close to 30% as feasible.

In an effort to provide a level of geographic greening equality, and recognizing there are other significant and meaningful factors beyond the condition and adequacy of school facilities, two sites were selected in each Board District (14 total) based on an assessment of elementary school sites' ranking on the Greening 1.0 Index; their 2021-22 unduplicated pupil count of free/reduced-price meals, English learners, and foster youth; and the projects planned or underway that would provide incremental greening (Outdoor Learning Environment (OLE) and PACEUP projects). Of the remaining 20 sites, 18 were identified based on the aforementioned methodology with the exclusion of geographic equality, and the remaining two were identified to address pre-existing site concerns and a reoccurring safety hazard.

The Board's authorization to execute all instruments necessary, as legally permissible, to implement the projects, including budget modifications, will help support efforts to expedite the Green Schoolyard Improvement projects (Non-DSA) at the 34 sites below.

Board District	Region	Site Name	Greening 1.0 Index Rank	Percentage of Unduplicated Pupil Count of Free/Reduced-Price Meals, English Learners & Foster Youth 2021-2022
1	South	La Salle	8	98.69%
1	South	Manhattan ES	93	97.96%
1	South	Menlo ES	37	98.60%
1	South	Woodcrest ES	60	99.15%
1	West	Wilton ES	80	95.30%
2	East	Belvedere ES	49	99.45%
2	East	Breed ES	53	97.42%
2	East	Evergreen ES	41	96.44%
2	East	Ford ES	87	95.11%
2	East	Hamasaki Magnet ES	62	92.51%
2	East	Lorena ES	62	97.92%
2	East	Marianna ES	30	96.76%
2	East	Soto ES	36	96.69%
3	North	Capistrano ES	124	75.63%
3	North	Sunny Brae ES	37	93.50%
3	West	Alta Loma ES	111	98.11%
3	West	Windsor Hills Magnet ES	644	82.71%
4	North	Garden Grove ES	225	93.40%
4	West	Stoner ES	91	91.27%
5	East	28th St. ES	43	99.03%
5	East	Hughes ES	88	94.59%
5	East	Stanford ES	51	96.48%
5	South	Norwood ES	64	96.10%
5	West	Hobart ES	84	96.26%
5	West	Hoover ES	40	99.28%
5	West	Los Angeles ES	56	98.91%
6	North	Coldwater Canyon ES	42	96.17%
6	North	Lankershim ES	86	90.99%
7	South	109th St. ES	39	96.76%
7	South	118th St. ES	71	98.65%
7	South	66th St. ES	81	98.18%
7	South	75th St. ES	33	98.15%
7	South	Griffith-Joyner ES	77	99.48%
7	South	Russell ES	92	96.56%

Initial Budget and COPs Allocation:	\$ 25,000,000
Restricted General Fund-ELOP (Allocated):	\$ 89,500,000
<u>Anticipated Future Funding Allocation(s):</u>	<u>\$ 25,000,000</u>
Total Anticipated Program Budget (all funding sources):	\$139,500,000

Program Schedule: Construction of the first project is anticipated to begin in Q1-2024 and the final project is anticipated to be completed in Q4-2027.

8. Campus Safety Systems Improvement Projects

Project Scope: Design and install new video camera and intrusion alarm systems for 719 school sites, 291 of which are included in the initial phase of this work ([site list](#)). The scope may include, but is not limited to the design and installation of video camera systems for each individual campus, based on current design standards that are specified in technical design guidelines:

- o Campus Perimeter
- o Entrance (Main, Parking)
- o Rear/Service Entrance/Delivery
- o Exterior Doors
- o Parking Structure
- o Bus Loading/Unloading Zones
- o Large Assembly Areas
- o Stairwells
- o Corridors
- o Valuable Resources (Storage)
- o Other site-specific critical areas

Each project will include approximately 20 camera locations at smaller schools and 30 camera locations at larger schools, with each consisting of three to four cameras, or a total of 60 to 120 cameras per school site. The “large and small” school designation will be determined by student enrollment, number of buildings, and campus layout.

The new system will include remote monitoring capabilities through LASPD’s Operations Center. In total, 719 sites have been identified for a project, and additional funding allocations will be required to complete all projects.

Initial Budget/COPs Allocation:	\$146,000,000
<u>Future Anticipated Funding Allocation(s):</u>	<u>\$210,000,000</u>
Total Anticipated Project Budget:	\$356,000,000

Project Schedule: Construction is anticipated to begin in Q1-2024, with the first 291 projects to be completed in Q1-2026, and the entire program of 719 sites anticipated to be completed in Q4-2028.

9. Cybersecurity Improvement Program

Project Scope: Delivery of Districtwide cybersecurity enhancements that address vulnerabilities identified in the 2021 Information Security Audit as well as recommendations from the Cybersecurity Task Force, which was convened in the wake of the September 2022 cyber-attack. The Cybersecurity Improvement Program includes augmentation of people, processes, and technology tools to identify and mitigate the risk of future cyber-attacks and disruption to District operations, requiring capital and reoccurring operational expenditures. The capitalizable scope may include, but is not limited to:

- o *Enhancing Network Security Models, including Identity Management to Control Account Access and Manage Digital Identities:* Implement a centralized system to manage the lifecycle of user accounts required to access District applications, including access and authorization management. This effort will modernize the current decentralized systems for managing user account passwords and workflow-based authorizations.
- o *Cloud Migration of Core Assets and Applications:* Migrate on-site core applications, including the District's enterprise resource planning tool (SAP), Student Information System (MiSiS), Special Education System (Welligent), Food Services, Transportation, and others, to the Cloud to achieve a better security posture, reduce down-time, and enhance systems' performance.
- o *Redesign and Hardening of Network Architecture and Infrastructure:* Install and implement modern Data Center firewalls and segment critical applications to inspect and block potentially malicious traffic and insider threats.
- o *Vulnerability Assessment and Threat Management for Protection and Detection:* Configure security tools for recurring enterprise-level scans of critical systems and applications to support identification, classification, prioritization, remediation, and mitigation of vulnerabilities.
- o *Security Operations Center:* Centralize application and system security alerts that may be indicators of compromise, or malicious activities. Implementation of an Artificial Intelligence platform that supports a 24x7x365 security operations center to monitor security alerts and take action as deemed necessary.

The Cybersecurity Improvement Program will be executed in multiple phases, with the first phase focused on the highest priority actions to elevate the District's security posture per Audit and Task Force findings.

Initial Budget and COPs Allocation:	\$ 72,517,106
<u>Future Anticipated Funding Allocation(s):</u>	<u>\$109,242,394</u>
Total Anticipated Capital Program Budget:	\$181,759,500

Full implementation of the Cybersecurity Improvement Program is currently estimated to require \$88,258,550 of General Funds and is included in the Capital Plan.

Project Schedule: Implementation began in Q2-2023 and is anticipated to be completed in Q2-2026.



Board of Education Report

File #: Rep-064-24/25, Version: 1

Approve the Definition of 12 Classroom Upgrade Projects and Amend the Facilities Services Division Strategic Execution Plan to Incorporate Therein

October 22, 2024

Facilities Services Division

Action Proposed:

Approve the definition of 12 Classroom Upgrade Projects (Projects), as described in Exhibit A, and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein. The combined budget for the proposed Projects is \$106,372,000.

Authorize the Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the proposed Projects including budget modifications and the purchase of equipment and materials.

Background:

On August 24, 2021, the Board of Education (Board) adopted an update to the School Upgrade Program (SUP) to integrate Measure RR funding and priorities into its operational framework. The updated SUP framework and the Measure RR Implementation Plan (Implementation Plan) help guide the identification of sites and development of project proposals. The Implementation Plan included, among other priorities, the development of projects to provide upgrades focused on the interior of existing classroom spaces.

The school sites identified for the proposed Projects were deemed to have the highest need for classroom upgrades based on their overall Facilities Condition Index (FCI) score for interior classroom spaces. FCI scores indicate the remaining service life of the physical components within classroom spaces and as compared to other schools. Additionally, the priority for implementation of the proposed Projects focused on middle school programs with the goal of attracting and retaining students transitioning from elementary to secondary education across the District's four geographic Regions.

The proposed Projects will provide upgrades to classrooms utilized for instruction, special education, and school set-asides within permanent and relocatable buildings. Each classroom within a school site has unique conditions and will be surveyed to understand deficiencies needing to be addressed. Based on the individual needs of each classroom, the scope may include upgrades to technology, electrical upgrades to support new classroom technology, white boards, tack boards, window blinds, paint, and security locks. The proposed Projects also include providing new classroom furniture, replacing damaged ceiling tiles, and other upgrades required to comply with local, state, and federal requirements.

Bond Oversight Committee Recommendations:

This item was considered by the School Construction Bond Citizens' Oversight Committee (BOC) at its meeting on October 10, 2024, as referenced in Exhibit B. The presentation that was provided is included as Exhibit C. Staff has concluded that this proposed Facilities SEP amendment is in alignment with BOC recommendations and will facilitate Los Angeles Unified School District's ability to successfully complete the

Facilities SEP.

Expected Outcomes:

Approval of the 12 proposed Projects and amendment to the Facilities SEP to incorporate therein. The approval will enable staff to proceed with the design and construction of the proposed Projects.

The upgraded classrooms, once completed, will provide facilities that support education programs and student achievement. The proposed Projects will also decrease demands for repair and maintenance, alleviate the burden on custodial staff, and benefit the local economy by creating tax revenue and new jobs.

Board Options and Consequences:

Adoption of the proposed action will authorize staff to proceed with the expenditure of Bond Program funds and begin the environmental reviews and clearances, design, procurement, construction, and other activities necessary to implement the proposed Projects.

If the proposal is not approved, the proposed Projects will not commence, and the schools will not benefit from the upgrades being proposed.

Policy Implications:

The proposal does not impact Los Angeles Unified policy. It furthers implementation of the update to the SUP to integrate Measure RR funding and priorities into its operational framework. Furthermore, the proposal is consistent with the District's long-term goal to address unmet school facilities needs and significantly improve the conditions of aging and deteriorating school facilities as described in the District's local bond measures K, R, Y, Q, and RR. The proposed action advances Los Angeles Unified's 2022-2026 Strategic Plan Pillar 4 Operational Effectiveness Modernizing Infrastructure by upgrading classrooms at schools.

Budget Impact:

The combined Project budget for the 12 proposed Projects is \$106,372,000. The proposed Projects will be funded by Bond Program funds targeted in the School Upgrade Program for major modernizations, upgrades, and reconfigurations to school campuses.

The \$11,423,000 budget for the proposed Project at Robert Louis Stevenson College & Career Prep includes \$1,819,000 for classrooms presently occupied by a co-located charter school pursuant to Education Code section 47614 (Proposition 39). Bond Program funds targeted for Charter School Facilities Upgrades and Expansions will be transferred to funds earmarked in the SUP for major modernizations, upgrades, and reconfigurations to school campuses, and all aspects of the proposed upgrades will be owned entirely by District.

The Project budgets were prepared based on the current information known, and assumptions about the proposed Project scope, site conditions, and market conditions. The Project budgets will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise and will be adjusted accordingly to enable the successful completion of the proposed Projects.

Student Impact:

The proposed Projects, once completed, will help ensure approximately 11,500 current and future students attending these 12 schools are provided with safe, welcoming, and state-of-the-art learning environments that support student-centered, experiential, and engaged learning. The proposed Projects will also allow schools to attract and retain future students, which builds school pride and enhances opportunities to create a positive

File #: Rep-064-24/25, Version: 1

school culture.

Equity Impact:

School sites represent all four Regions (North, East, South, and West) and were prioritized based on their Facilities Condition Index scores.

Issues and Analysis:

Staff will implement all opportunities to minimize construction impacts on school operations and existing education programs. As necessary, the temporary use of unused classrooms, off-hour construction and other opportunities will be utilized to reduce impacts to the existing education programs at each school.

The Office of Environmental Health and Safety (OEHS) will evaluate the proposed Projects in accordance with the California Environmental Quality Act (CEQA).

Attachments:

Exhibit A: Scope, Budget, and Schedule for 12 Classroom Upgrade Projects

Exhibit B: BOC Resolution

Exhibit C: BOC Presentation

Informatives:

None

Submitted:

09/20/24

RESPECTFULLY SUBMITTED,**APPROVED BY:**


ALBERTO M. CARVALHO
Superintendent



PEDRO SALCIDO
Deputy Superintendent, Business Services and Operations

REVIEWED BY:**APPROVED BY:**


DEVORA NAVERA REED
General Counsel




KRISZTINA TOKES
Chief Facilities Executive
Facilities Services Division

☒ Approved as to form.

REVIEWED BY:**PRESENTED BY:**


NORBERTO DELGADILLO
Deputy Chief Financial Officer



ISSAM DAHDUL
Director of Facilities Planning & Development
Facilities Services Division

☒ Approved as to budget impact statement.

1. Dodson Middle School – Classroom Upgrade Project

Region South, Board District 7 (Tanya Ortiz Franklin)

The proposed project includes upgrades to the interiors of approximately 60 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the Americans with Disabilities Act (ADA), Division of the State Architect (DSA), California Environmental Quality Act (CEQA), Department of Toxic Substances Control (DTSC), or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$9,570,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

2. Drew Middle School - Classroom Upgrade Project

Region South, Board District 7 (Tanya Ortiz Franklin)

The proposed project includes upgrades to the interiors of approximately 56 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$9,106,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

3. El Sereno Middle School – Classroom Upgrade Project

Region East, Board District 2 (Dr. Rocio Rivas)

The proposed project includes upgrades to the interiors of approximately 55 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$8,847,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

4. Mann UCLA Community School – Classroom Upgrade Project

Region South, Board District 1 (Dr. George McKenna)

The proposed project includes upgrades to the interiors of approximately 41 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$6,660,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

5. Mount Gleason Middle School – Classroom Upgrade Project

Region North, Board District 6 (Kelly Gonez)

The proposed project includes upgrades to the interiors of approximately 50 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$8,125,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

6. Nimitz Middle School - Classroom Upgrade Project

Region East, Board District 5 (Jackie Goldberg)

The proposed project includes upgrades to the interiors of approximately 63 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$9,960,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

7. Pio Pico Middle School – Classroom Upgrade Project

Region West, Board District 1 (Dr. George McKenna)

The proposed project includes upgrades to the interiors of approximately 28 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$4,587,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

8. Reed Middle School – Classroom Upgrade Project

Region North, Board District 3 (Scott Schmerelson)

The proposed project includes upgrades to the interiors of approximately 58 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$9,441,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

9. Revere Charter Middle School – Classroom Upgrade Project

Region West, Board District 4 (Nick Melvoin)

The proposed project includes upgrades to the interiors of approximately 69 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$10,586,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

10. Robert Louis Stevenson College & Career Prep – Classroom Upgrade Project

Region East, Board District 2 (Dr. Rocio Rivas)

The proposed project includes upgrades to the interiors of approximately 72 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$11,423,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

11. Sepulveda Middle School – Classroom Upgrade Project

Region North, Board District 6 (Kelly Gonez)

The proposed project includes upgrades to the interiors of approximately 72 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$11,229,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

12. Twain Middle School – Classroom Upgrade Project

Region West, Board District 4 (Nick Melvoin)

The proposed project includes upgrades to the interiors of approximately 42 classrooms utilized for instruction, special education, and support spaces. Based on the individual needs of each classroom, the scope may include, but is not limited to:

- Technology upgrades such as:
 - Installation of new interactive display boards.
 - Upgrading sound enhancement devices for teacher oration.
- Limited electrical upgrades to support new classroom technology.
- Installation of new and/or renovation of white boards/tack boards.
- Purchase and installation of new classroom furniture.
- Upgrades to window blinds.
- Painting of classroom interior surfaces.
- Installation of security locks.
- Replacement of ceiling tiles as needed.
- Requirements from the ADA, DSA, CEQA, DTSC, or other improvements to ensure compliance with local, state, and federal requirements.

Project Budget: \$6,838,000

Project Schedule: Construction will be implemented in two phases and is anticipated to begin in Q4-2025 and be completed in Q1-2027.

SCHOOL CONSTRUCTION BOND CITIZENS' OVERSIGHT COMMITTEE

D. Michael Hamner, FAIA, Chair
American Institute of Architects
Robert Campbell, Vice-Chair
L.A. Co. Auditor-Controller's Office
Dr. Samantha Rowles, Secretary
LAUSD Student Parent
Patrick MacFarlane, Executive Committee
Early Education Coalition
Scott Pansky, Executive Committee
L.A. Area Chamber of Commerce

Joseph P. Buchman – Legal Counsel
Burke, Williams & Sorensen, LLP
Lori Raineri and Keith Weaver – Oversight Consultants
Government Financial Services Joint Powers Authority

Neelura Bell
CA Charter School Association
Sandra Betts
CA Tax Reform Assn.
Chad Boggio
L.A. Co. Federation of Labor AFL-CIO
Aleigh Lewis
L.A. City Controller's Office
Jennifer McDowell
L.A. City Mayor's Office
Brian Mello
Assoc. General Contractors of CA

Santa Ramirez
Tenth District PTSA
William O. Ross IV
31st District PTSA
Ashley Kaiser (Alternate)
Assoc. General Contractors of CA
Connie Yee (Alternate)
L.A. Co. Auditor-Controller's Office
Vacant
Senior Citizens' Organization
Vacant
LAUSD Student Parent

Timothy Popejoy
Bond Oversight Administrator
Perla Zitle
Bond Oversight Coordinator

RESOLUTION 2024-30**BOARD REPORT 064-24/25**

**RECOMMENDING BOARD APPROVAL TO DEFINE AND APPROVE 12
CLASSROOM UPGRADE PROJECTS AND AMEND THE FACILITIES SERVICES
DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN**

WHEREAS, Los Angeles Unified School District (Los Angeles Unified) Staff proposes that the Board of Education (Board) define and approve 12 Classroom Upgrade Projects (Projects), as described in Exhibit A to Board Report No. 064-24/25, and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein; and

WHEREAS, Los Angeles Unified Staff also requests that the Board authorize the Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the proposed Projects including budget modifications and the purchase of equipment and materials; and

WHEREAS, The proposed Projects will provide upgrades to classrooms utilized for instruction, special education, and school set-asides within permanent and relocatable buildings. Each classroom within a school site has unique conditions and will be surveyed to understand deficiencies needing to be addressed. Based on the individual needs of each classroom, the scope may include upgrades to technology, electrical upgrades to support new classroom technology, white boards, tack boards, window blinds, paint, and security locks. The proposed Projects also include providing new classroom furniture, replacing damaged ceiling tiles, and other upgrades required to comply with local, state, and federal requirements; and

WHEREAS, The combined Project budget for the proposed Projects is \$106,372,000. The proposed Projects will be funded with Bond Program funds targeted in the School Upgrade Program for major modernizations, upgrades, and reconfigurations to school campuses; and

RESOLUTION 2024-30**RECOMMENDING BOARD APPROVAL TO DEFINE AND APPROVE 12 CLASSROOM UPGRADE PROJECTS AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN**

WHEREAS, The \$11,423,000 budget for the proposed Project at Robert Louis Stevenson College & Career Prep includes \$1,819,000 for classrooms presently occupied by a co-located charter school pursuant to Education Code section 47614 (Proposition 39). Bond Program funds targeted for Charter School Facilities Upgrades and Expansions will be transferred to funds earmarked in the SUP for major modernizations, upgrades, and reconfigurations to school campuses, and all aspects of the proposed upgrades will be owned entirely by Los Angeles Unified ; and

WHEREAS, The Los Angeles Unified Office of General Counsel has reviewed the proposed Projects and determined that they may proceed to the School Construction Bond Citizens' Oversight Committee (BOC) for its consideration for recommendation to the Board of Education; and

WHEREAS, Los Angeles Unified Staff has concluded that this proposed Facilities SEP amendment will facilitate Los Angeles Unified's ability to successfully implement the Facilities SEP.

NOW, THEREFORE, BE IT RESOLVED THAT:

1. The BOC recommends that the Board define and approve 12 Classroom Upgrade Projects as described in Board Report No. 064-24/25, a copy of which is attached hereto in the form it was presented to the BOC and is incorporated herein by reference and amend the Facilities SEP accordingly.
2. This resolution shall be transmitted to the Los Angeles Unified Board and posted on the BOC's website.
3. Los Angeles Unified is directed to track the above recommendation and to report on the adoption, rejection, or pending status of the recommendations as provided in section 6.2 of the Charter and Memorandum of Understanding between the BOC and Los Angeles Unified.

ADOPTED on October 10, 2024, by the following vote:

AYES: 11

ABSTENTIONS: 1

NAYS: 0

ABSENCES: 1

/Michael Hamner/

D. Michael Hamner
Chair

/Samantha Rowles/

Dr. Samantha Rowles
Secretary



Classroom Upgrade Projects



*Bond Oversight Committee Meeting
October 10, 2024*

Background



- August 2021 – Facilities School Upgrade Program was approved, which included \$350 Million for Classroom Upgrade Projects
 - 2,000 classrooms at approximately 50 schools
- Projects will upgrade classroom interiors throughout a school, without moving walls or replacing ceilings, lighting, or windows

Priority Middle Schools–Top 48



*Equally Distributed per Region + Ranked by Classroom FCI**

Group	Rank by Highest Classroom FCI*	Region East	Region North	Region South	Region West	Board Approval of Project Definition
1	1	LA ACADEMY MS	PACOIMA MS	GOMPERS MS	PALMS MS	Q4 2023
2	2	ADAMS MS	ARMSTRONG MS	AUDUBON MS**	BANCROFT MS	Q2 2024
	3	BURBANK ATC MAG MS	HALE CHART ACAD MS	FLEMING MS	WEBSTER MS**	Q2 2024
3	4	EL SERENO MS	SEPULVEDA MS	DODSON MS	TWAIN MS	Q4 2024
	5	STEVENSON C&CP**	MOUNT GLEASON MS	DREW MS	REVERE CHARTER MS	Q4 2024
	6	NIMITZ MS	REED MS	MANN UCLA COMM SCH	PIO PICO MS	Q4 2024
4	7	CARVER MS	SAN FERNANDO MS	MUIR MS	KING MAG MS	Q1 2025
	8	GAGE MS	PORTOLA CHARTER MS	MARKHAM MS	EMERSON COMM CHART MS	Q1 2025
	9	VIRGIL MS**	SUTTER MS**	BETHUNE MS	BERENDO MS	Q1 2025
5	10	SOUTH GATE MS	PORTER MS	WILMINGTON MAG MS	COCHRAN MS	Q3 2025
	11	NIGHTINGALE MS	MULHOLLAND MS	EDISON MS	WRIGHT STEAM MAG MS**	Q3 2025
	12	GRIFFITH STEAM MAG MS	LAWRENCE MS	CARNEGIE MS	LE CONTE MS**	Q3 2025

**Classroom FCI includes classrooms used for instruction, special education, and school set asides*

***Co-located charter present at campus site*

~2,000 classrooms proposed for upgrade

~46,000 middle school students positively impacted

Scoping Tenets



Project will include upgrades to classrooms:

- In permanent and relocatable buildings
- Used for instruction, special education, and school set-asides
- Co-located charter school classrooms
- Does not include upgrades to District set-asides, classrooms out-of-service, and unallocated

Scoping Tenets



Work may include:

- New classroom technology equipment
- Sound enhancements
- New classroom furniture
- Replacement of window blinds
- Interior painting
- Replacement of damaged ceiling tiles
- Limited electrical upgrades to support new classroom technology
- Accessibility improvements
(as necessary per DSA requirements)

Construction Execution Strategy

Work to occur in 2 Phases

- **Phase 1 (Year 1-2) – Non-DSA Scope**
 - Upgrade Blinds, Classroom Door Locks, and Damaged Ceiling Tiles
 - Provide New Classroom Furniture and Interior Painting
- **Phase 2 (Year 2-3) – DSA review required**
 - Classroom Technology Equipment
 - Provide Electrical Support for Technology and Required Accessibility Improvements

Construction Execution Strategy **LAUSD** UNIFIED

Work to be scheduled for nights, weekends, and school breaks

- No Interim Housing to be added to school sites
- Maximize existing swing space, if available





Dodson Middle School Classroom Upgrade Project


Board District 7 (Tanya Ortiz Franklin)
Region South

Project:
Upgrade of approximately 60 classrooms used for instruction, special education, and support spaces.

Scope:
Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:	\$9,570,000
• Site & Environmental	0.3%
• Plans	8%
• Construction	83%
• Management	5%
• Other/Reserve	4%

Project Schedule:	
• Construction Start	Q4-2025
• Construction Complete	Q1-2027

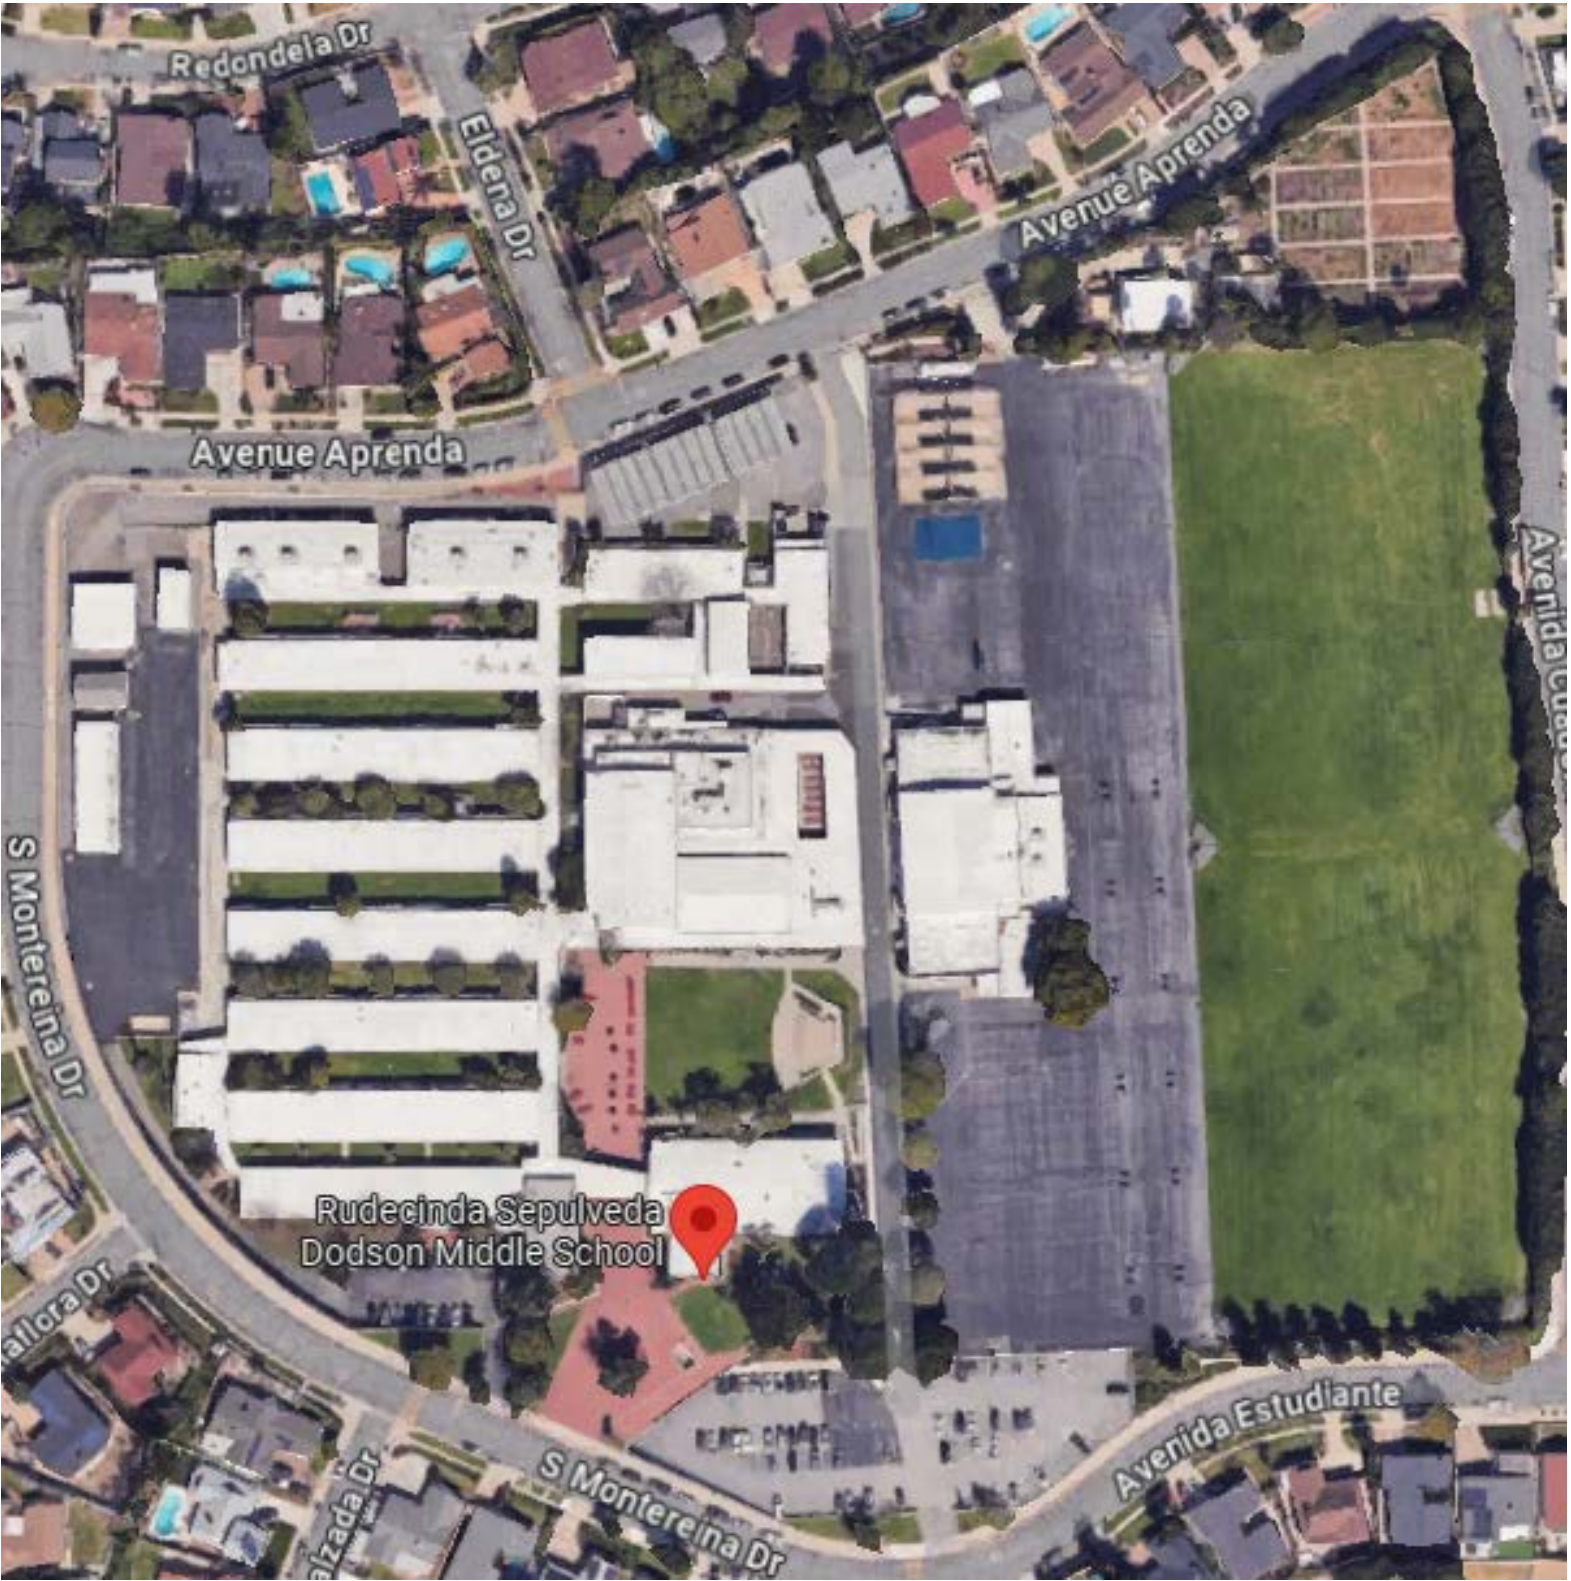

Drew Middle School Classroom Upgrade Project

Board District 7 (Tanya Ortiz Franklin)
Region South

Project:

Upgrade of approximately 56 classrooms used for instruction, special education, and support spaces.

Scope:

Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:

	\$9,106,000
• Site & Environmental	0.4%
• Plans	8%
• Construction	83%
• Management	5%
• Other/Reserve	4%

Project Schedule:

• Construction Start	Q4-2025
• Construction Complete	Q1-2027



El Sereno Middle School Classroom Upgrade Project

Board District 2 (Dr. Rocio Rivas)
Region East

Project:

Upgrade of approximately 55 classrooms used for instruction, special education, and support spaces.

Scope:

Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:

	\$8,847,000
• Site & Environmental	0.4%
• Plans	8%
• Construction	83%
• Management	5%
• Other/Reserve	4%

Project Schedule:

• Construction Start	Q4-2025
• Construction Complete	Q1-2027



Mann UCLA Community School Classroom Upgrade Project

Board District 1 (Dr. George McKenna)
Region South

Project:

Upgrade of approximately 41 classrooms used for instruction, special education, and support spaces.

Scope:

Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:

	\$6,660,000
• Site & Environmental	0.5%
• Plans	8%
• Construction	83%
• Management	5%
• Other/Reserve	4%

Project Schedule:

• Construction Start	Q4-2025
• Construction Complete	Q1-2027



Mount Gleason Middle School Classroom Upgrade Project

Board District 6 (Kelly Gonez)
Region North

Project:

Upgrade of approximately 50 classrooms used for instruction, special education, and support spaces.

Scope:


Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:

	\$8,125,000
• Site & Environmental	0.4%
• Plans	8%
• Construction	83%
• Management	5%
• Other/Reserve	4%

Project Schedule:

• Construction Start	Q4-2025
• Construction Complete	Q1-2027

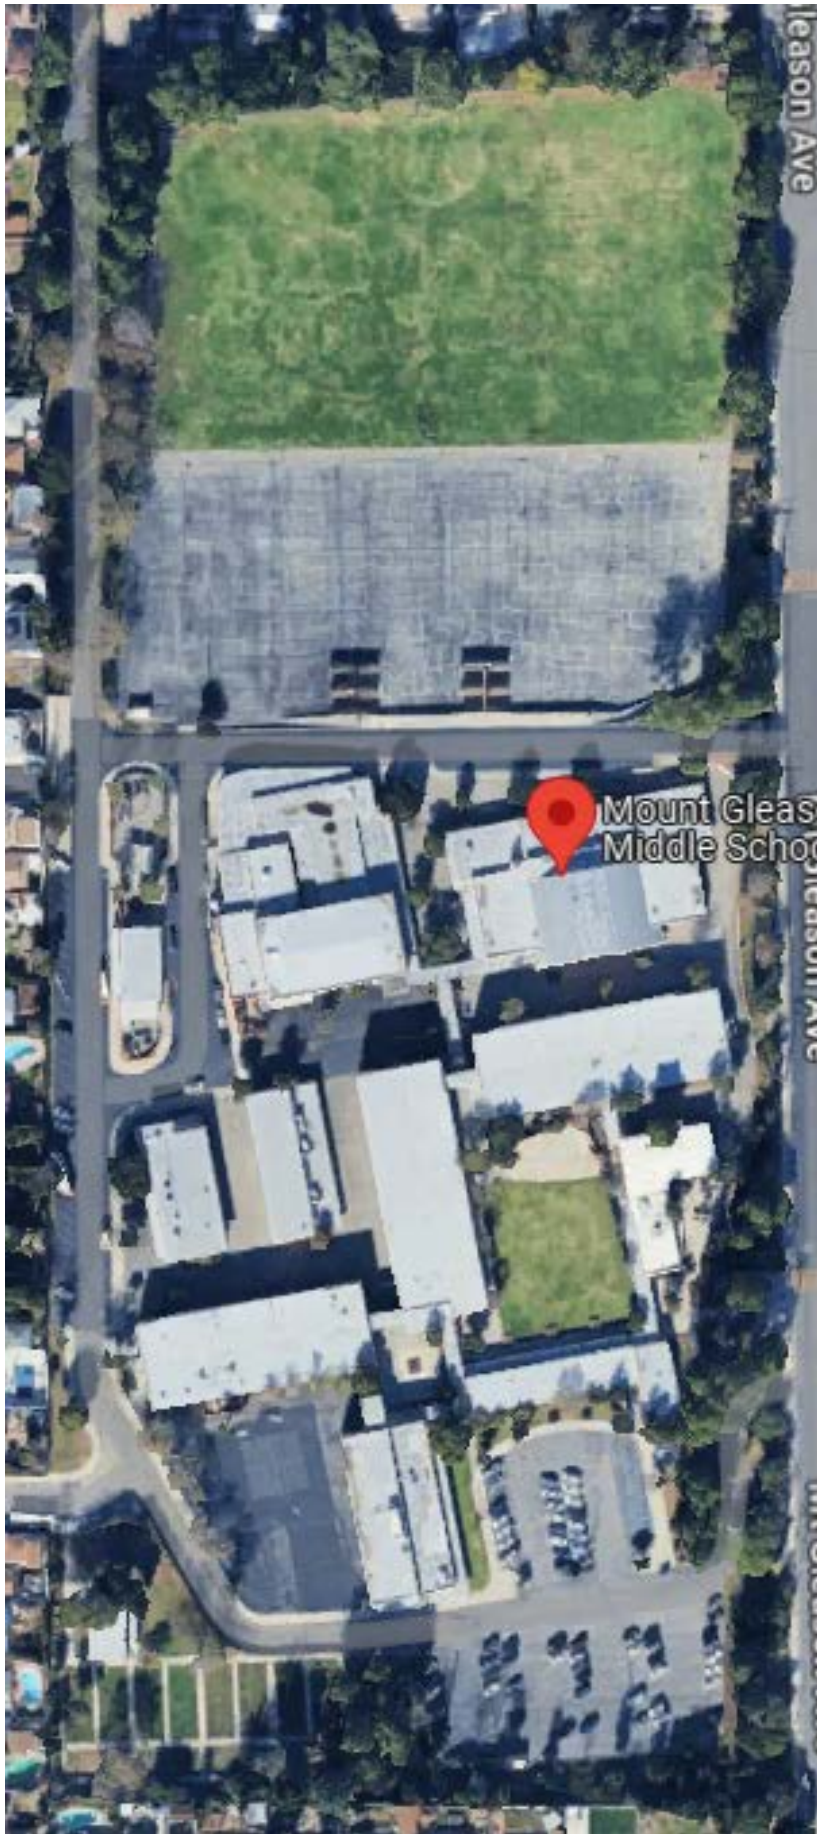

Nimitz Middle School Classroom Upgrade Project

Board District 5 (Jackie Goldberg)
Region East

Project:

Upgrade of approximately 63 classrooms used for instruction, special education, and support spaces.

Scope:

Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:

	\$9,960,000
• Site & Environmental	0.3%
• Plans	8%
• Construction	83%
• Management	5%
• Other/Reserve	4%

Project Schedule:

• Construction Start	Q4-2025
• Construction Complete	Q1-2027



Pio Pico Middle School Classroom Upgrade Project

Board District 1 (Dr. George McKenna)
Region West

Project:

Upgrade of approximately 28 classrooms used for instruction, special education, and support spaces.

Scope:

Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:

	\$4,587,000
• Site & Environmental	0.7%
• Plans	8%
• Construction	82%
• Management	5%
• Other/Reserve	4%

Project Schedule:

• Construction Start	Q4-2025
• Construction Complete	Q1-2027



Reed Middle School Classroom Upgrade Project

Board District 3 (Scott Schmerelson)
Region North

Project:

Upgrade of approximately 58 classrooms used for instruction, special education, and support spaces.

Scope:

Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:

	\$9,441,000
• Site & Environmental	0.3%
• Plans	8%
• Construction	83%
• Management	5%
• Other/Reserve	4%

Project Schedule:

• Construction Start	Q4-2025
• Construction Complete	Q1-2027



Revere Charter Middle School Classroom Upgrade Project

Board District 4 (Nick Melvoin)
Region West

Project:

Upgrade of approximately 69 classrooms used for instruction, special education, and support spaces.

Scope:

Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:

\$10,586,000	
• Site & Environmental	0.3%
• Plans	8%
• Construction	83%
• Management	5%
• Other/Reserve	4%

Project Schedule:

• Construction Start	Q4-2025
• Construction Complete	Q1-2027



Robert Louis Stevenson College & Career Prep Classroom Upgrade Project

Board District 2 (Dr. Rocio Rivas)
Region East

Project:
Upgrade of approximately 72 classrooms used for instruction, special education, and support spaces.

Scope:
Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:	\$11,423,000
• Site & Environmental	0.3%
• Plans	8%
• Construction	83%
• Management	5%
• Other/Reserve	4%

Project Schedule:	
• Construction Start	Q4-2025
• Construction Complete	Q1-2027

*Upgrades to classrooms occupied by co-located charter school will be funded with \$1,819,000 from Bond Program funds earmarked for Charter School Facilities Upgrades and Expansions.



Sepulveda Middle School Classroom Upgrade Project

Board District 6 (Kelly Gonez)
Region North

Project:

Upgrade of approximately 72 classrooms used for instruction, special education, and support spaces.

Scope:


Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:

	\$11,229,000
• Site & Environmental	0.3%
• Plans	8%
• Construction	83%
• Management	5%
• Other/Reserve	4%

Project Schedule:

• Construction Start	Q4-2025
• Construction Complete	Q1-2027

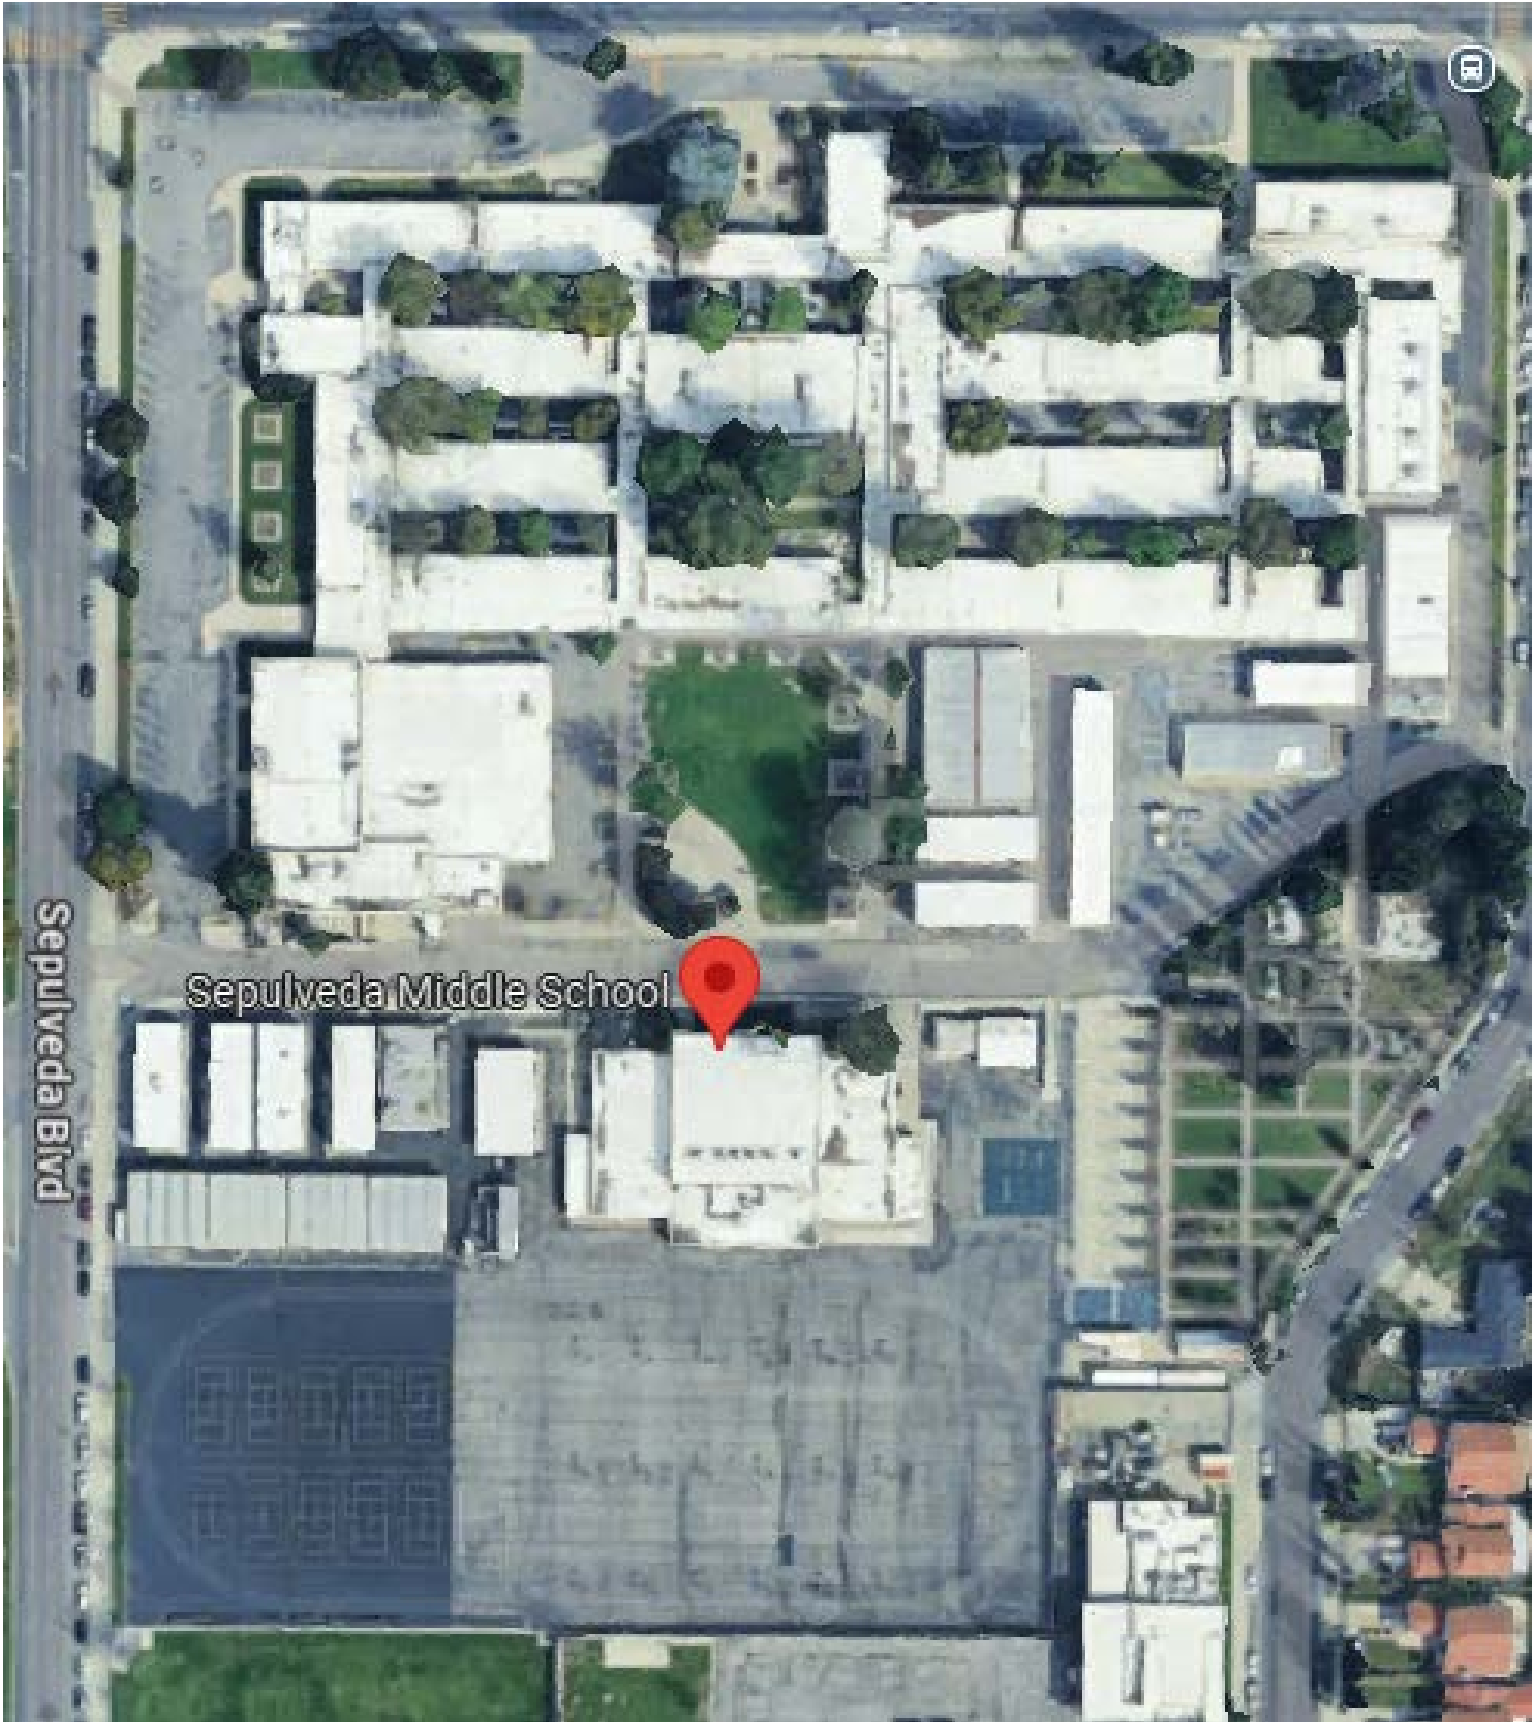

Twain Middle School Classroom Upgrade Project

Board District 4 (Nick Melvoin)
Region West

Project:

Upgrade of approximately 42 classrooms used for instruction, special education, and support spaces.

Scope:

Upgrades to technology infrastructure (digital display screens, sound enhancement systems, electrical services, and low voltage systems), security locks, new classroom furniture, white boards, tack boards, window blinds, paint, and replacement of damaged ceiling tiles.

Project Budget:

	\$6,838,000
• Site & Environmental	0.5%
• Plans	8%
• Construction	83%
• Management	5%
• Other/Reserve	4%

Project Schedule:

• Construction Start	Q4-2025
• Construction Complete	Q1-2027



Questions?



Board of Education Report

File #: Rep-018-23/24, Version: 1

Define and Approve Seven Playground and Campus Exterior Upgrade Projects and Amend the Facilities Services Division Strategic Execution Plan to Incorporate Therein

August 22, 2023

Facilities Services Division

Action Proposed:

Define and approve seven Playground and Campus Exterior Upgrade Projects (Projects) at Grant Elementary School, Kester Avenue Elementary School, Pomelo Community Charter Elementary School, Colfax Charter Elementary School, Mar Vista Elementary School, Noble Elementary School, and Plummer Elementary School, as described in Exhibit A, and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein. The total combined budget for the seven Projects is \$78,252,858.

Authorize the Chief Procurement Officer and/or the Chief Facilities Executive and/or their designee(s) to execute all instruments necessary, as legally permissible, to implement the proposed projects, including budget modifications and the purchase of equipment and materials.

Background:

On August 24, 2021, the Board of Education (Board) adopted an update to the School Upgrade Program (SUP) to integrate Measure RR funding and priorities into its operational framework and approved the Measure RR Implementation Plan (Implementation Plan) to help guide the identification of sites and development of project proposals. The Implementation Plan included, among other things, the development of playground and campus exterior upgrade projects within the category of need for Critical Replacements and Upgrades of School Building/Site Systems and Components. These Projects will address the most deteriorated paving conditions and transform playground areas.

The proposed Projects include, but are not limited to, paving replacement in playgrounds and other areas, solar reflective coating in playgrounds, greening and landscaping throughout the campus, privacy fencing where needed, exterior painting of all buildings, and accessibility upgrades. In addition, select Projects include critical replacements of failing building systems that create safety concerns and are disruptive to school operations as described in Exhibit A.

Bond Oversight Committee Recommendations:

This item was considered by the School Construction Bond Citizens' Oversight Committee (BOC) at its meeting on August 10, 2023. Staff has concluded that this proposed Facilities SEP amendment is in alignment with BOC recommendations and will facilitate Los Angeles Unified's ability to successfully implement the Facilities SEP.

Expected Outcomes:

Staff anticipates the Board will adopt this proposed amendment to the Facilities SEP to define and approve the seven proposed Projects. Approval will authorize staff to proceed with the implementation of the proposed Projects to improve student health, safety, and educational quality.

Board Options and Consequences:

Adoption of the proposed action will authorize staff to proceed with the expenditure of Bond Program funds to undertake the proposed Projects in accordance with the provisions set forth in Los Angeles Unified local bond measures K, R, Y, Q, and RR. If the proposed action is not approved, Bond Program funds will not be expended, and playground and campus exterior upgrade needs will remain unaddressed.

Policy Implications:

The proposal is consistent with Los Angeles Unified's long-term goal to address unmet school facilities needs and significantly improve the conditions of aging and deteriorating school facilities as described in Los Angeles Unified local bond measures. The proposed action advances Los Angeles Unified's 2022-2026 Strategic Plan Pillar 4 Operational Effectiveness Modernizing Infrastructure by providing playground and campus exterior upgrades at schools.

Budget Impact:

The total combined budget for the seven Projects is \$78,252,858. The Projects will be funded with Bond Program funds earmarked specifically for critical replacements and upgrades of school building/site systems and components.

Each Project budget was prepared based on the current information known and assumptions about the Project scope, site conditions, and market conditions. Individual Project budgets will be reviewed throughout the planning, design, and construction phases as new information becomes known or unforeseen conditions arise and will be adjusted accordingly to enable the successful completion of each Project.

Student Impact:

Approval of the proposed Projects enables the District to continue ongoing efforts to undertake facilities improvements that help ensure the approximately 4,500 students attending the seven schools are provided with a safe school environment that promotes teaching and learning.

Equity Impact:

Facilities Condition Assessment data identified schools with the worst paving condition based on age, aesthetics, deterioration, health and safety concerns, and weighting factors for paving condition and the Los Angeles Unified Greening Index was applied to achieve an equitable distribution and prioritized 30 schools across the District for development of a proposed Project.

Issues and Analysis:

It may be necessary to undertake feasibility studies, site analysis, scoping, and/or due diligence activities on the proposed Projects prior to initiating design. As necessary, the Office of Environmental Health and Safety (OEHS) will evaluate the proposed Projects in accordance with the California Environmental Quality Act (CEQA) to ensure compliance. If, through the planning and design process, it is determined the proposed Project scopes will not sufficiently address the critical needs identified, the Project scopes, schedule, and budget will be revised accordingly.

Attachments:

Exhibit A - Projects to Provide Playground and Campus Exterior Upgrades and Replace Building Systems to Improve Safety and School Operations

Exhibit B - BOC Resolution

File #: Rep-018-23/24, Version: 1


Informatives:

None

Submitted:

July 23, 2023


RESPECTFULLY SUBMITTED,


ALBERTO M. CARVALHO
Superintendent


APPROVED BY:


PEDRO SALCIDO
Deputy Superintendent,
Business Services and Operations

REVIEWED BY:


DEVORA NAVERA REED
General Counsel☒ Approved as to form.

APPROVED BY:


KRISZTINA TOKES
Chief Facilities Executive
Facilities Services Division

REVIEWED BY:


NOLBERTO DELGADILLO
Deputy Chief Business Officer, Finance☒ Approved as to budget impact statement.

PRESENTED BY:


INDIA R. GRIFFIN
Director of Facilities Maintenance and Operations

**LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report**

Exhibit A

Seven Playground and Campus Exterior Upgrade Projects

- 1. Grant Elementary School – Project to Provide Playground and Campus Exterior Upgrades and New Fire Alarm System**
 - *Board District 5 – Jackie Goldberg, West Region*
 - *Project Background and Scope* – The Playground and Campus Exterior Upgrade Project replaces approximately 72,000 square feet of paving to include the main and kindergarten playgrounds. The scope of work includes solar reflective coating in playgrounds, greening and landscaping throughout the campus, and privacy fencing where needed. The Project also provides a new fire alarm system for the entire site and accessibility upgrades.
 - *Project Budget* -- \$9,392,469
 - *Project Schedule* – Construction is anticipated to begin in Q4 2025 and conclude in Q4 2027.

- 2. Kester Avenue Elementary School – Project to Provide Playground and Campus Exterior Upgrades and New Underground Utilities**
 - *Board District 3 – Scott Schmerelson, North Region*
 - *Project Background and Scope* – The Playground and Campus Exterior Upgrade Project replaces approximately 108,000 square feet of paving to include the main and kindergarten playgrounds. The scope of work includes solar reflective coating in playgrounds and greening and landscaping throughout the campus. The Project also provides approximately 9,850 linear feet of underground utilities, a new trash enclosure, and accessibility upgrades.
 - *Project Budget* -- \$14,982,806
 - *Project Schedule* – Construction is anticipated to begin in Q4 2025 and conclude in Q4 2027.

- 3. Pomelo Community Charter Elementary School – Project to Provide Playground and Campus Exterior Upgrades and Slope Remediation**
 - *Board District 3 – Scott Schmerelson, North Region*
 - *Project Background and Scope* – The Playground and Campus Exterior Upgrade Project replaces approximately 134,000 square feet of paving to include the main and kindergarten playgrounds. The scope of work includes solar reflective coating in playgrounds, greening and landscaping throughout the campus, privacy fencing where needed, and exterior painting of all buildings. The Project also provides a new trash enclosure, approximately 26,000 square feet of slope remediation along the site perimeter, and accessibility upgrades.
 - *Project Budget* -- \$12,324,181
 - *Project Schedule* – Construction is anticipated to begin in Q4 2025 and conclude in Q4 2027.

**LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report**

Exhibit A

4. Colfax Charter Elementary School – Project to Provide Playground and Campus Exterior Upgrades

- *Board District 3 – Scott Schmerelson, North Region*
- *Project Background and Scope* – The Playground and Campus Exterior Upgrade Project replaces approximately 104,000 square feet of paving to include the main and kindergarten playgrounds. The scope of work includes solar reflective coating in playgrounds, greening and landscaping throughout the campus, and exterior painting of all buildings. The Project also provides a new trash enclosure and accessibility upgrades.
- *Project Budget* -- \$10,151,937
- *Project Schedule* – Construction is anticipated to begin in Q4 2025 and conclude in Q4 2027.

5. Mar Vista Elementary School – Project to Provide Playground and Campus Exterior Upgrades

- *Board District 4 – Nick Melvoin, West Region*
- *Project Background and Scope* – The Playground and Campus Exterior Upgrade Project replaces approximately 89,000 square feet of paving to include the main and kindergarten playgrounds. The scope of work includes solar reflective coating in playgrounds, greening and landscaping throughout the campus, privacy fencing where needed, and exterior painting of all buildings. The Project also provides a new trash enclosure and accessibility upgrades.
- *Project Budget* -- \$8,426,271
- *Project Schedule* – Construction is anticipated to begin in Q4 2025 and conclude in Q4 2027.

6. Noble Elementary School – Project to Provide Playground and Campus Exterior Upgrades

- *Board District 6 – Kelly Gonez, North Region*
- *Project Background and Scope* – The Playground and Campus Exterior Upgrade Project replaces approximately 70,000 square feet of paving to include the main and kindergarten playgrounds and select circulation areas. The scope of work includes solar reflective coating in playgrounds, greening and landscaping throughout the campus, along with privacy fencing and exterior painting of buildings where needed. The Project also provides a new trash enclosure and accessibility upgrades.
- *Project Budget* -- \$8,782,685
- *Project Schedule* – Construction is anticipated to begin in Q4 2025 and conclude in Q4 2027.

**LOS ANGELES UNIFIED SCHOOL DISTRICT
Board of Education Report**

Exhibit A

7. Plummer Elementary School – Project to Provide Playground and Campus Exterior Upgrades

- *Board District 6 – Kelly Gonez, North Region*
- *Project Background and Scope* – The Playground and Campus Exterior Upgrade Project replaces approximately 138,000 square feet of paving to include the main and kindergarten playgrounds and a new event plaza. The scope of work includes solar reflective coating in playgrounds, greening and landscaping throughout the campus, privacy fencing where needed, exterior painting of all buildings, and accessibility upgrades.
- *Project Budget* -- \$14,192,509
- *Project Schedule* – Construction is anticipated to begin in Q4 2025 and conclude in Q4 2027.

LOS ANGELES UNIFIED SCHOOL DISTRICT

SCHOOL CONSTRUCTION BOND CITIZENS' OVERSIGHT COMMITTEE

Margaret Fuentes, Chair
LAUSD Student Parent
D. Michael Hamner, FAIA, Vice-Chair
American Institute of Architects
Samantha Rowles, Secretary
LAUSD Student Parent
Robert Campbell, Executive Committee
L.A. Co. Auditor-Controller's Office
Scott Pansky, Executive Committee
L.A. Area Chamber of Commerce

Neelura Bell
CA Charter School Association
Jeffrey Fischbach
CA Tax Reform Assn.
Chris Hannan
L.A. Co. Federation of Labor AFL-CIO
Patrick MacFarlane
Early Education Coalition
Jennifer McDowell
L.A. City Mayor's Office
Brian Mello
Assoc. General Contractors of CA

Dr. Clarence Monteclaro
Tenth District PTSA
William O. Ross IV
31st District PTSA
Dolores Sobalvarro
AARP
Chad Boggio (Alternate)
L.A. Co. Federation of Labor AFL-CIO
Connie Yee (Alternate)
L.A. Co. Auditor-Controller's Office
Vacant
L.A. City Controller's Office

Joseph P. Buchman – Legal Counsel
Burke, Williams & Sorensen, LLP
Lori Raineri and Keith Weaver – Oversight Consultants
Government Financial Services Joint Powers Authority

Timothy Popejoy
Bond Oversight Administrator
Perla Zitle
Bond Oversight Coordinator

RESOLUTION 2023-22

BOARD REPORT 018-23/24

RECOMMENDING BOARD APPROVAL TO DEFINE AND APPROVE SEVEN PLAYGROUND AND CAMPUS EXTERIOR UPGRADE PROJECTS AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN

WHEREAS, District Staff proposes that the Board of Education (Board) define and approve seven Playground and Campus Exterior Upgrade Projects with a combined budget of \$78,252,858 (the "Projects") as described in Board Report 018-23/24 attached hereto, and amend the Facilities Services Division (Facilities) Strategic Execution Plan (SEP) to incorporate therein, and authorize the Chief Procurement Officer and/or the Chief Facilities Executive, and/or their designee(s), to execute all instruments necessary to implement the Projects; and

WHEREAS, The Measure RR Implementation Plan included, among other things, the development of playground and campus exterior upgrades projects within the category of need for Critical Replacements and Upgrades of School Building/Site Systems and Components; and

WHEREAS, These Projects will address the most deteriorated paving conditions and transform playground areas; and

WHEREAS, The proposed Projects include, but are not limited to, paving replacement in playgrounds and other areas, solar reflective coating in playgrounds, greening and landscaping throughout the campus, privacy fencing where needed, exterior painting of all buildings, and accessibility upgrades; and

WHEREAS, Select Projects include critical replacements of failing building systems that create safety concerns and are disruptive to school operations; and

WHEREAS, District Staff has determined that the Projects are necessary to improve student health, safety, and educational quality; and

RESOLUTION 2023-22**RECOMMENDING BOARD APPROVAL TO DEFINE AND APPROVE SEVEN PLAYGROUND AND CAMPUS EXTERIOR UPGRADE PROJECTS AND AMEND THE FACILITIES SERVICES DIVISION STRATEGIC EXECUTION PLAN TO INCORPORATE THEREIN**

WHEREAS, the Board of Education's approval of the Projects will authorize District Staff to proceed with the expenditure of Bond Program funds to undertake the Projects in accordance with the provisions set forth in Los Angeles Unified local bond measures K, R, Y, Q, and RR; and

WHEREAS, District staff has concluded that this proposed Facilities SEP amendment will facilitate Los Angeles Unified's ability to successfully complete the Facilities SEP.

NOW, THEREFORE, BE IT RESOLVED THAT:

1. The School Construction Citizens' Bond Oversight Committee (BOC) recommends that the Board of Education define and approve seven Playground and Campus Exterior Upgrade Projects, with a combined budget of \$78,252,858, and amend the Facilities SEP to incorporate therein, as described in Board Report 018-23/24, a copy of which is attached hereto in the form it was presented to the BOC and is incorporated herein by reference.
2. This resolution shall be transmitted to the Los Angeles Unified Board and posted on the BOC's website.
3. Los Angeles Unified is directed to track the above recommendation and to report on the adoption, rejection, or pending status of the recommendations as provided in section 6.2 of the Charter and Memorandum of Understanding between the BOC and Los Angeles Unified.

ADOPTED on August 10, 2023, by the following vote:

AYES: 12

ABSTENTIONS: 0

NAYS: 0

ABSENCES: 3

/Michael Hamner/

D. Michael Hamner
Vice-Chair

/Samantha Rowles/

Samantha Rowles
Secretary

September 2025 Board Report - A/E Extra Services

#	Extra Service #	Contract #	Ariba #	School	Architect	ES Amount \$	Original Contract \$	Total Contract \$
1	ES-25186	1620141	C3074	San Pedro HS	LPA, Inc.	\$3,696.12	\$7,753,631.71	\$15,736,209.73
2	ES-25187	1920023	C1140	Taft Charter HS	NAC Architecture	\$9,698.57	\$7,932,816.00	\$13,054,690.33
3	ES-25188	1920023	C1140	Taft Charter HS	NAC Architecture	\$6,966.35	\$7,932,816.00	\$13,061,656.68
4	ES-25183	2220012	C3092	Hollenbeck MS	Lehrer Architects	\$19,311.34	\$1,051,478.58	\$1,070,789.92
5	ES-25164	2220013	C3093	San Pedro ES	Tate Snyder Kimsey	\$22,278.76	\$259,626.58	\$302,851.76
6	ES-25163	2420029	C3008	Cleveland Charter HS	PBK	\$41,271.06	\$447,599.66	\$493,696.36
7	ES-25178	2420037	C1200	Canyon Creek Campground	Westgroup Design	\$4,026.16	\$923,140.22	\$1,971,807.61
8	ES-25179	2420037	C1200	Canyon Creek Campground	Westgroup Design	\$20,723.97	\$923,140.22	\$1,992,531.58
9	ES-25180	2420037	C1200	Canyon Creek Campground	Westgroup Design	\$99,579.04	\$923,140.22	\$2,092,110.62
Total						\$227,551.37		
Average						\$25,283.49		
Median						\$19,311.34		

September 16, 2025 (Board Report No. TBD - 24/25)

EXTRA SERVICES/AMENDMENT

#	Amount	Contract #	Ariba #	Architect	School	Project Description	ES/AC Number	RFQ #	Effective Date	Expiration Date	Max Contract Value or Capacity after the Amendment	Ariba Value Encumbered (Released)	Board District	Region
1	\$ 19,311.34	2220012	C3092	Lehrer Architects LA, Inc.	Hollenbeck MS	Barriers for three lunch shelter drinking fountains, and guardrails for barriers	ES-25183	RFQ R-19012 Architectural Services In Support of Asset Management Branch	05/19/25	DSA Certification	\$ 1,070,789.92	\$ 1,070,789.92	2	E
2	\$ 41,271.06	2420029	C3008	PBK Architects	Cleveland Charter HS	Removal of existing perimeter curb for track and decomposed granite track surface. Rev. 6-lanes to 8-lane rubber track. Design for new curb	ES-25163	RFQ R-19012 Architectural Services In Support of Asset Management Branch	05/06/25	DSA Certification	\$ 493,696.36	\$ 452,425.30	3	N
3	\$ 9,698.57	1920023	C1140	NAC Inc. dba NAC Architecture	Taft Charter HS	Replacement of the existing L-shaped exterior brick wall attached to the MPR building, and to patch/repair the ares of the MPR's existing wall where the existing L-shaped wall was attached	ES-25187	RFQ R-13019 Architectural Services In Support of Asset Management Branch	06/12/25	DSA Certification	\$ 13,054,690.33	\$ 13,025,562.39	4	N
4	\$ 6,966.35	1920023	C1140	NAC Inc. dba NAC Architecture	Taft Charter HS	A/E design services for interior Bard unit anchorage detailing that can be installed without disassembling the Bard unit	ES-25188	RFQ R-13019 Architectural Services In Support of Asset Management Branch	06/13/25	DSA Certification	\$ 13,061,656.68	\$ 13,025,562.39	4	N
5	\$ 22,278.76	2220013	C3093	Tate Snyder Kimsey, Inc. dba TSK	San Pedro ES	10-additional onsite meetings, 4-hrs LOE at each meeting totaling 40 hours	ES-25164	RFQ R-13019 Architectural Services In Support of Asset Management Branch	04/14/25	DSA Certification	\$ 302,851.76	\$ 302,851.76	5	E
6	\$ 3,696.12	1620141	C3074	LPA, Inc.	San Pedro HS	New temporary Ice Machine for Athletic's Coach's Temporary Office & Hook up.	ES-25186	RFQ R-13019 Architectural Services In Support of Asset Management Branch	06/12/25	DSA Certification	\$ 15,736,209.73	\$ 15,767,557.75	7	S
7	\$ 4,026.16	2420037	C1200	Westgroup Designs, Inc.	Canyon Creek Campground	Develop code analysis plan that demonstrates occupancy types. Life Safety Exit Plan	ES-25178	RFQ R-13019 Architectural Services In Support of Asset Management Branch	04/25/25	DSA Certification	\$ 1,971,807.61	\$ 2,092,110.62		

#	Amount	Contract #	Ariba #	Architect	School	Project Description	ES/AC Number	RFQ #	Effective Date	Expiration Date	Max Contract Value or Capacity after the Amendment	Ariba Value Encumbered (Released)	Board District	Region
8	\$ 20,723.97	2420037	C1200	Westgroup Designs, Inc.	Canyon Creek Campground	Drawings, specs, installation of timers in Dormitory 1 multipurpose area HVAC	ES-25179	RFQ R-13019 Architectural Services In Support of Asset Management Branch	05/13/25	DSA Certification	\$ 1,992,531.58	\$ 2,092,110.62		
9	\$ 99,579.04	2420037	C1200	Westgroup Designs, Inc.	Canyon Creek Campground	Dormitory 1, Main Lodge, Backbone Wiring Fire Alarn system and wiring for future integration.	ES-25180	RFQ R-13019 Architectural Services In Support of Asset Management Branch	05/13/25	DSA Certification	\$ 2,092,110.62	\$ 2,092,110.62		

\$ 227,551.37

INTEROFFICE CORRESPONDENCE
Los Angeles Unified School District
Facilities Services Division

INFORMATIVE

TO: Members, Board of Education
Alberto M. Carvalho, Superintendent

DATE: September 16, 2025

FROM: Issam Dahdul, Director of Facilities, Planning & Development

**SUBJECT: REQUEST FOR APPROVAL OF CONTRACT PROCURED VIA RFP R-25024
FIRE LIFE SAFETY TRAINING AND VIDEO CREATION SERVICES**

Vendor
Building Safety Solutions, Inc.

Contract Number
C9166 / 2590050

Contract amount: \$356,914.00

Student Impact:

This contract supports the safe operation of the LAUSD Administrative Headquarters ("Beaudry" building), which houses essential administrative functions that support students, families, and schools. Although the direct impact on students is limited, ensuring the safe and compliant operation of this administrative hub is critical to the efficient functioning of District services, ultimately benefiting the broader school community.

Equity Impact:

There are no direct equity implications identified for this contract.

Introduction:

The Facilities Services Division (Asset Management) seeks approval for a contract with Building Safety Solutions, Inc. (BSS) to provide fire and life safety training for the LAUSD Administrative Headquarters. These services will ensure emergency preparedness for all building occupants, including District staff and visitors.

In accordance with Los Angeles Municipal Code (LAMC) Section 57.408 and High-Rise Evacuation Ordinance No. 180648, LAUSD is ***legally required*** to provide high-rise fire and life safety training to maintain occupancy of the Beaudry building.

The current training videos and certification programs, developed by BSS in the early 2000s, are becoming obsolete as BSS retires its legacy web-based platform. Additionally, concerns about potential cybersecurity risks have been raised by the Information Technology Services (ITS) Division.

The new contract will update these videos and certification programs to address the evolving safety needs of staff and visitors while ensuring compliance with current regulations.

Why is this necessary?

This contract addresses ***three key requirements***:

1. Regulatory Compliance:

LAUSD must comply with LAMC Section 57.408 and High-Rise Evacuation Ordinance No.

180648 to legally occupy the Beaudry building. All individuals accessing the building must complete fire and life safety training within 14 days of receiving a work badge.

2. Replacement of Outdated Training Materials:

BSS's retirement of its legacy platform necessitates the creation of new training videos and certification programs. These updated materials will be tailored to the Beaudry building and will provide training for the following groups:

- General Occupants
- Floor Wardens
- Emergency Response Team (ERT) members
- Fire Safety Directors

The new materials will be hosted on a secure, District-managed platform (e.g., MyPLN), enhancing accessibility, security, and ease of maintenance.

As part of the development, on-site filming and use 3D imaging will be used to create ***building-specific emergency procedures***. These procedures will cover a variety of potential incidents, including, but not limited to:

Active Shooter	Bomb Threat	Building Evacuation
Civil Disturbance	Earthquake	Elevator Entrapment
Fire	Medical Emergency	Power Outage
Terrorist Attack	Workplace Violence	

3. Strengthen Cybersecurity:

ITS has raised concerns regarding cybersecurity risks associated with the outdated platform. Moving to a District-managed solution ensures:

- Enhanced data security
- Improved user authentication and access controls
- Alignment with District IT security protocols

Additional Emergency Services Included:

This contract also includes obtaining the following emergency preparedness services:

- Annual LAFD Emergency Procedures Manual certification
- LAFD-required fire drill certification and documentation
- Completion of LAFD-required Building Inventory Forms (BIFs)
- On-site training for key personnel, as needed

Why do we need to do this now?

Approval is required to:

- Ensure legal compliance with fire and life safety training
- Transition to a secure, District-managed platform
- Address cybersecurity concerns before the legacy platform is retired

What would happen if this were not approved?

Without approval, the District risks:

- **Regulatory Non-Compliance:** Violations of LAMC 57.408 could lead to penalties from the City of Los Angeles.
- **Potential Building Closure:** Non-compliance could lead to restrictions on occupancy at Beaudry.
- **Reduced Emergency Readiness:** Over 3,500 staff and visitors could be less prepared for emergencies.
- **Cybersecurity Threats:** Continued use of the outdated platform could expose the District to data security risks.

What are the terms of the proposed agreement?

The term of agreement will be three (3) years, with two (2) one-year options.

- **One-Time Development Cost:**
\$273,514 for the creation of *four* updated, LAFD-approved fire and life *safety training videos* tailored to Beaudry's infrastructure and occupants.

The four training modules will be specifically tailored for four building groups:

1. General Occupants
 2. Building Floor Wardens
 3. Emergency Response Team (ERT) members
 4. Fire Safety Directors
- **Annual Program Costs:**
\$16,680 per year for:
 - o Licensing for training program use
 - o Mandated building fire drills
 - o Certifications for emergency response personnel
 - o Ongoing training updates
 - o On-site emergency preparedness training, as needed

Is this a single source? ☐ Yes ☒ No

If yes, why

Is this an after-the-fact? ☐ Yes ☒ No

If yes, why

If you have any questions, please contact me at (213) 241-6478 or email Issam.dahdul@lausd.net.

INTEROFFICE CORRESPONDENCE
Los Angeles Unified School District
Office of the Superintendent

INFORMATIVE

DATE: July 15, 2025

TO: Members, Board of Education
 Alberto M. Carvalho, Superintendent

FROM: Dennis Bradburn, Director of Maintenance & Operations

SUBJECT: RFQ R-25021 MATERIALS TESTING SPECIAL INSPECTION SERVICES

FIRM NAMES:

AESCO, Inc. Contract # 2590092/C9718
 American Engineering Laboratories, Inc. Contract # 2590093/C9719
 California Testing & Inspections, Inc. Contract # 2590094/C9720
 RMA Group. Contract # 2590095/C9721
 Fenagh, Inc. Contract # 2590096/C9722
 Geocon West, Inc. Contract # 2590097/C9723
 Group Delta Consultants, Inc. Contract # 2590098/C9724
 Koury Engineering & Testing, Inc. Contract # 2590099/C9725
 MTGL, Inc. Contract # 2590100/C9726
 Ninyo & Moore Geotechnical and
 Environmental Sciences Consultants. Contract # 2590101/C9727
 Smith Emery Laboratories, Inc. Contract # 2590102/C9728
 Southwest Inspection and Testing, Inc. Contract # 2590103/C9729
 The Converse Professional Group. Contract # 2590104/C9730
 Twining, Inc. Contract # 2590105/C9731

INITIAL AGGREGATE CONTRACT AMOUNT: \$80,000,000.00
CONTRACT TERM: THREE (3) YEARS WITH TWO (2) ONE-YEAR
RENEWAL OPTIONS.
REQUEST FOR FOURTEEN (14) TASK ORDER SERVICES
CONTRACTS.

Members, Board of Education
 Alberto M. Carvalho, Superintendent
 July 15, 2025
 Page 2 of 3

Student Impact:

These contracts for Material Testing and Special Inspection Services will support District staff in providing a safe and healthy learning environment.

Introduction:

Maintenance & Operations is requesting the Board of Education's approval to award Task Order contracts to the firms to provide Material Testing and Special Inspections Services to the District.

Why is this necessary?

Material Testing and Special Inspection Services are required by California Building Code, Title 24, Part 2 of the California Code of Regulations and the Division of State Architect (DSA), to ensure quality control for school building construction and modernization projects. Testing services include identifying and testing all construction materials such as concrete, masonry, reinforcing rebar, structural steel, and wood. Special Inspection Services include inspections of steel welding and fabrication, concrete and masonry construction, and other specialty construction items. While overall construction inspection is provided by the District's Inspection Branch, specialty services are required that the District does not have the resources to perform..

Why do we need to do this now?

Current Material Testing and Special Inspection Services Agreements expire on October 31, 2025. The District must have new contracts in place to support ongoing facilities repair and modernization programs without interruption.

What would happen if this were not approved?

If this contract is not approved, facilities improvement and maintenance programs may be disrupted due to insufficient support for the required Material Testing and Special Inspection Services and related DSA approvals.

What are the terms of the proposed agreement?

The proposed contract term is three (3) years, with two (2) one-year renewal options. Funding will be provided on an as-needed basis, utilizing an estimated 90% Bond Funds and 10% General Funds.

c: Devora Navera Reed
 Pedro Salcido
 Karla V. Estrada
 Carolyn Spaht Gonzalez
 Kristen K. Murphy
 Jaime Torrens
 Martha Alvarez
 Veronica Arreguin
 Shannon Coppa

Members, Board of Education
Alberto M. Carvalho, Superintendent
July 15, 2025
Page 3 of 3

Jana Carter
Amanda Wherritt
Sasha Lopez
Patricia Chambers
Karen Mercado
Carol Delgado
Michael McLean
Krisztina Tokes
Alix O'Brien
Mark Cho
Aiyla Balakumar
